


PORTFOLIO

ROSHAN RAJ KANTHARAJA



CONTENTS

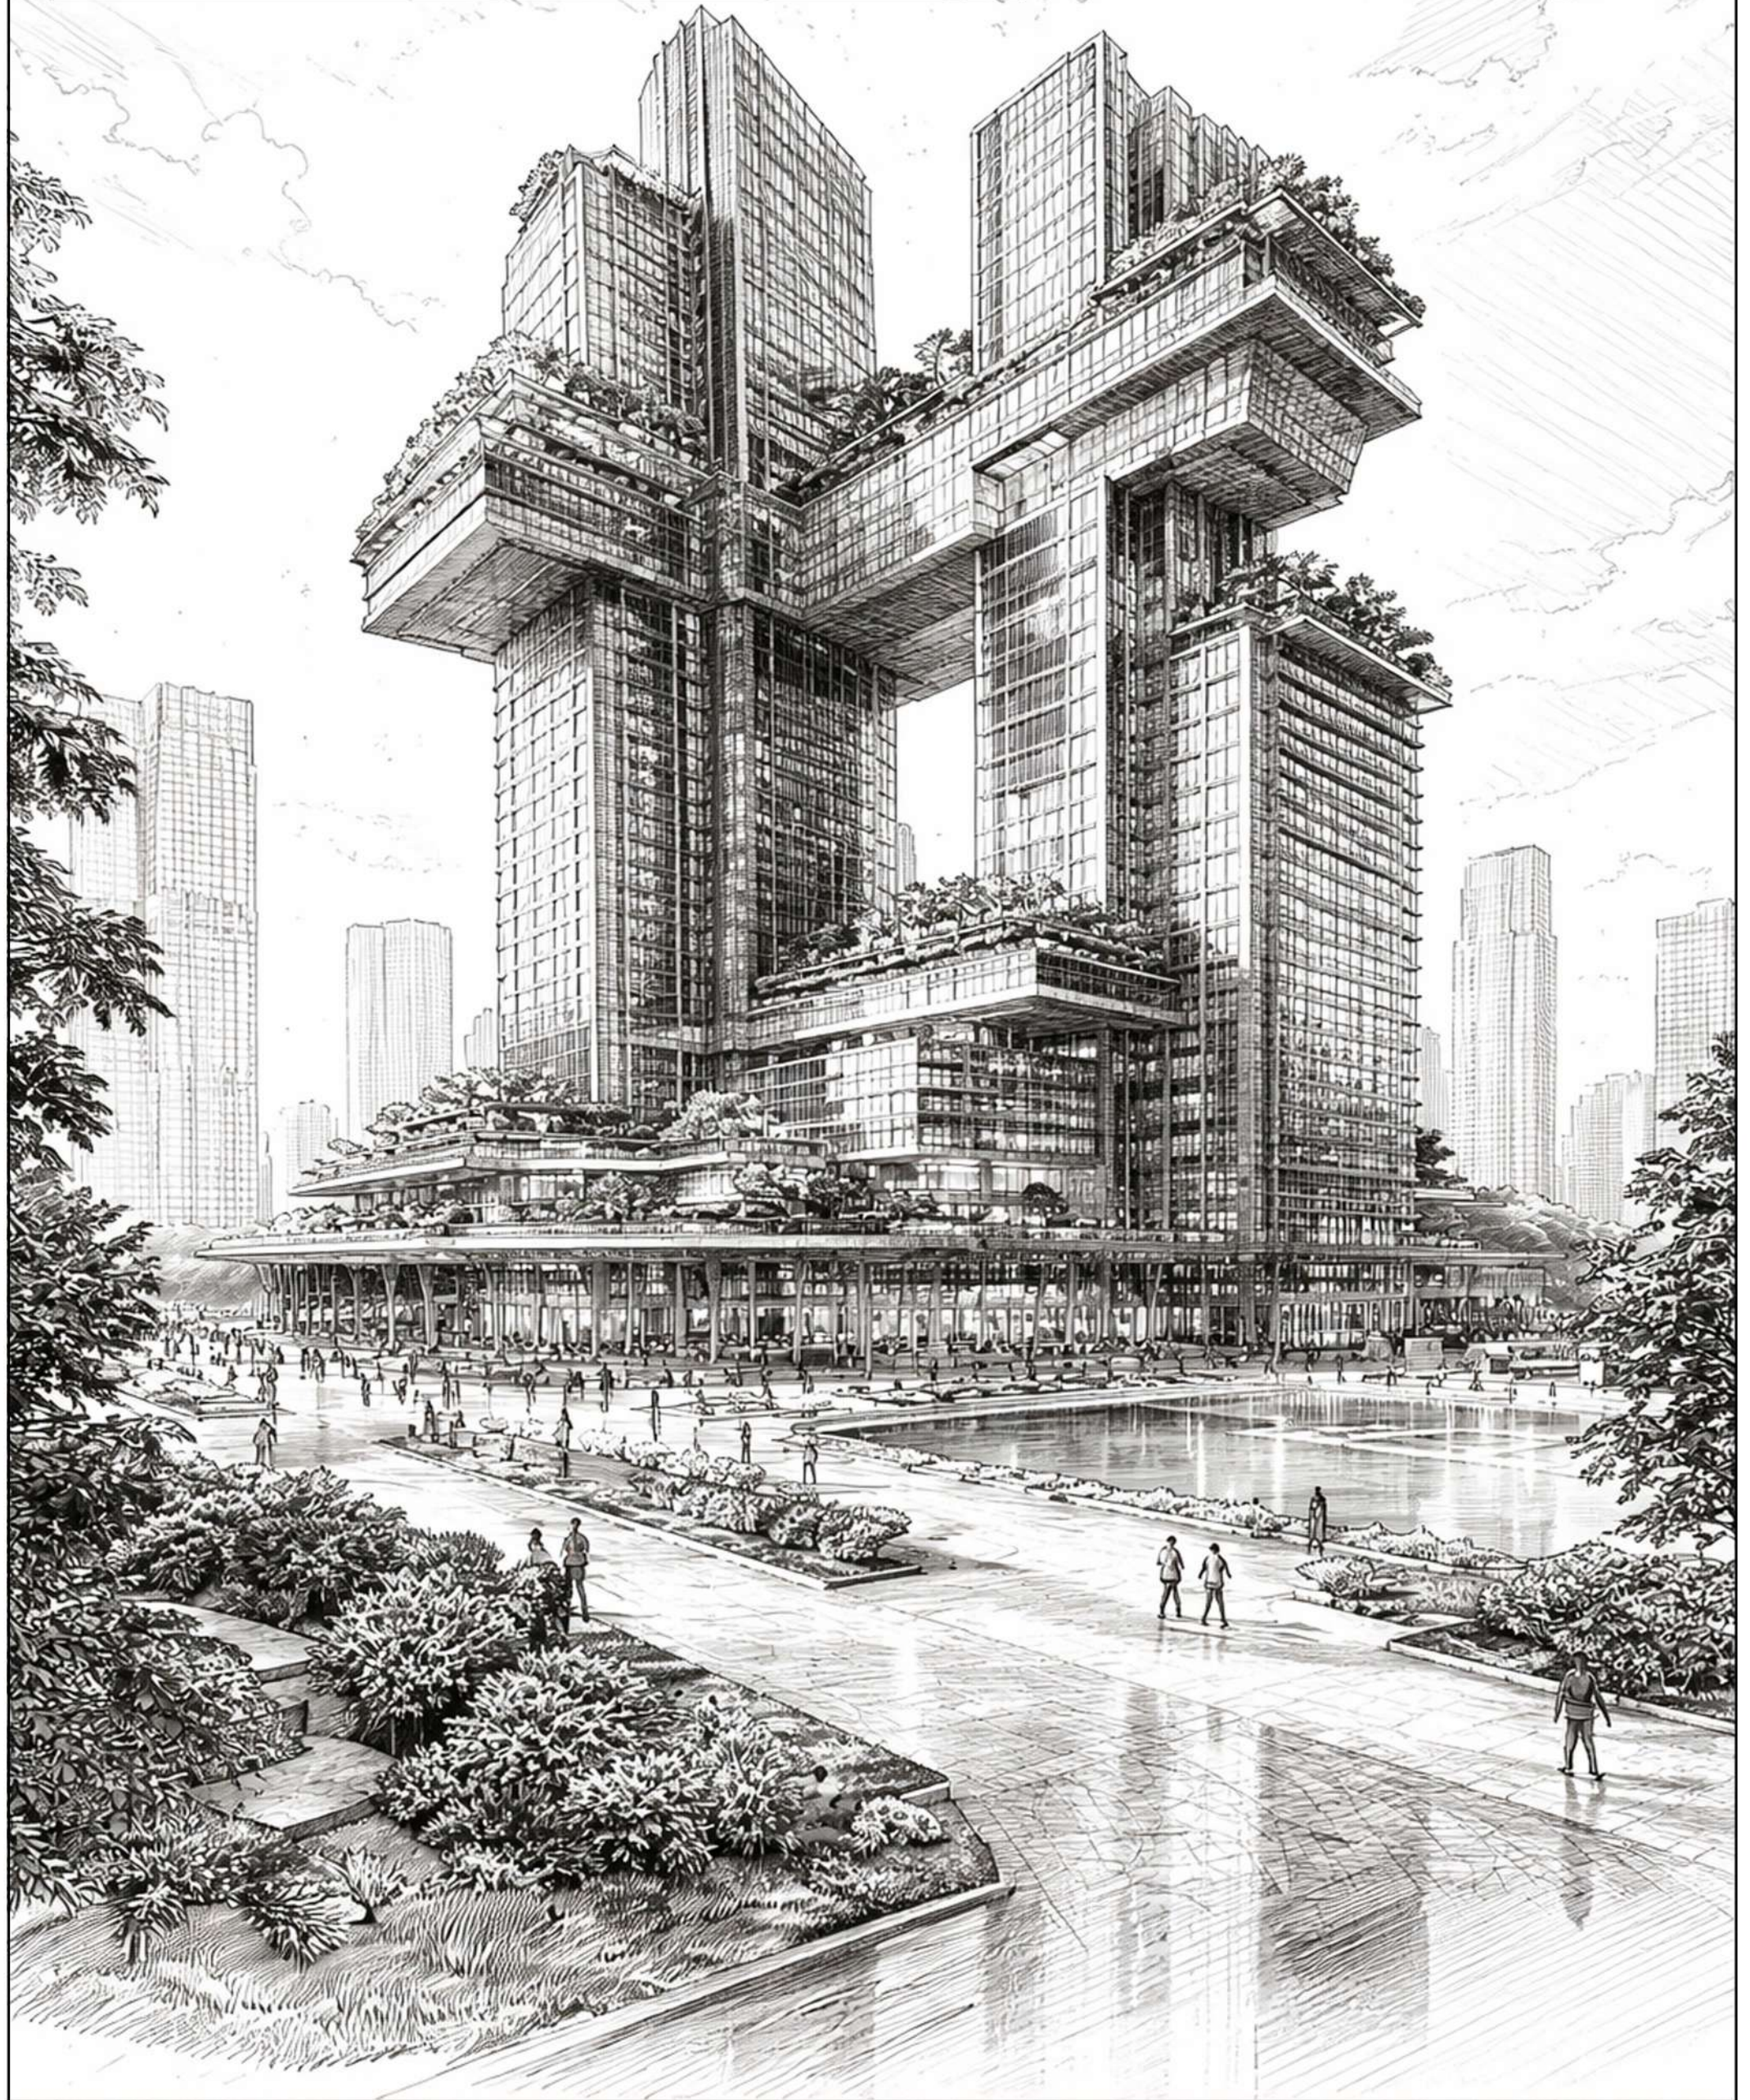

RESUME

NEXUS TERMINAL

MIAMI TOWER

PRIMAVERA P6 REPORTS

SHINDE EYE CARE AND DENTAL
CLINIC

WINDMERE VALLEY RESORT
RESTAURANT

MOTORCYCLE SERVICE FACILITY

ROSHAN RAJ KANTHARAJA, , LEED GA, CMAA-CMIT, OSHA 30

CMAA SoCal Scholarship Recipient

Driven by a passion for building, I bring a unique blend of architectural design insight and construction management expertise to project delivery. With experience leading and supporting projects across residential, commercial, and healthcare sectors exceeding \$5M, I excel at coordinating teams, streamlining workflows, and maintaining control over cost, schedule, and quality.

EDUCATION

University of Southern California Master of Construction Management (2023 - 2025)

Planning & Preconstruction, Construction Practices, Accounting & Finance, Project Controls, Marketing Strategy, Foundations of Real Estate, Consulting & Strategies, Negotiation & Deal Making, Innovation in Engineering & Design in Global Crisis

Reva University Bachelor of Architecture (2017 - 2022)

Architecture Design, Urban Planning and Landscape Design, Design Thesis, Building Structures, Cost Estimation, Interior design, Building Construction Materials, Sustainability in Design, Building Services, Geotechnical & Foundation Systems, Structural Analysis.

CONTACT


📍 ADDRESS-
Apt 2029,
West Adams Blvd,
Los Angeles,
California, 90007

☎️ PHONE-
979-721-3727

✉️ EMAIL-
rajroshank1998@gmail.com

📱 LINKEDIN-
www.linkedin.com/in/roshan-raj-k

MAJOR MILESTONES

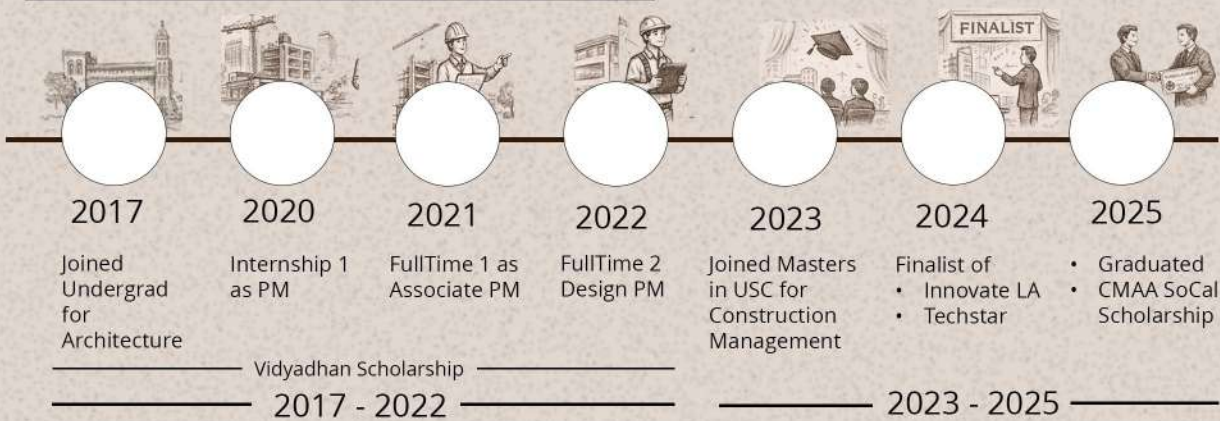

ACADEMIC WORK



TECHNICAL SKILLS

Member: SoCal CMAA, ASCE, AACE, USC ITE
Certifications: OSHA 30, Procore, CMAA-CMIT, LEED Green Associate, Bluebeam
Software: AutoCAD, Revit, BIM, Primavera P6, Bluebeam, PlanSwift, Microsoft Office, CADD, MicroStation, Arc GIS, CAFM
Tools: RFIs, Submittals, RFP, Cost Estimation, Cost & Schedule Analysis, BOQs, CPM Scheduling, QA/QC Management, PCO
Project Management: Leadership, Value Engineering, Risk Management, Procurement, Negotiation, Critical thinking
Real Estate and Finance: Legal Foundations, Debt & Equity Investment, Financial Forecasting

CO CURRICULAR

USC Wildfire Relief (2025): facilitated crisis response during the Los Angeles wildfires by connecting affected students and residents to emergency housing, food, and recovery resources.

Clean Air for Families (USC Viterbi x Families Forward): Designed and distributed DIY MERV-13 air filters for wildfire-affected kindergartens and families in Pasadena, increasing indoor air quality and community resilience.

Wildfire Shelter Volunteer (2025): Assisted displaced families with shelter setup, food distribution, and logistics coordination to ensure safety and comfort during crisis.

Children's Booney Island Expo Park(2023-2024): Helped organize, set up, and supervise event stalls and administrative operations for a community children's fair, facilitating public engagement and education.

EXPERIENCE

Project Coordinator

October 2024-December 2025

USC Facilities Planning and Management, Los Angeles, CA

- Acted as the primary coordination hub between resident assistance, technicians, vendors, and supervisors, maintaining clear communication and smooth operations across healthcare, hospitality, & facility services
- Supported cost control by reviewing vendor invoices, verifying quantities, and reconciling expenses against approved scope while coordinating maintenance and small capital projects by tracking scope, cost, and schedule to ensure timely delivery
- Streamlined project execution by identifying and resolving coordination issues in the digital twin model
- Tracked and facilitated RFIs and submittals to clarify technical requirements and prevent delays or rework
- Ensured QA/QC compliance through field follow-ups, reviewing documentation, and verifying adherence to OSHA safety standards and project performance requirements for technicians and contractors

Design Project Manager

December 2022-November 2023

Phantom Hands LLP, Bangalore, India

- Directed the full lifecycle of 10,800 sq. ft. of a \$950k design bid build multilevel condominium, including a landscape project from preconstruction to execution, developing detailed drawings, schedules, cost estimates, and supervising bidding and vendor selection to align design intent scope within budget
- Executed value-engineering solutions such as IPS concrete flooring to enhance durability and reduce maintenance costs, while designing a concrete-M-sand-limestone mesh wall system improved acoustics
- Supervised construction & MEP operations, ensuring safety, quality, & schedule through inspections & QA/QC enforcement
- Optimized BIM workflows for 3D coordination and clash detection and developed CPM schedules in Primavera P6, improving design-to-field coordination and project delivery efficiency
- Updated onsite progress reports by filing change order reviews, performing quantity takeoffs, drafting RFIs & submittals
- Directed coordination across 20+ subcontractors, sequencing activities, tracking progress against schedule milestones, and mitigating delays to protect cost and timeline performance

Associate Project Manager

January 2021-November 2022

AARDE Construction & Designer, Bangalore, India


- Coordinated with architects, engineers, and contractors on residential and commercial design-build, IPD projects totaling \$3million, controlling complete project lifecycles while upholding integrity, ethical standards, and quality delivery
- Led business development and preconstruction efforts, acquiring new clients, preparing RFP, and performing budgeting and feasibility analyses to align scope, cost, and timelines, securing major projects
- Led 24,300 sq.ft. \$2.6 Million motorcycle service facility, collaborating with architectural, structural, and MEP teams to convert a bare shell into an integrated workshop, office space, restaurant, with optimized spatial planning
- Managed and coordinated OEM equipment integration into facility systems, directing procurement and construction execution for a service station project while developing equipment layouts and shop drawings
- Collaborated with suppliers and subcontractors, resolved on-site issues, interpreted technical specifications, and supported project delivery within budget and 15 days ahead of schedule
- Led design and construction for a \$300K multifamily project, optimizing MEP/structural integration for energy efficiency and implementing tracking systems to resolve field conflicts and accelerate schedule performance

Construction Project Management Internship


January 2020-December 2020

Indianstory Studio, Bangalore, India

- Created and managed AutoCAD & Revit drawings for residential, commercial, and hospitality projects valued at over \$1.8M, developing design concepts, presentation sets, and coordinating revisions with the principal architect, clients, & consultants
- Led end-to-end of a 4,000 sq ft Eye & Dental Hospital, translating the client's vision into efficient, safe, and patient-centric layouts while securing permits and ensuring ISO-compliant healthcare standards
- Collaborated with senior architects and consultants to develop zoning medical equipment layouts, ensuring seamless coordination across MEP systems within spatial constraints. Prepared BOQs, bid packages, carpentry details, and cost analyses to support contractor selection and improve budgeting accuracy
- Tracked RFIs & submittals across stakeholders, revamping coordination, reducing conflicts by 20%, ensuring QA/QC standards
- Assisted principal architect in design and documentation of a 2-acre boutique resort, preparing detailed drawings, FF&E layouts, and interior elevations for guest rooms, restaurant, and public areas

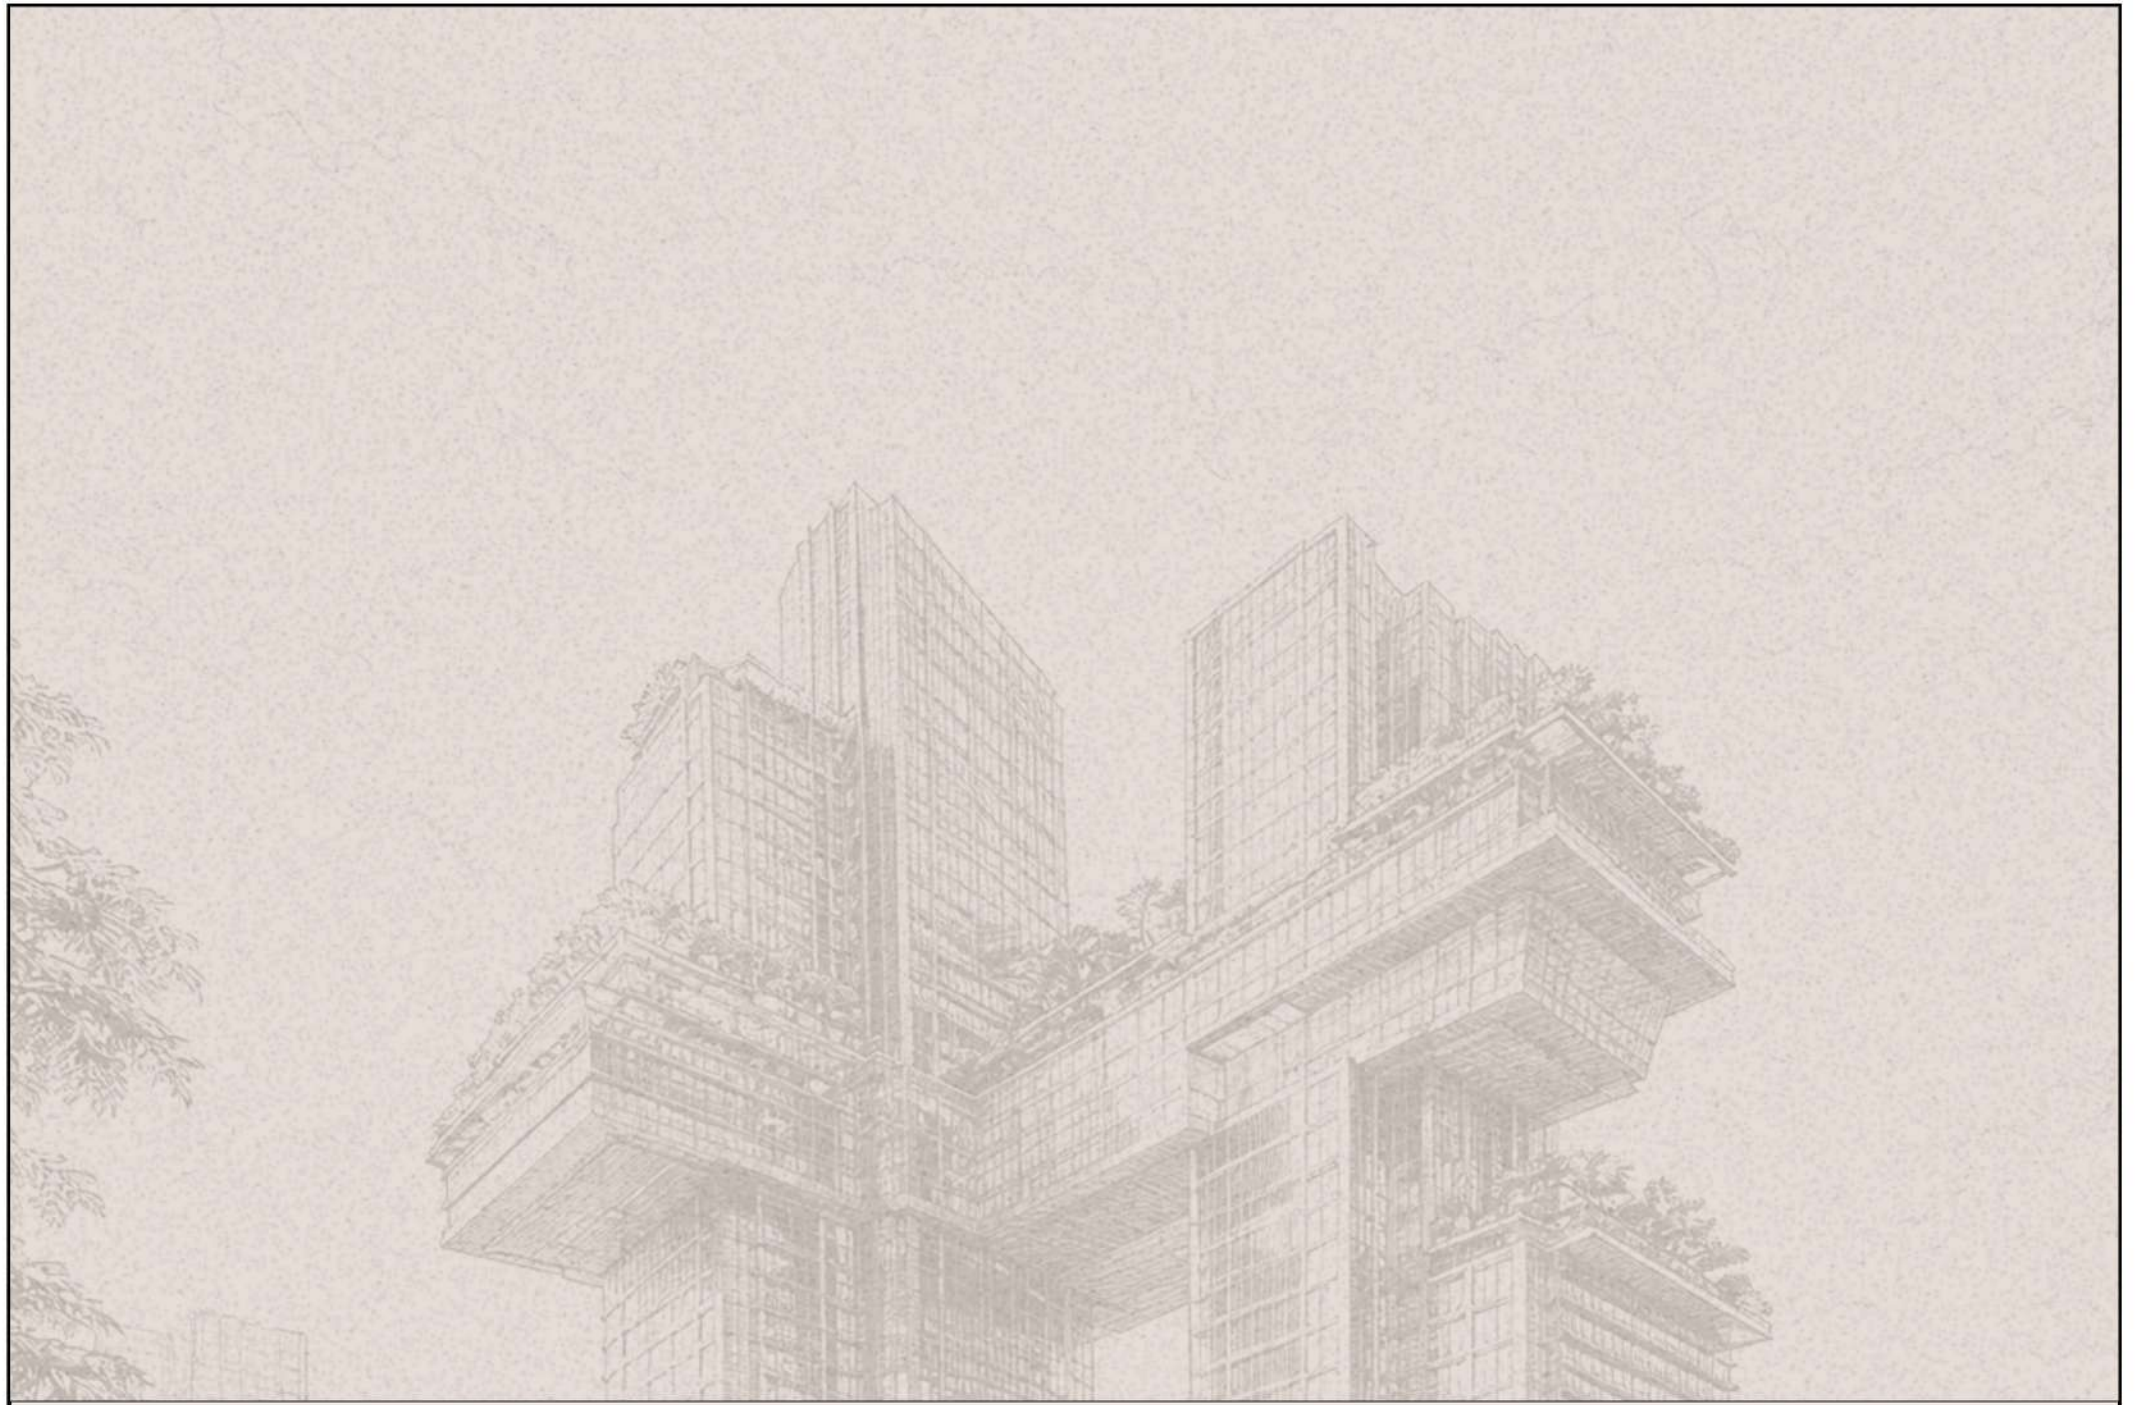

PRECONSTRUCTION

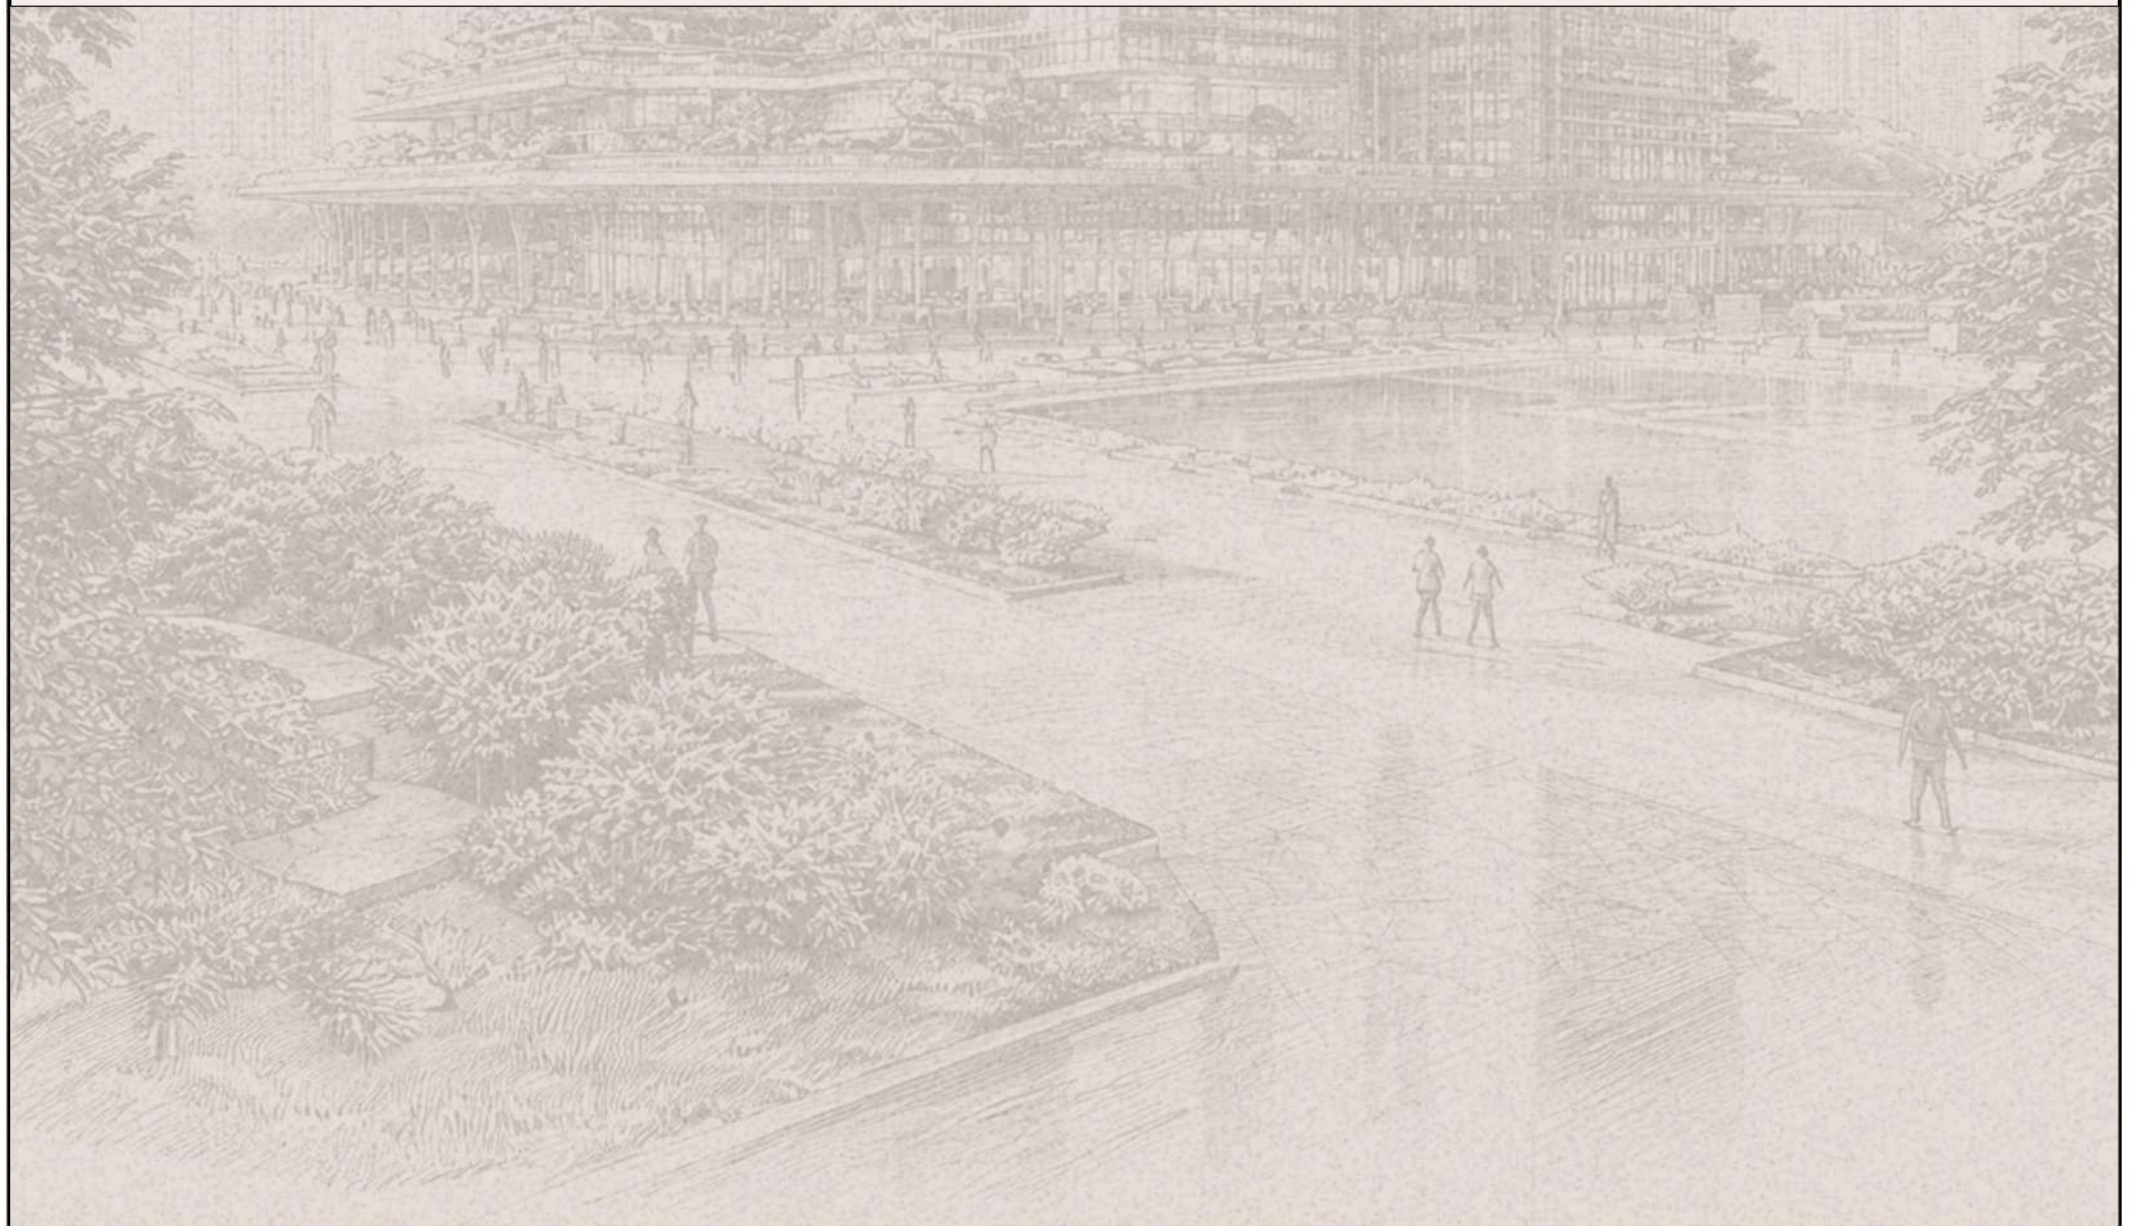

NEXUS TERMINAL

This project was completed over six months, during which I was involved in a comprehensive range of preconstruction activities. Leveraged BIM and Navisworks during preconstruction to coordinate architectural, structural, and MEP models, perform clash detection, and improve constructability. Integrated project schedules from Primavera P6 to support 4D sequencing and visualize construction workflows. Utilized model-based quantity takeoffs and Bluebeam validation to enhance cost accuracy and support informed planning decisions.





PROJECT DESCRIPTION


The Nexus Terminal involves the complete preconstruction development of a multi-level metro station. Beginning with a feasibility study, the project evaluated site suitability, environmental constraints, transit demand, and integration with surrounding urban infrastructure. The design evolved through concept and detailed technical stages, establishing architectural layouts, structural, and coordinated MEP strategies required for a high-capacity transportation hub.

PROJECT SUMMARY


- Project Name: Nexus Terminal
- Project Location and Address: Avenida da Boavista – Porto – Portugal
- Project Coordinates: 41° 9'36.97" N; 8°38'45.76" W
- Total Site Area: 118,403 SF
- Gross Built-Up Area: 260,000 SF
- Project Cost: \$60,082,987
- Project Duration: 530 Days
- Project Delivery Method: Design Build

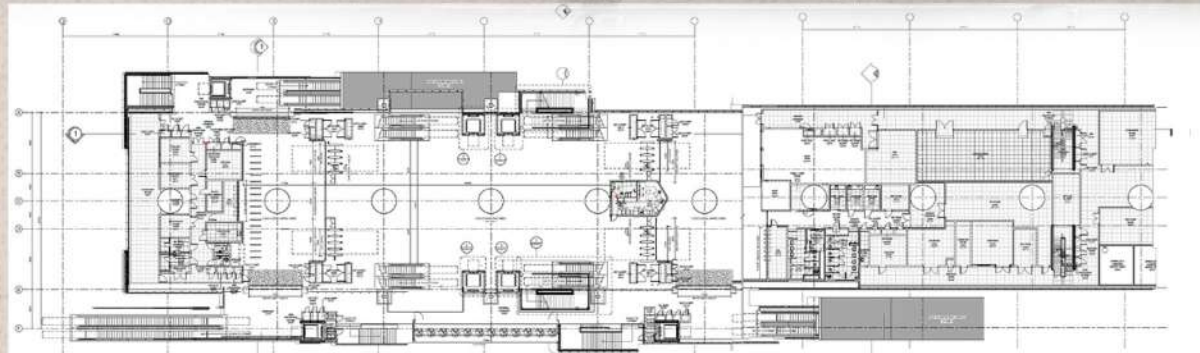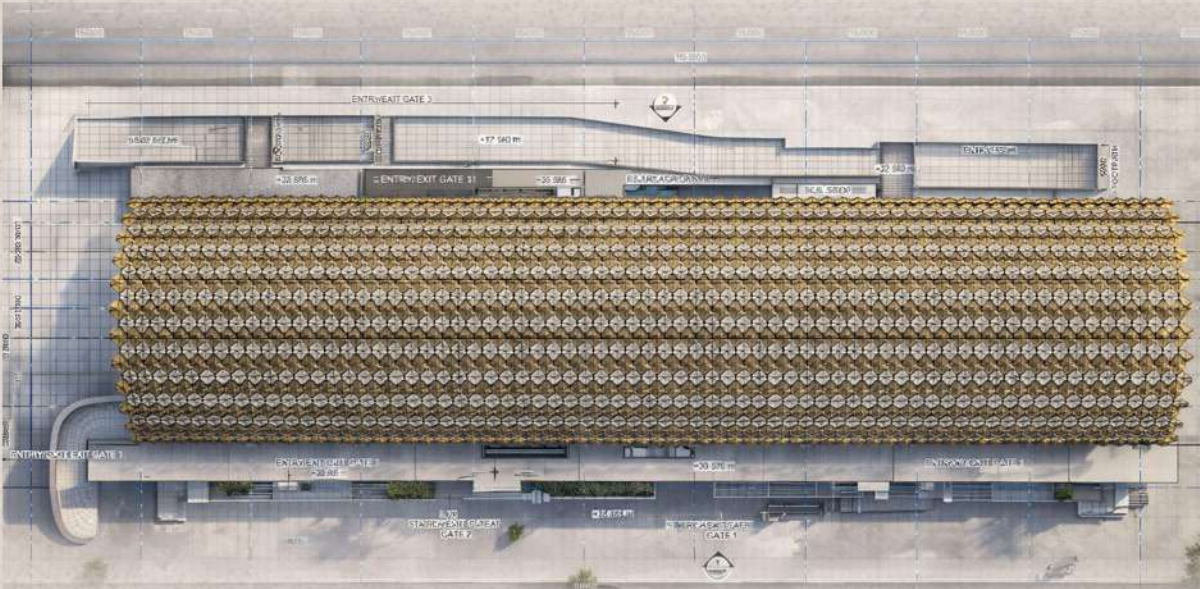

CONCOURSE PLAN

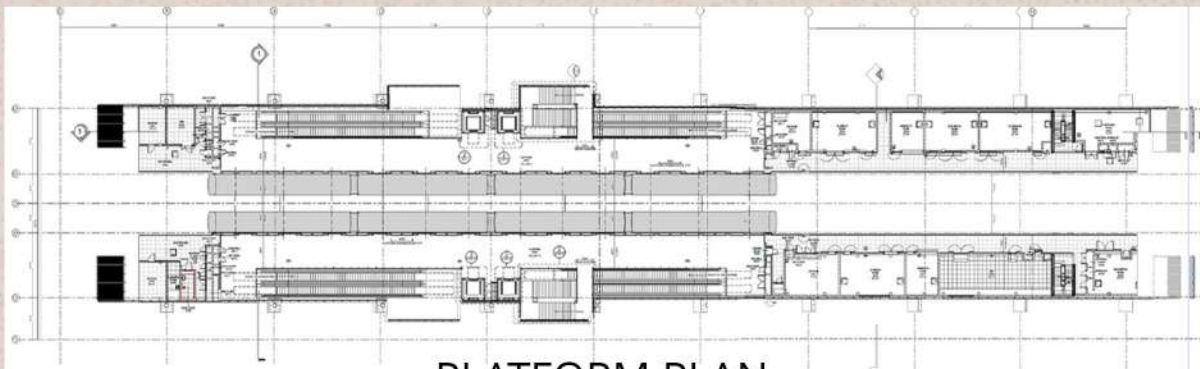

PLATFORM PLAN

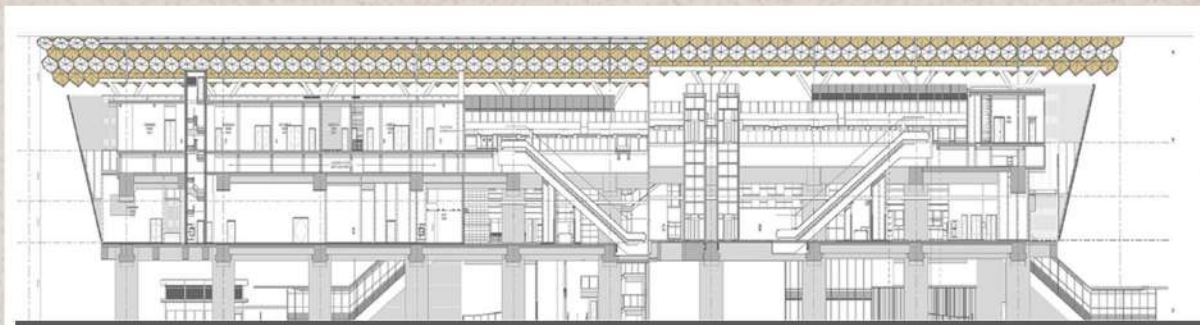

SECTION




FEASIBILITY STUDY

Avenida da Boavista is one of Porto's longest & most strategic urban corridors, linking the city and the coastal tourism belt. Despite its importance, the corridor has historically lacked high-capacity transit.

SITE CONTEXT

- Linear urban corridor with mixed-use development
- High activity near Casa da Música node
- Gradual decrease in density towards western edge
- Existing dependency on road-based transport

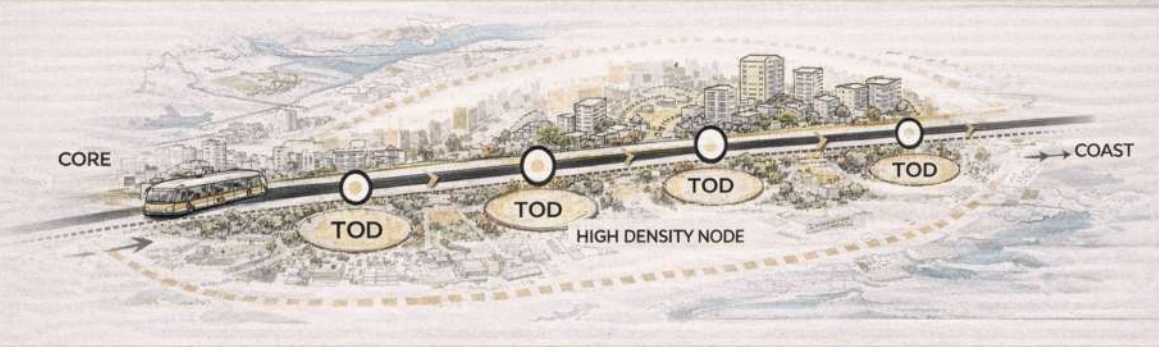

KEY ISSUES IDENTIFIED

1. Mobility & Traffic

- Heavy reliance on private vehicles
- High traffic congestion during peak hours
- Inefficient public transport connectivity



2. Public Transport Gap

- No fixed rail connectivity towards west
- Over-reliance on Bus Rapid Transit (BRT)
- Poor integration between transport modes



3. Hub Overcrowding

- Metro crowding increases
- Bus-to-metro transfers saturate



4. Land Use & Density

- High density concentrated at nodes
- Underutilized land along corridor
- Lack of mixed-use TOD clusters



5. Walkability & Urban Experience

- Wide roads reduce pedestrian accessibility
- Unsafe crossings and limited sidewalks



SOCIAL FEASIBILITY

- Enhances public transport accessibility
- Reduces dependency on private vehicles
- Improves pedestrian safety and walkability
- Supports inclusive mobility (all age groups)
- Activates public spaces and street life

ECONOMIC FEASIBILITY

- Boosts property value along corridor
- Encourages mixed-use commercial development
- Reduces long-term transport costs
- Attracts investment near TOD nodes
- Supports local businesses

ENVIRONMENTAL FEASIBILITY

- Reduces carbon emissions (less car use)
- Promotes public transport + cycling
- Increases green corridors and shading
- Improves air quality
- Supports sustainable urban growth



TECHNICAL FEASIBILITY

- Existing wide corridor supports metro integration
- Phased implementation possible
- Integration with existing BRT network
- Available right-of-way for redesign
- Scalable infrastructure for future growth

ESTIMATION SUMMARY

Level of Estimate-

- Conceptual Estimate: Early estimate based on gross area, typical transit station costs around the area, and major systems were studied and identified. RsMeans quick cost estimation is also used.
- Design Development Estimate (Baseline Budget): Final bid-level quantities and specifications were derived from given design drawings using bluebeam. The rate was taken from RsMeans.
- According to the CSI MasterFormat at the detailed level, WBS are created.

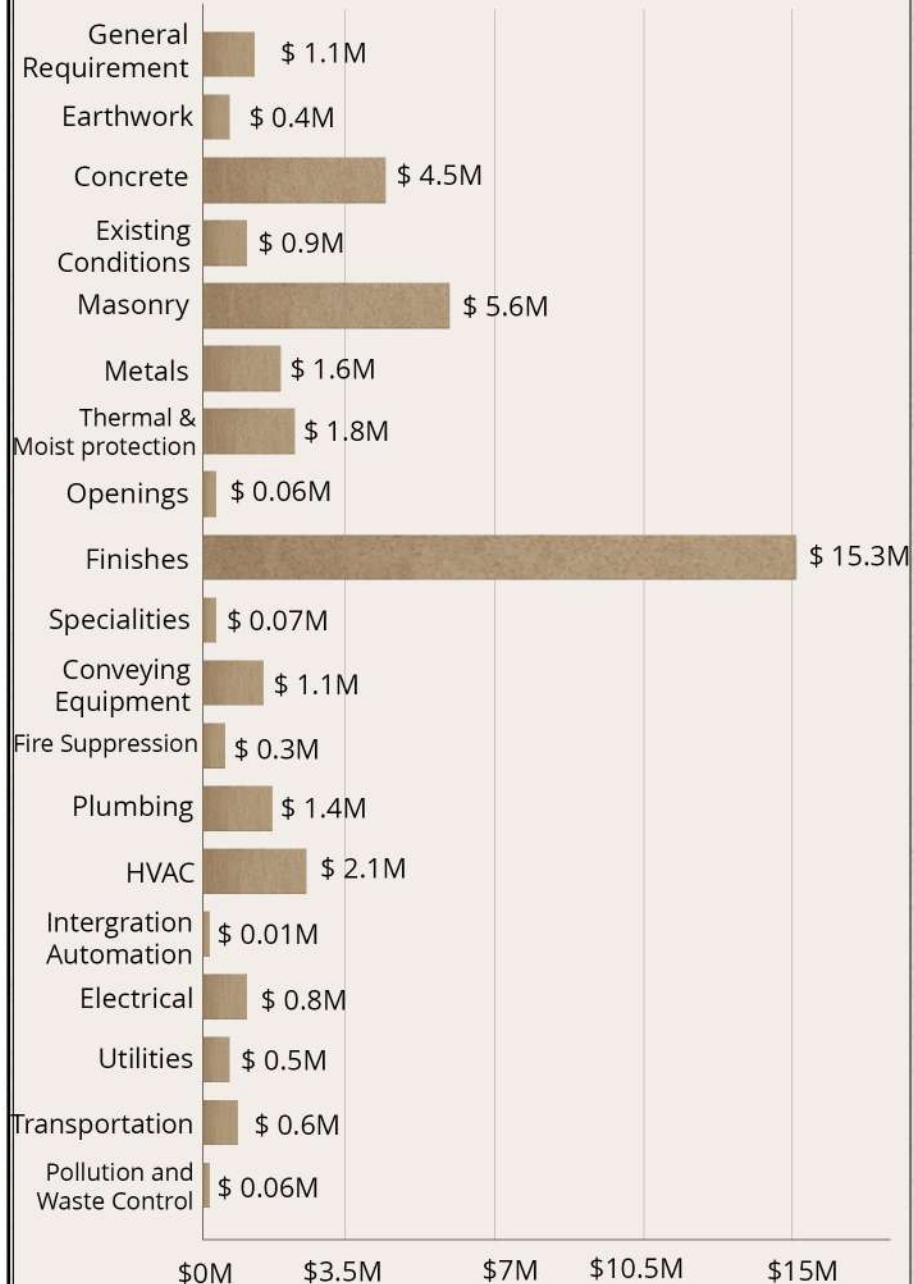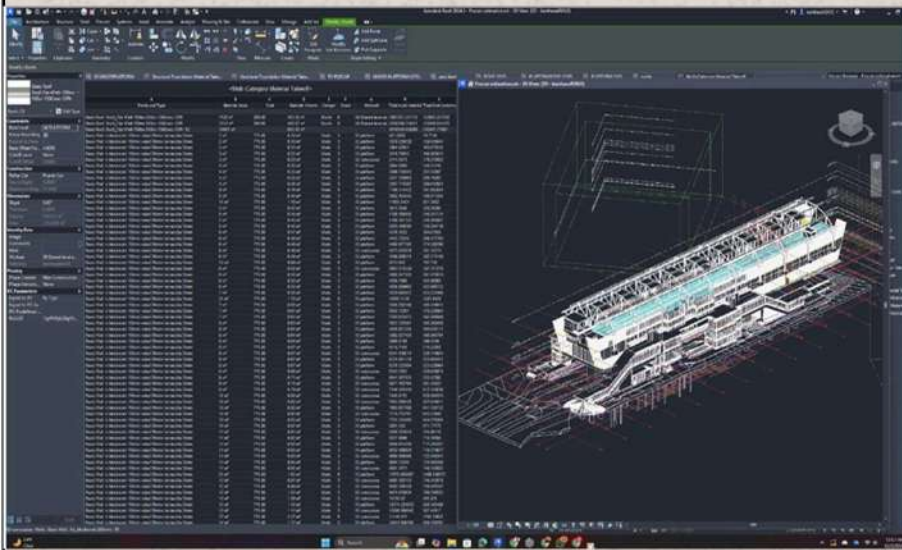

CSI	Trade	Qty	Unit	Unit Cost	Subtotal
01 00 00	GENERAL REQUIREMNET				\$1,074,800
01 30 00	Administrative Requirement	1	LS	\$2,500.00	\$2,500
01 41 00	Regulatory Requirement	1	LS	1800	\$1,800
01 50 00	Temporary Facility ad Controls	1	LS	1066500	\$1,066,500
01 74 00	Cleaning and Waste Management	10	DAYS	400	\$4,000
01 79 00	Demonstration and Training	80	HR		\$0
02 00 00	EXISTING CONDITIONS				8968311.8
02 06 00	Report for Existing Conditions	1	LS	1200	1200
02 21 00	Surveys	1	LS	5000	5000
02 22 00	Existing Conditions Assessment	1	LS	2500	2500
02 24 00	Environmental Assessment	1	LS	8000	8000
02 25 00	Existing Material Assessmenr	1	LS	2200	2200
02 26 00	Hazardous Material Assessment	1	LS	6500	6500
02 41 00	Demolition	1,274,987.40	LS	7	8924911.8
02 50 00	Structure Remediation	1	LS	18000	18000
31 00 00	EARTHWORK				\$401,930
31 63 00	Bored piles	56214	CY	\$7.15	\$401,930
03 00 00	CONCRETE				\$4,464,080
03 20 00	Concrete Reinforcing	1895.3	TONS	\$100.00	\$189,530
03 30 00	Cast-in-Place Concrete	28497	CY	\$150.00	\$4,274,550
04 00 00	MASONRY				\$5,592,489
04 22 00	Concrete Masonry	344,825	SF	\$10.00	\$3,448,250
04 40 00	Stone Assemblies				\$0
04 43 13	Stone Masonry Veneer	102106.6	SF	\$21.00	\$2,144,239
05 00 00	METALS				\$1,597,200
05 12 00	Structural Steel Framing	726	TONS	\$2,200.00	\$1,597,200
07 00 00	THERMAL AND MOISTURE PROTECTION				\$1,830,812
07 13 00	Sheet Waterproofing	94940	SF	\$10.00	\$949,400
07 18 00	Traffic Coatings				\$0
07 18 13	Pedestrian Traffic Coatings	794	SF	\$12.00	\$9,528
07 18 16	vehicular Traffic Coatings	0	SF	\$0.00	\$0
07 50 00	Membrane Roofing	48438	SF	\$18.00	\$871,884
08 00 00	OPENINGS				\$55,690
08 10 00	Doors and Frames				
	D1 - 1510MM X 2400MM SWING DOOR	6	EA	\$800.00	\$4,800
	D2 - 910MM X 2400MM SWING DOOR	60	EA	\$200.00	\$12,000
	D3 - 1250MM X 2200MM SWING DOOR	29	EA	\$300.00	\$8,700
	D4 - 2000MM X 2500MM DOUBLE SWING DOOR	35	EA	\$400.00	\$14,000
	D7 - 1510MM X 2410MM ALUMINIUM LOUVERED DOOR	23	EA	\$550.00	\$12,650
08 44 00	Curtain Walls and Glazed Assemblies				\$0
08 44 13	Glazed Composite Curtain Walls	4	EA	\$885.00	\$3,540
09 00 00	FINISHES				\$15,305,796
09 22 00	Supports for Plaster and Gypsum Board				
09 22 16	Non-Structural Metal Framing	102106.6	SF	\$35.00	\$3,573,731
09 30 00	Tiling				\$0
09 30 13	Ceramic Tiling	295127	SF	\$25.00	\$7,378,175
09 30 33	Stone Tiling	42670.4	SF	\$50.00	\$2,133,520
09 54 00	Speciality Ceilings				\$0
09 54 26	Suspended wood Ceiling	531500	LF	\$2.88	\$1,530,720
09 91 00	Painting				\$0
09 91 23	Interior Painting	344,825	SF	\$2.00	\$689,650
10 00 00	SPECIALITIES				\$72,000
10 11 00	Visual Display Unit	20	EA	\$1,200.00	\$24,000
10 14 00	Signage	120	EA	\$150.00	\$18,000
10 18 00	Information Kiosks	4	EA	\$4,000.00	\$16,000
10 44 00	Fire Protection Specialities	40	EA	\$350.00	\$14,000
14 00 00	CONVEYING EQUIPMENT				\$1,120,000
14 20 00	Elevator	8	EA	\$85,000.00	\$680,000
14 30 00	Escalator	4	EA	\$110,000.00	\$440,000
21 00 00	FIRE SUPPRESSION				\$259,530
21 12 00	Fire Suppression standpipes	800	LF	\$70.00	\$56,000
21 13 00	Sprinkler system	2874	EA	\$45.00	\$129,330
21 20 00	Fire Extinguisher system	115	EA	\$80.00	\$9,200
21 40 00	Fire Suppression Water storage	260	CY	\$250.00	\$65,000
22 00 00	PLUMBING				\$1,353,300
22 10 00	Plumbing Piping	52500	LF	\$25.00	\$1,312,500
22 14 00	Facility Storm Drainage	720	LF	\$35.00	\$25,200
22 30 00	Plumbing Equipment	10	EA	\$1,200.00	\$12,000
22 47 00	Drinking Fountain and water coolers	6		\$600.00	\$3,600
23 00 00	HVAC				\$2,181,700
23 07 00	HVAC Insulation	54000	SF	\$8.00	\$432,000
23 09 00	Controls for HVAC	12	EA	\$600.00	\$7,200
23 21 00	HVAC piping and pumps	8500	LF	\$45.00	\$382,500
23 23 00	Refrigerant piping	5000	LF	\$22.00	\$110,000
23 31 00	HVAC Ducts and Casings	54000	SF	\$20.00	\$1,080,000
23 34 00	HVAC Fans	14	EA	\$1,700.00	\$23,800
23 37 00	Air Outlets and Inlets	180	EA	\$80.00	\$14,400
23 50 00	Central Heating Equipment	4	EA	\$3,500.00	\$14,000
23 73 00	Indoor Central-Station Air-Handling Units	14	EA	\$7,500.00	\$105,000
23 82 00	Convection Heating and Cooling Units	8	EA	\$1,600.00	\$12,800
25 00 00	INTEGRATION AUTOMATION				\$14,400
25 30 00	Integrated Automation Instrumentation and Terminal Devices	120	EA	\$120.00	\$14,400
26 00 00	ELECTRICAL				\$751,150
26 05 33	Raceway and Boxes for Electrical Systems	18000	LF	\$15.00	\$270,000
26 09 00	Instrumentation and Control for Electrical Systems	20	EA	\$90.00	\$1,800
26 11 00	Substations	4	EA	\$40,000.00	\$160,000
26 21 00	Low-Voltage Electrical Service Entrance	600	LF	\$35.00	\$21,000
26 40 00	Electrical Protection	90	EA	\$65.00	\$5,850
26 50 00	Lighting	6500	EA	\$45.00	\$292,500
33 00 00	UTILITIES				\$527,850
33 09 00	Instrumentation and Control for Utilities	18	EA	\$15,000.00	\$270,000
33 10 00	Water Utilities	1200	LF	\$40.00	\$48,000
33 30 00	Sanitary Sewerage	950	LF	\$35.00	\$33,250
33 40 00	Stormwater Utilities	1450	LF	\$38.00	\$55,100
33 50 00	Hydrocarbon Utilities	220	LF	\$25.00	\$5,500
33 70 00	Electrical Utilities	1600	LF	\$50.00	\$80,000
33 80 00	Communications Utilities	1200	LF	\$30.00	\$36,000
34 00 00	TRANSPORTATION				\$624,000
34 42 00	Railway Signaling and Control Equipment	12	EA	25000	300000
34 50 00	Transportation Fare Collection Equipment	18	EA	18000	324000
44 00 00	POLLUTION AND WASTE CONTROL				53000
44 10 00	Air pollution	3	EA	3000	9000
44 20 00	Noise Pollution	8	EA	5000	40000
44 41 00	Water Pollution Containment and Cleanup Equipment	2	EA	2000	4000
DIRECT TOTAL COST					\$46,248,039
INDIRECT COST					
Material Wastage	5% (Masonry + flnishes + metal + Concrete)	5		\$26,959,565	\$1,347,978
Overhead Cost		10	%		\$4,624,804
Contingency		5	%		\$2,312,402
Profit		12	%		\$5,549,765
INDIRECT TOTAL COST					\$13,834,949
TOTAL PROJECT COST					\$60,082,987

Weather Risk- Excavation
& foundation avoided
during monsoon period

[illegible]

CPM ACTIVITIES

Nexus Terminal						
ActivityID	ActivityName	Original Duration	Start	Finish	Total Float	
A12.380	Site context analysis	4	01-Jan-26	06-Jan-26	0	
A12.720	Project Initiation	0	01-Jan-26		0	
A12.90	Establish Benchmarks & Horizontal Layout & As Built	1	17-Jan-26*	07-Jan-26	0	
A13.00	Well Layout & As Built	2	18-Jan-26*	09-Jan-26	0	
A13.10	Layout and Transfer Building	3	2-Jan-26*	14-Jan-26	0	
A13.20	Site Sheet	3	5-Jan-26*	19-Jan-26	0	
A13.30	Final Survey with Final Elevation	0		19-Jan-26	0	
A12.410	Technical feasibility	4	20-Jan-26	23-Jan-26	0	
A12.420	cost and time feasibility	2	26-Jan-26	27-Jan-26	0	
A12.430	Feasibility report	2	28-Jan-26	29-Jan-26	0	
A12.440	Architectural concept design	14	30-Jan-26	18-Feb-26	0	
A12.480	Concept Design report	3	19-Feb-26	23-Feb-26	0	
A12.620	Architecture DD	14	24-Feb-26	13-Mar-26	0	
A12.650	Integration Review	5	16-Mar-26	20-Mar-26	0	
A12.730	Construction Drawing Documents	2	13-Mar-26	24-Mar-26	0	
A12.530	Quantity takeoff BOQ	7	15-Mar-26	02-Apr-26	0	
A12.540	Cost Estimation	4	03-Apr-26	08-Apr-26	0	
A12.550	Tender Document	7	09-Apr-26	17-Apr-26	0	
A12.560	Tender issuance	5	20-Apr-26	24-Apr-26	0	
A12.570	Bid Period	14	27-Apr-26	4-May-26	0	
A12.580	Bid Evaluation	7	5-May-26	5-May-26	0	
A12.590	Negotiation	5	16-May-26	01-Jun-26	0	
A12.600	Contract award	3	02-Jun-26	04-Jun-26	0	
A10.70	Submit Material Details	10	05-Jun-26	18-Jun-26	0	
A11.10	Submit Curtain Wall System	10	15-Jun-26*	18-Jun-26	0	
A12.610	Notice to Proceed	0	05-Jun-26		0	
A11.40	Approve Material Details Sub	7	19-Jun-26	29-Jun-26	0	
A11.80	Approve Curtain Wall System	7	9-Jul-26*	29-Jun-26	0	
A12.10	Deliver Materials	20	30-Jun-26	27-Jul-26	0	
A12.50	Fabricate and Deliver Curtain	20	10-Jul-26*	27-Jul-26	0	
A12.760	Material storage setup	5	28-Jul-26	03-Aug-26	0	
A13.60	Mass Excavation	2	4-Aug-26*	05-Aug-26	0	
A13.70	Leveling and Compacting	2	06-Aug-26	07-Aug-26	0	
A13.80	Install Perimeter Drains	2	10-Aug-26	11-Aug-26	0	
A13.90	Excavated Material Disposal	2	12-Aug-26	13-Aug-26	0	
A14.00	Excavate Utility Lines	2	14-Aug-26	17-Aug-26	0	
A14.00	Install Utility Lines	2	18-Aug-26	19-Aug-26	0	
A15.20	Surveying and Marking Pile Locations	3	21-Aug-26	25-Aug-26	0	
A15.40	Alignment Check	2	31-Aug-26	01-Sep-26	0	
A15.50	Boring of Piles	17	02-Sep-26	24-Sep-26	0	
A15.60	Install Reinforcement Cage	10	25-Sep-26	08-Oct-26	0	
A15.70	Pouring of Concrete	12	09-Oct-26	26-Oct-26	0	
A15.80	Pile Cutting & Capping	10	27-Oct-26	09-Nov-26	0	
A15.90	Backfill Footings and Level the Form	4	10-Nov-26	13-Nov-26	0	
A16.00	Form and Installation for mat	15	16-Nov-26	04-Dec-26	0	
A16.10	Rebar Installation for mat slab	20	07-Dec-26	01-Jan-27	0	
A12.380	Site context analysis	4	01-Jan-26	06-Jan-26	0	
A12.720	Project Initiation	0	01-Jan-26		0	
A12.90	Establish Benchmarks & Horizontal Layout & As Built	1	17-Jan-26*	07-Jan-26	0	
A13.00	Well Layout & As Built	2	18-Jan-26*	09-Jan-26	0	
A13.10	Layout and Transfer Building	3	2-Jan-26*	14-Jan-26	0	
A13.20	Site Sheet	3	5-Jan-26*	19-Jan-26	0	
A13.30	Final Survey with Final Elevation	0		19-Jan-26	0	
A12.410	Technical feasibility	4	20-Jan-26	23-Jan-26	0	
A12.420	cost and time feasibility	2	26-Jan-26	27-Jan-26	0	
A12.430	Feasibility report	2	28-Jan-26	29-Jan-26	0	
A12.440	Architectural concept design	14	30-Jan-26	18-Feb-26	0	
A12.480	Concept Design report	3	19-Feb-26	23-Feb-26	0	
A12.620	Architecture DD	14	24-Feb-26	13-Mar-26	0	
A12.650	Integration Review	5	16-Mar-26	20-Mar-26	0	
A12.730	Construction Drawing Documents	2	13-Mar-26	24-Mar-26	0	
A12.530	Quantity takeoff BOQ	7	15-Mar-26	02-Apr-26	0	
A12.540	Cost Estimation	4	03-Apr-26	08-Apr-26	0	
A12.550	Tender Document	7	09-Apr-26	17-Apr-26	0	
A12.560	Tender issuance	5	20-Apr-26	24-Apr-26	0	
A12.570	Bid Period	14	27-Apr-26	4-May-26	0	
A12.580	Bid Evaluation	7	5-May-26	5-May-26	0	
A12.590	Negotiation	5	16-May-26	01-Jun-26	0	
A12.600	Contract award	3	02-Jun-26	04-Jun-26	0	
A10.70	Submit Material Details	10	05-Jun-26	18-Jun-26	0	
A11.10	Submit Curtain Wall System	10	15-Jun-26*	18-Jun-26	0	
A12.610	Notice to Proceed	0	05-Jun-26		0	
A11.40	Approve Material Details Sub	7	19-Jun-26	29-Jun-26	0	
A11.80	Approve Curtain Wall System	7	9-Jul-26*	29-Jun-26	0	
A12.10	Deliver Materials	20	30-Jun-26	27-Jul-26	0	
A12.50	Fabricate and Deliver Curtain	20	10-Jul-26*	27-Jul-26	0	
A12.760	Material storage setup	5	28-Jul-26	03-Aug-26	0	
A13.60	Mass Excavation	2	4-Aug-26*	05-Aug-26	0	
A13.70	Leveling and Compacting	2	06-Aug-26	07-Aug-26	0	
A13.80	Install Perimeter Drains	2	10-Aug-26	11-Aug-26	0	
A13.90	Excavated Material Disposal	2	12-Aug-26	13-Aug-26	0	
A14.00	Excavate Utility Lines	2	14-Aug-26	17-Aug-26	0	
A14.00	Install Utility Lines	2	18-Aug-26	19-Aug-26	0	
A15.20	Surveying and Marking Pile Locations	3	21-Aug-26	25-Aug-26	0	
A15.40	Alignment Check	2	31-Aug-26	01-Sep-26	0	
A15.50	Boring of Piles	17	02-Sep-26	24-Sep-26	0	
A15.60	Install Reinforcement Cage	10	25-Sep-26	08-Oct-26	0	
A15.70	Pouring of Concrete	12	09-Oct-26	26-Oct-26	0	
A15.80	Pile Cutting & Capping	10	27-Oct-26	09-Nov-26	0	
A15.90	Backfill Footings and Level the Form	4	10-Nov-26	13-Nov-26	0	
A16.00	Form and Installation for mat	15	16-Nov-26	04-Dec-26	0	
A16.10	Rebar Installation for mat slab	20	07-Dec-26	01-Jan-27	0	
A11.720	Site Final Cleaning	5	02-Dec-27	08-Dec-27	0	
A11.730	Architect Walk through	1	08-Dec-27	09-Dec-27	0	
A11.740	Substantial Completion	0		09-Dec-27	0	
A11.810	Testing	5	10-Dec-27	16-Dec-27	0	
A11.760	Correct Punch list	2	17-Dec-27	20-Dec-27	0	
A12.710	BMS Integration	12	17-Dec-27	03-Jan-28	0	
A12.690	Develop O&M Strategy	10	21-Dec-27	03-Jan-28	0	
A12.700	Facility management Planning	10	21-Dec-27	03-Jan-28	0	
A11.770	Operational Training	3	04-Jan-28	06-Jan-28	0	
A11.780	Owner Sign-off	1	07-Jan-28	07-Jan-28	0	
A11.790	Records and Certificate	3	10-Jan-28	12-Jan-28	0	
A11.800	Project Closeout	0		12-Jan-28	0	



MIAMI TOWER

The proposed development is the construction of a Bank & Office Tower located in Miami, Florida. This landmark project is envisioned to enhance the city's skyline, integrating cutting-edge architectural design with functional excellence. It will include state-of-the-art facilities tailored to the needs of both banking operations and office spaces, serving as a hub for business and community activities.

The scope of my role involved a comprehensive engagement across preconstruction and planning phases, including site logistics coordination, quantity takeoff and cost estimation, and construction scheduling. I contributed to developing efficient site strategies, accurate budgeting, and time-based planning to ensure seamless project execution.



PROJECT SUMMARY

- Project Name: Bank and Office Tower
- Project Location- Miami, Florida
- Total Site Area: 342,685 SF
- Gross Built-Up Area: 57,233 SF
- Project Cost: \$147,387,115
- Project Duration: 714 Days
- Project Delivery Method: Design Bid Build




DESIGN CONCEPT

A cutting-edge architectural marvel with a sleek, twisted form that soars skyward, symbolizing modernity and innovation at the city's skyline.




KEY FEATURES


- Bold, futuristic design with a striking inverted trapezoidal shape.
- 25 stories of premium office and banking space
- LEED-certified, with eco-friendly design elements
- High-end retail and amenities at the base
- Panoramic views of the Miami skyline and ocean
- A landmark structure designed to enhance the urban landscape
- Modern Technology collaboration for better coordination

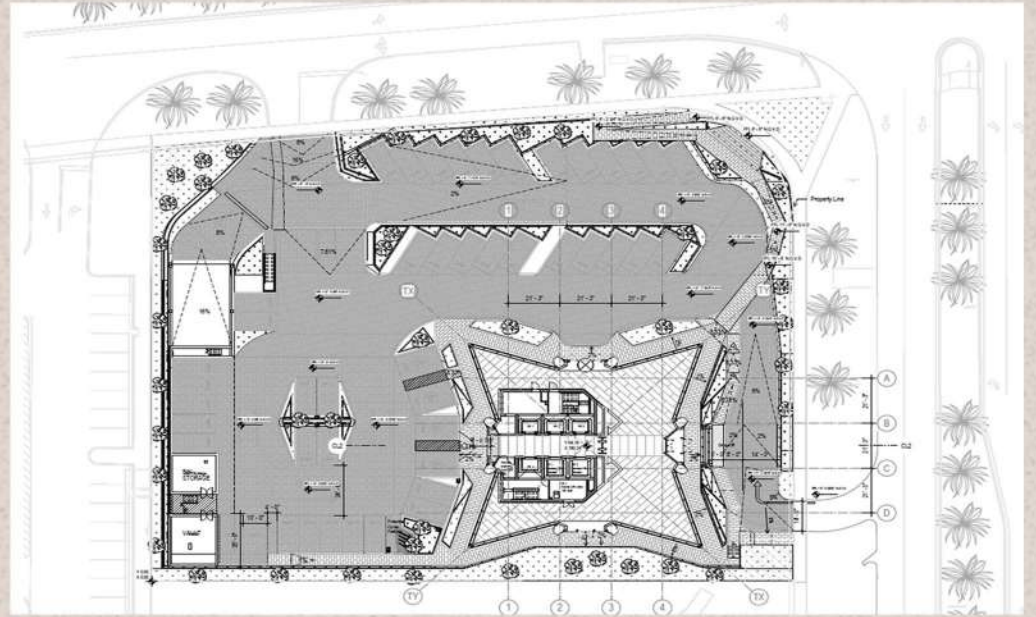


MASTER PLAN

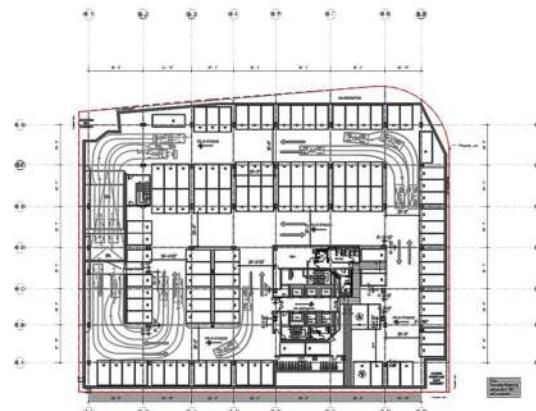


PARKING BASEMENT 3-1

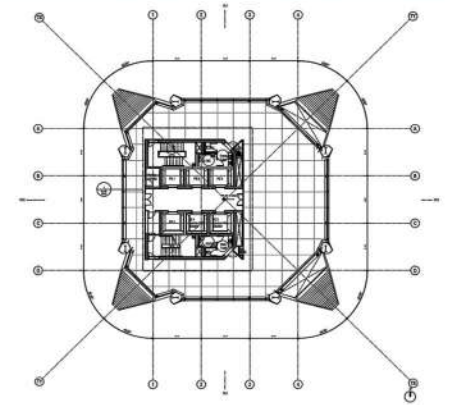




GROUND FLOOR PLAN

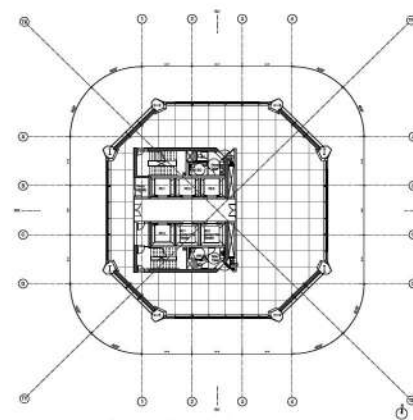


FLOOR PLAN 2- 12

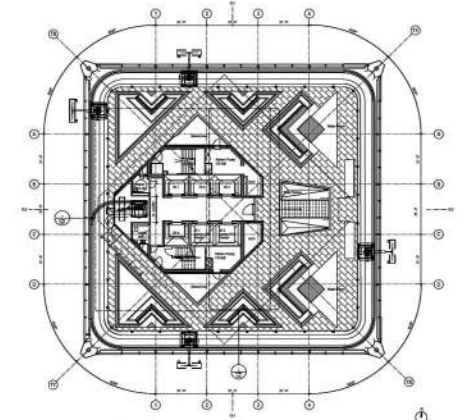

TERRACE PLAN

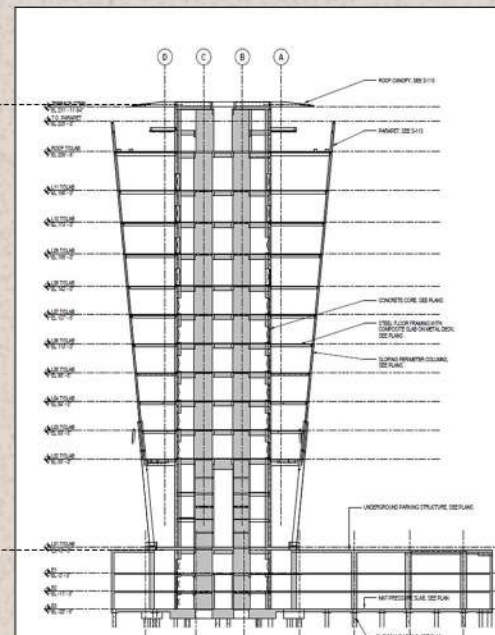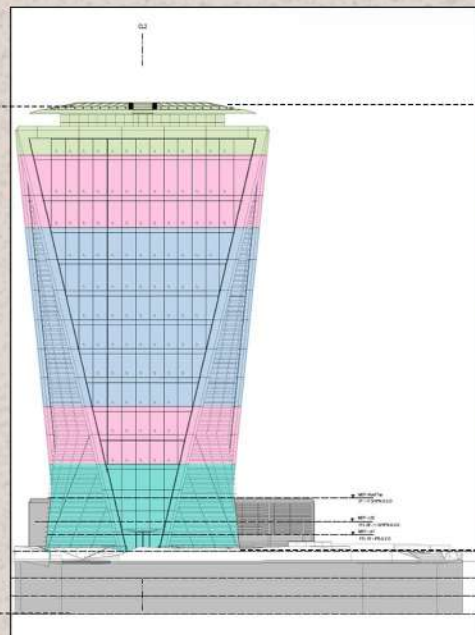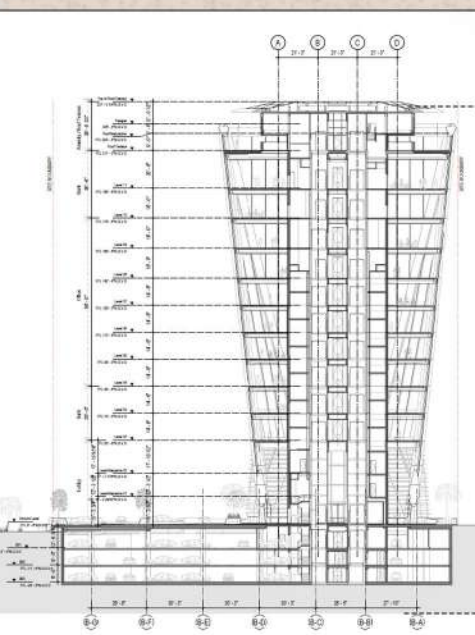

SITE LOGISTICS

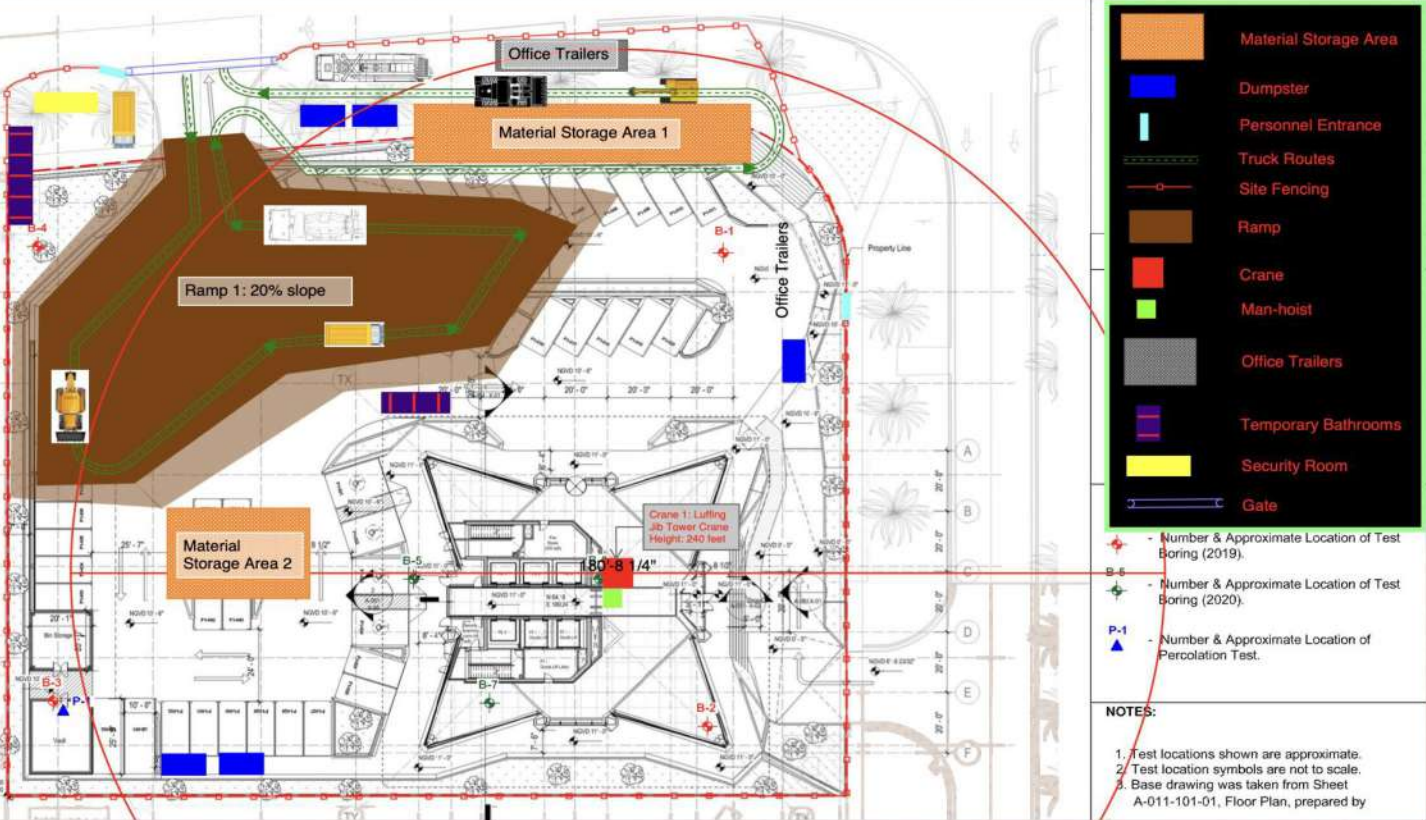

Crane Placement: A 240-foot luffing jib tower crane optimally positioned for efficient material handling.

- Material Storage: Two dedicated areas ensure streamlined access and reduced transit times.
- Worker Facilities: Temporary offices, restrooms, and break areas enhance comfort and productivity.
- Clearly marked entry and exit points to minimize congestion and maintain safety.
- Real-time monitoring of traffic conditions to adjust routes as necessary.

ESTIMATION

PROJECT: Bank & Office Building, Miami FL
LOCATION: Corner of Ave. A & Street B, Miami, Florida

Construction Start (NTP): 12/23/24
Construction Finish (TCO): 9/16/27
Duration: 142.43 weeks
Duration: 32.86 months

Weeks: 142
Months: 33
Date: 12/12/24

Job Title	Notes (ie: Name)	Salary + Burden	Weekly Rate	Start	Finish	# Of Weeks	% of time on job	Subtotal	3% Raises	Total Labor
Monthly Allocations:										
VP Operations	Max Verstappen	\$ 674,960.00	\$ 12,980.00	12/23/24	9/16/27	142.43	5%	\$ 92,436.14	\$ 2,773.08	\$ 95,209.23
Director Of Field Ops	Serena Williams	\$ 552,240.00	\$ 10,620.00	12/23/24	9/16/27	142.43	10%	\$ 151,259.14	\$ 4,537.77	\$ 155,796.92
Regional Safety Director	Elon Musk	\$ 429,520.00	\$ 8,260.00	12/23/24	9/16/27	142.43	5%	\$ 58,823.00	\$ 1,764.69	\$ 60,587.69
Regional Scheduling Director	Dwayne Johnson	\$ 386,360.00	\$ 7,430.00	12/23/24	9/16/27	142.43	5%	\$ 52,912.21	\$ 1,587.37	\$ 54,499.58
Regional BIM / VDC Director	Scarlett Johansson	\$ 411,320.00	\$ 7,910.00	12/23/24	9/16/27	142.43	5%	\$ 56,330.50	\$ 1,689.92	\$ 58,020.42
Project Executive III	Brad Pitt	\$ 515,320.00	\$ 9,910.00	12/23/24	9/16/27	142.43	10%	\$ 141,146.71	\$ 4,234.40	\$ 145,381.12
Project Executive II	Gaja Gana	\$ 460,200.00	\$ 8,850.00	12/23/24	9/16/27	142.43	10%	\$ 126,049.29	\$ 3,781.48	\$ 129,830.76
Project Executive I	Nishan S	\$ 411,320.00	\$ 7,910.00	12/23/24	9/16/27	142.43	10%	\$ 112,661.00	\$ 3,379.83	\$ 116,040.83
Main Office Support Staff:										
Chief Estimator	Roshan Raj Kantharaja	\$ 497,120.00	\$ 9,560.00	12/23/24	9/16/27	142.43	5%	\$ 68,080.86	\$ 2,042.43	\$ 70,123.28
Estimating Manager	Daniel Craig	\$ 349,960.00	\$ 6,730.00	12/23/24	9/16/27	142.43	5%	\$ 47,927.21	\$ 1,437.82	\$ 49,365.03
Senior Estimator I	Jennifer Lawrence	\$ 349,960.00	\$ 6,730.00	12/23/24	9/16/27	142.43	10%	\$ 95,854.43	\$ 2,875.63	\$ 98,730.06
Estimator I	Chris Hemsworth	\$ 221,000.00	\$ 4,250.00	12/23/24	9/16/27	142.43	10%	\$ 60,532.14	\$ 1,815.96	\$ 62,348.11
MEP Estimator	Natalie Portman	\$ 221,000.00	\$ 4,250.00	12/23/24	9/16/27	142.43	5%	\$ 30,266.07	\$ 907.98	\$ 31,174.05
BIM / VDC Manager	Jared James	\$ 170,560.00	\$ 3,280.00	12/23/24	9/16/27	142.43	5%	\$ 23,358.29	\$ 700.75	\$ 24,059.03
Project Management Staff:										
Senior Project Manager II	Angelina Jolie	\$ 411,320.00	\$ 7,910.00	12/23/24	9/16/27	142.43	15%	\$ 168,991.50	\$ 5,069.75	\$ 174,061.25
Senior Project Manager I	Tom Cruise	\$ 331,240.00	\$ 6,370.00	12/23/24	9/16/27	142.43	15%	\$ 136,090.50	\$ 4,082.72	\$ 140,173.22
Project Manager II	Karthik Girkala	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	20%	\$ 164,647.43	\$ 4,939.42	\$ 169,586.85
Project Manager II	Gal Gadot	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	20%	\$ 164,647.43	\$ 4,939.42	\$ 169,586.85
Project Manager II	Ryan Reynolds	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	20%	\$ 164,647.43	\$ 4,939.42	\$ 169,586.85
Project Manager I	Chris Pratt	\$ 257,920.00	\$ 4,960.00	12/23/24	9/16/27	142.43	20%	\$ 141,289.14	\$ 4,238.67	\$ 145,527.82
Project Manager I	Henry Cavill	\$ 257,920.00	\$ 4,960.00	12/23/24	9/16/27	142.43	20%	\$ 141,289.14	\$ 4,238.67	\$ 145,527.82
Project Manager I	Zendaya	\$ 257,920.00	\$ 4,960.00	12/23/24	9/16/27	142.43	20%	\$ 141,289.14	\$ 4,238.67	\$ 145,527.82
Assist. Project Manager II	Timothée Chalamet	\$ 221,000.00	\$ 4,250.00	12/23/24	9/16/27	142.43	10%	\$ 60,532.14	\$ 1,815.96	\$ 62,348.11
Assist. Project Manager II	Florence Pugh	\$ 221,000.00	\$ 4,250.00	12/23/24	9/16/27	142.43	10%	\$ 60,532.14	\$ 1,815.96	\$ 62,348.11
Assist. Project Manager II	Anya Taylor-Joy	\$ 221,000.00	\$ 4,250.00	12/23/24	9/16/27	142.43	10%	\$ 60,532.14	\$ 1,815.96	\$ 62,348.11
Assist. Project Manager I	Millie Bobby Brown	\$ 184,080.00	\$ 3,540.00	12/23/24	9/16/27	142.43	10%	\$ 50,419.71	\$ 1,512.59	\$ 51,932.31
Assist. Project Manager I	Finn Wolfhard	\$ 184,080.00	\$ 3,540.00	12/23/24	9/16/27	142.43	10%	\$ 50,419.71	\$ 1,512.59	\$ 51,932.31
Assist. Project Manager I	Simu Liu	\$ 184,080.00	\$ 3,540.00	12/23/24	9/16/27	142.43	10%	\$ 50,419.71	\$ 1,512.59	\$ 51,932.31
MEP Project Manager	Awkwafina	\$ 294,320.00	\$ 5,660.00	12/23/24	9/16/27	142.43	15%	\$ 120,921.86	\$ 3,627.66	\$ 124,549.51
Project Engineer	Noah Schnapp	\$ 153,400.00	\$ 2,950.00	12/23/24	9/16/27	142.43	15%	\$ 63,024.64	\$ 1,890.74	\$ 64,915.38
Intern	Gandhi	\$ 98,280.00	\$ 1,890.00	12/23/24	9/16/27	142.43	2%	\$ 5,383.80	\$ 161.51	\$ 5,545.31
Project Controller	Snegha Sugandarraj	\$ 269,880.00	\$ 5,190.00	12/23/24	9/16/27	142.43	5%	\$ 36,960.21	\$ 1,108.81	\$ 38,069.02
Project Accountant	Millie Bobby Brown	\$ 177,840.00	\$ 3,420.00	12/23/24	9/16/27	142.43	5%	\$ 24,355.29	\$ 730.66	\$ 25,085.94
Scheduler	Finn Wolfhard	\$ 313,040.00	\$ 6,020.00	12/23/24	9/16/27	142.43	5%	\$ 42,871.00	\$ 1,286.13	\$ 44,157.13
Junior Scheduler	Noah Schnapp	\$ 202,280.00	\$ 3,890.00	12/23/24	9/16/27	142.43	5%	\$ 27,702.36	\$ 831.07	\$ 28,533.43
Project Administrator	Anya Taylor-Joy	\$ 128,960.00	\$ 2,480.00	12/23/24	9/16/27	142.43	5%	\$ 17,661.14	\$ 529.83	\$ 18,190.98
On-Site Field Staff:										
General Superintendent I	Rohan Babu Soumya Babu	\$ 546,000.00	\$ 10,500.00	12/23/24	9/16/27	142.43	10%	\$ 149,550.00	\$ 4,486.50	\$ 154,036.50
Senior Superintendent III	Tom Brady	\$ 472,680.00	\$ 9,090.00	12/23/24	9/16/27	142.43	10%	\$ 129,467.57	\$ 3,884.03	\$ 133,351.60
Senior Superintendent II	Roger Federer	\$ 423,280.00	\$ 8,140.00	12/23/24	9/16/27	142.43	10%	\$ 115,936.86	\$ 3,478.11	\$ 119,414.96
Senior Superintendent I	Rafael Nadal	\$ 392,600.00	\$ 7,550.00	12/23/24	9/16/27	142.43	10%	\$ 107,533.57	\$ 3,226.01	\$ 110,759.58
Superintendent III	Kevin Durant	\$ 349,960.00	\$ 6,730.00	12/23/24	9/16/27	142.43	10%	\$ 95,854.43	\$ 2,875.63	\$ 98,730.06
Superintendent III	Stephen Curry	\$ 349,960.00	\$ 6,730.00	12/23/24	9/16/27	142.43	10%	\$ 95,854.43	\$ 2,875.63	\$ 98,730.06
Superintendent III	Stephan Mango	\$ 349,960.00	\$ 6,730.00	12/23/24	9/16/27	142.43	10%	\$ 95,854.43	\$ 2,875.63	\$ 98,730.06
Superintendent II	Giannis Antetokounmpo	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	10%	\$ 82,323.71	\$ 2,469.71	\$ 84,793.43
Superintendent II	Nikola Jokic	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	10%	\$ 82,323.71	\$ 2,469.71	\$ 84,793.43
Superintendent II	Joel Embiid	\$ 300,560.00	\$ 5,780.00	12/23/24	9/16/27	142.43	10%	\$ 82,323.71	\$ 2,469.71	\$ 84,793.43
Superintendent I	Luka Doncic	\$ 257,400.00	\$ 4,950.00	12/23/24	9/16/27	142.43	10%	\$ 70,502.14	\$ 2,115.06	\$ 72,617.21
Superintendent I	Ja Morant	\$ 257,400.00	\$ 4,950.00	12/23/24	9/16/27	142.43	10%	\$ 70,502.14	\$ 2,115.06	\$ 72,617.21
Superintendent I	Jayson Tatum	\$ 257,400.00	\$ 4,950.00	12/23/24	9/16/27	142.43	10%	\$ 70,502.14	\$ 2,115.06	\$ 72,617.21
Assistant Superintendent I	Zion Williamson	\$ 196,560.00	\$ 3,780.00	12/23/24	9/16/27	142.43	10%	\$ 53,838.00	\$ 1,615.14	\$ 55,453.14
Assistant Superintendent I	Anthony Edwards	\$ 196,560.00	\$ 3,780.00	12/23/24	9/16/27	142.43	10%	\$ 53,838.00	\$ 1,615.14	\$ 55,453.14
Assistant Superintendent I	LaMelo Ball	\$ 196,560.00	\$ 3,780.00	12/23/24	9/16/27	142.43	10%	\$ 53,838.00	\$ 1,615.14	\$ 55,453.14
MEP Superintendent	Kawhi Leonard	\$ 245,440.00	\$ 4,720.00	12/23/24	9/16/27	142.43	10%	\$ 67,226.29	\$ 2,016.79	\$ 69,243.07
Senior Safety Manager I	Ajit Kumar	\$ 282,360.00	\$ 5,430.00	12/23/24	9/16/27	142.43	10%	\$ 77,338.71	\$ 2,320.16	\$ 79,658.88
Safety Manager I	Draymond Green	\$ 257,920.00	\$ 4,960.00	12/23/24	9/16/27	142.43	10%	\$ 70,644.57	\$ 2,119.34	\$ 72,763.91
Totals								\$ 4,637,517.01	\$ 139,125.51	\$ 4,776,642.52

Estimate Summary


Project:	Bank & Office Building, Miami FL	Total GSF	342,685
Location:	Corner of Ave. A & Street B, Miami, Florida	Office Tower	126,263
Owner:	Jonathan Holzer	Subterranean Parking Garage	159,189
Drawing Phase:	100%DD Complete	Ground Floor Site & Parking	57,233
Estimate Date:	December 12, 2024		
Prepared By:	SKRR Constructions		

Item	Description	Price
01-30-10	General Requirements	\$5,795,098
01-40-60	Site Safety	in GRs
01-54-42	Final Cleaning	in GRs
02-21-00	Survey	\$28,000
03-00-10	Concrete Shell	\$11,877,000
04-20-00	Masonry	\$0
05-10-00	Structural steel	\$6,962,600
05-50-00	Misc. Metals	\$3,537,170
07-10-00	Waterproofing	\$3,484,000
07-50-00	Roofing	\$533,612
07-81-00	Fireproofing	\$344,500
08-11-00	Doors and Hardware	\$407,225
08-33-00	Overhead doors	\$26,000
08-50-00	Curtainwall Systems and Metal Cladding	\$25,400,434
09-00-10	General Finishes	\$9,269,273
09-21-00	Framing and Drywall	\$5,380,769
09-24-00	Stucco	N/A
09-91-00	Painting	\$291,282
10-00-10	Specialties	\$85,424
11-24-00	Window Washing Equipment	\$1,430,000
13-10-00	Water Features	\$195,000
14-20-00	Elevators and Lifts	\$4,271,260
21-10-00	Fire Protection	\$740,200
22-10-00	Plumbing	\$2,895,688
23-00-00	HVAC	\$4,035,004
26-00-10	Electrical	\$6,338,525
27-00-00	IT / AV / Security Systems	\$1,456,411
31-00-10	Sitework	\$937,684
31-00-20	Site Demolition and Hardscape	\$1,300,000
31-23-19	Dewatering	In Foundations
31-63-00	Deep Soil Mix / Augercast Piles	\$18,120,570
32-14-00	Unit Pavers	\$373,968
32-90-00	Landscaping	\$325,000
33-20-00	Drainage Well	In Site Work
	Subtotal	\$115,841,695
	Subcontractor Bonds	0.50% \$579,208
	Subtotal	\$116,420,904
	General Conditions	\$5,358,120
	Subtotal	\$121,779,024
	Owner Design Development Contingency	8.00% \$9,742,322
	Contractor Contingency	4.00% \$4,871,161
	Subtotal	\$136,392,507
	Construction Management Fee	5.00% \$6,819,625
	Subtotal	\$143,212,132
	Insurance - Other (OCIP by Owner)	1.50% \$2,148,182
	Subtotal	\$145,360,314
	Payment & Performance Bond	0.50% \$726,802
	Subtotal	\$146,087,115
	Preconstruction Services	\$1,300,000
	Total Cost	\$147,387,115

[illegible]


PRIMAVERA P6 ANALYSIS

This Primavera P6 schedule report represents a fully developed baseline construction plan for a 224-day project (Mar 11, 2026 – Nov 26, 2026) with a total budget of approximately \$1.21M and actual cost of ~\$1.18M, integrating activity sequencing, WBS structuring across Preparation, Construction (Blocks A, B, C), and Final phases, and detailed resource and cost loading for labor, materials, and equipment; it includes activity-level durations, start/finish dates, and progress tracking with many activities reaching 100% completion, while the Gantt chart visualizes the project timeline, highlights critical path activities (zero float) driving completion, and compares baseline versus actual performance, enabling analysis of schedule adherence, cost control, and resource utilization, and demonstrating a comprehensive project controls approach incorporating scheduling, cost tracking, and performance monitoring aligned with industry best practices.

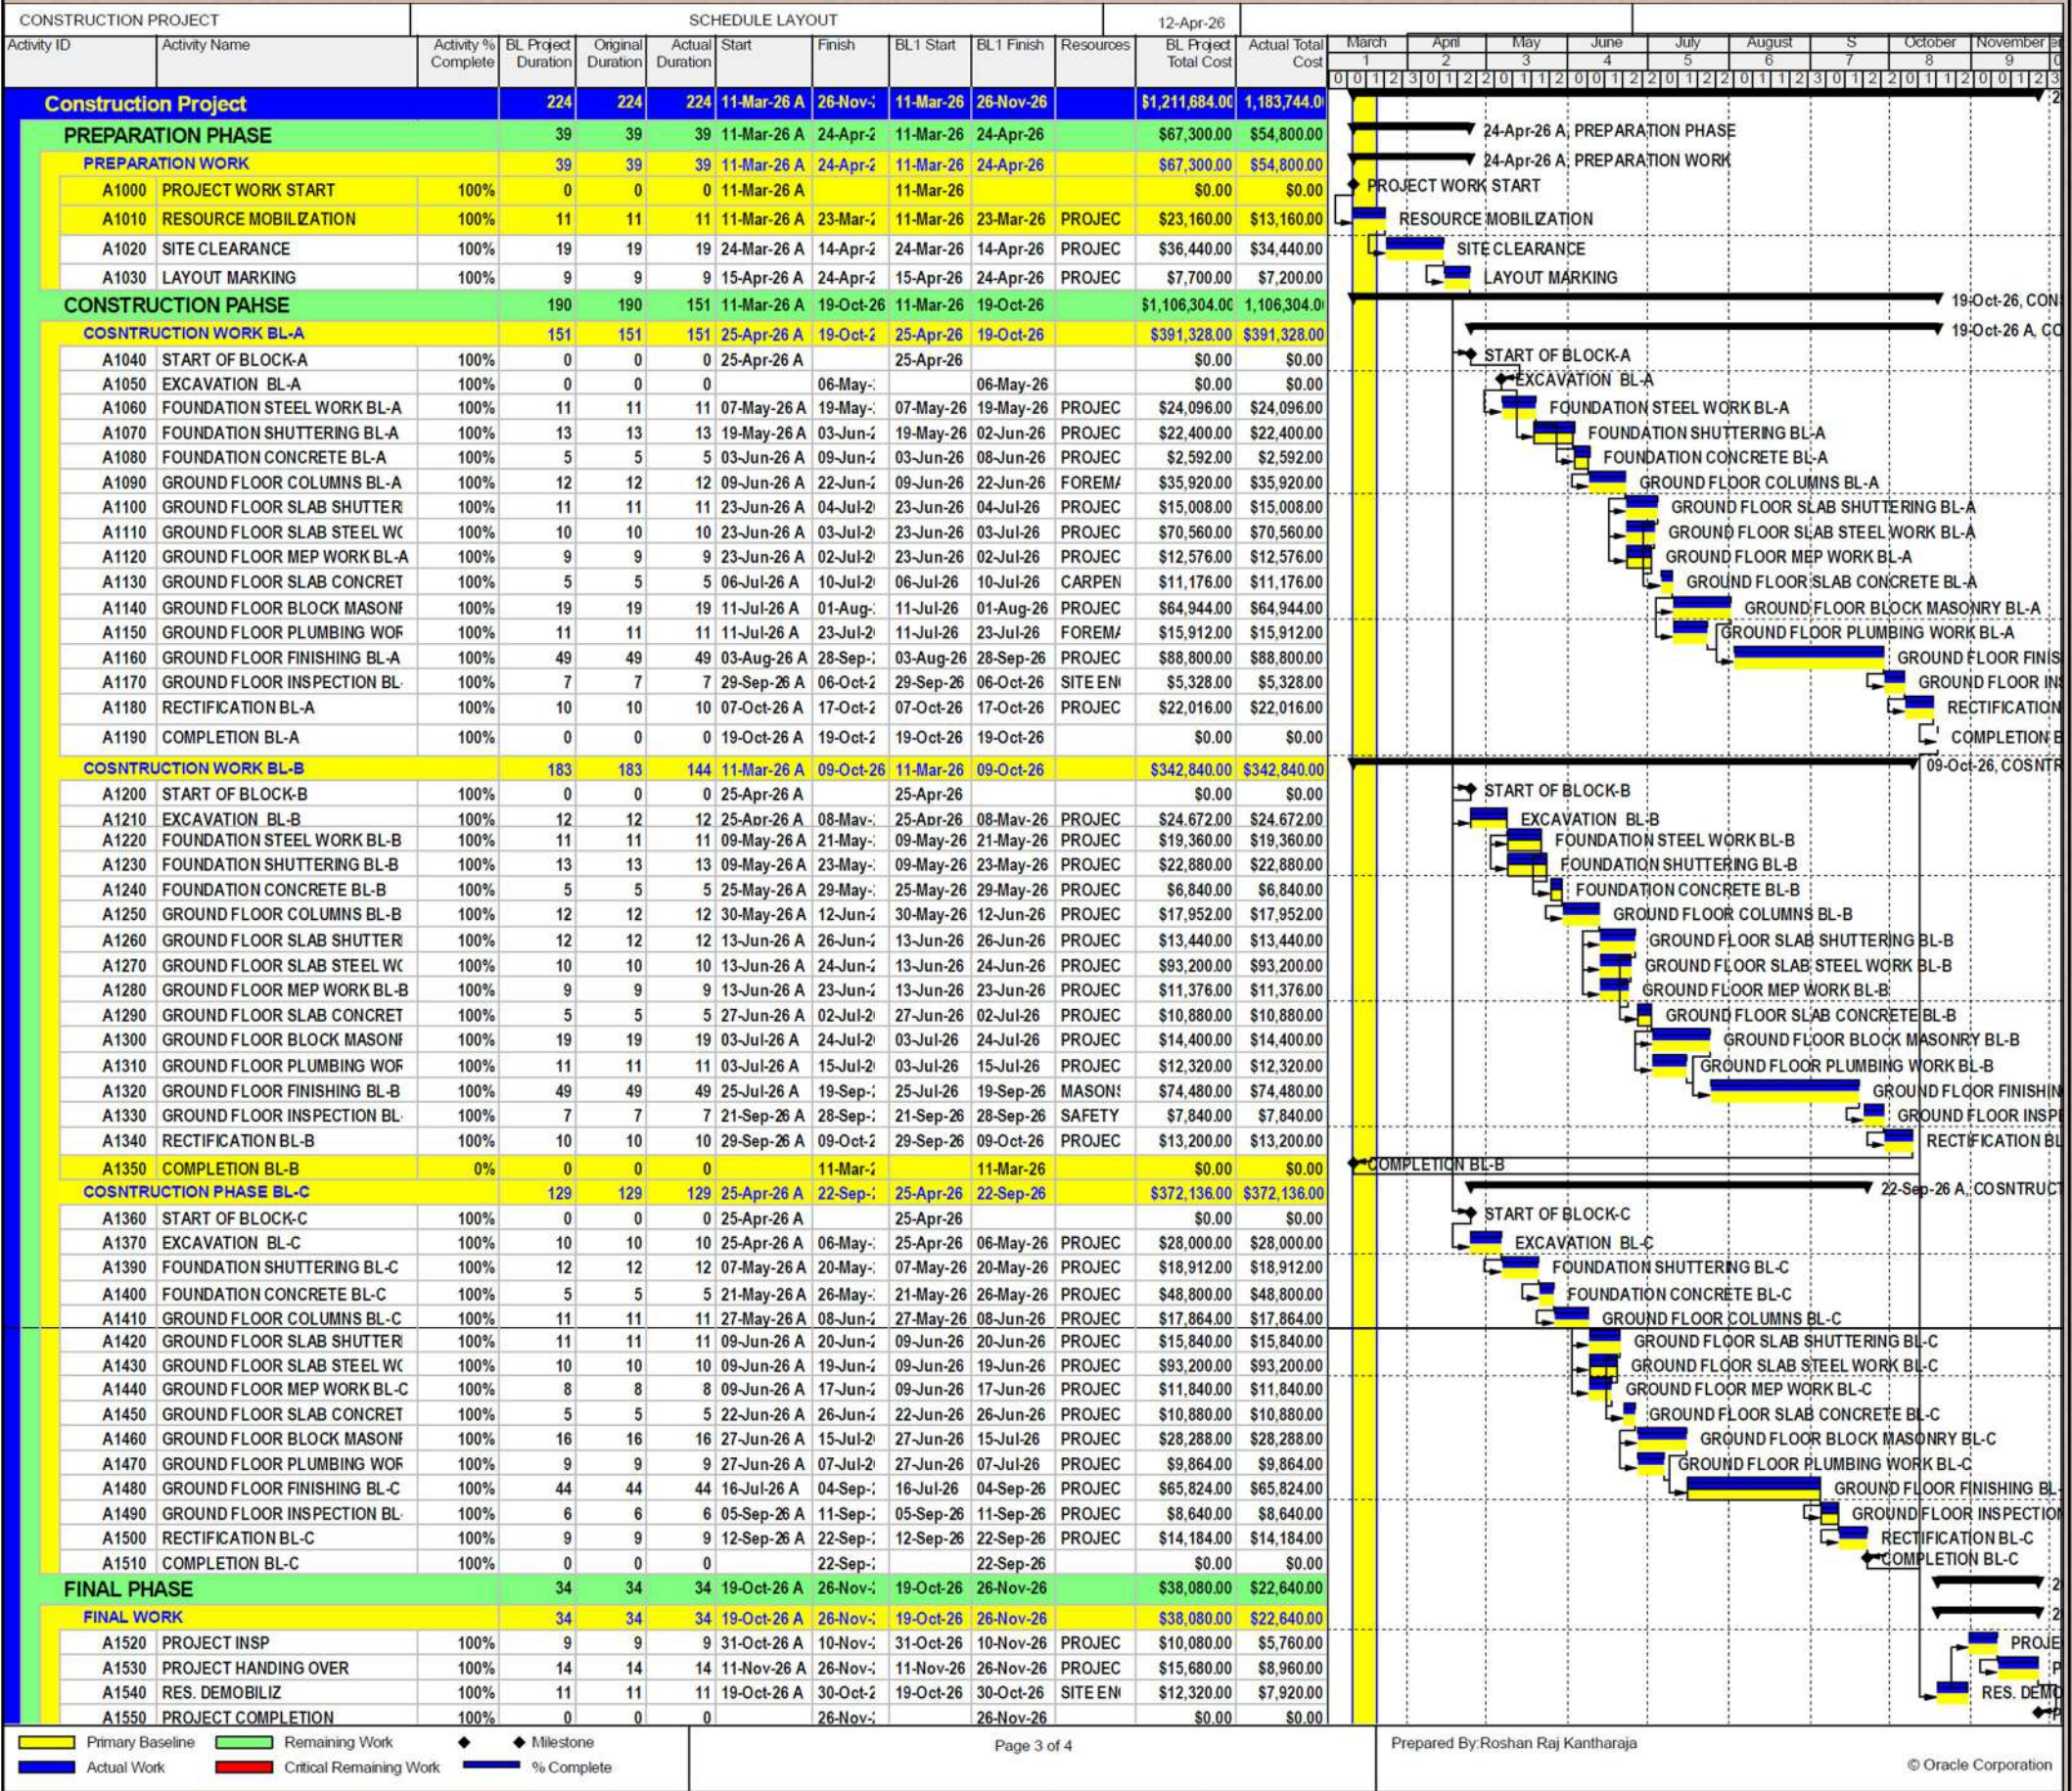


WORKLOAD ANALYSIS WITH COST TRACKING

This work load analysis report integrates activity sequencing with resource allocation and cost tracking, enabling evaluation of cost distribution, resource utilization, and execution efficiency across project phases.

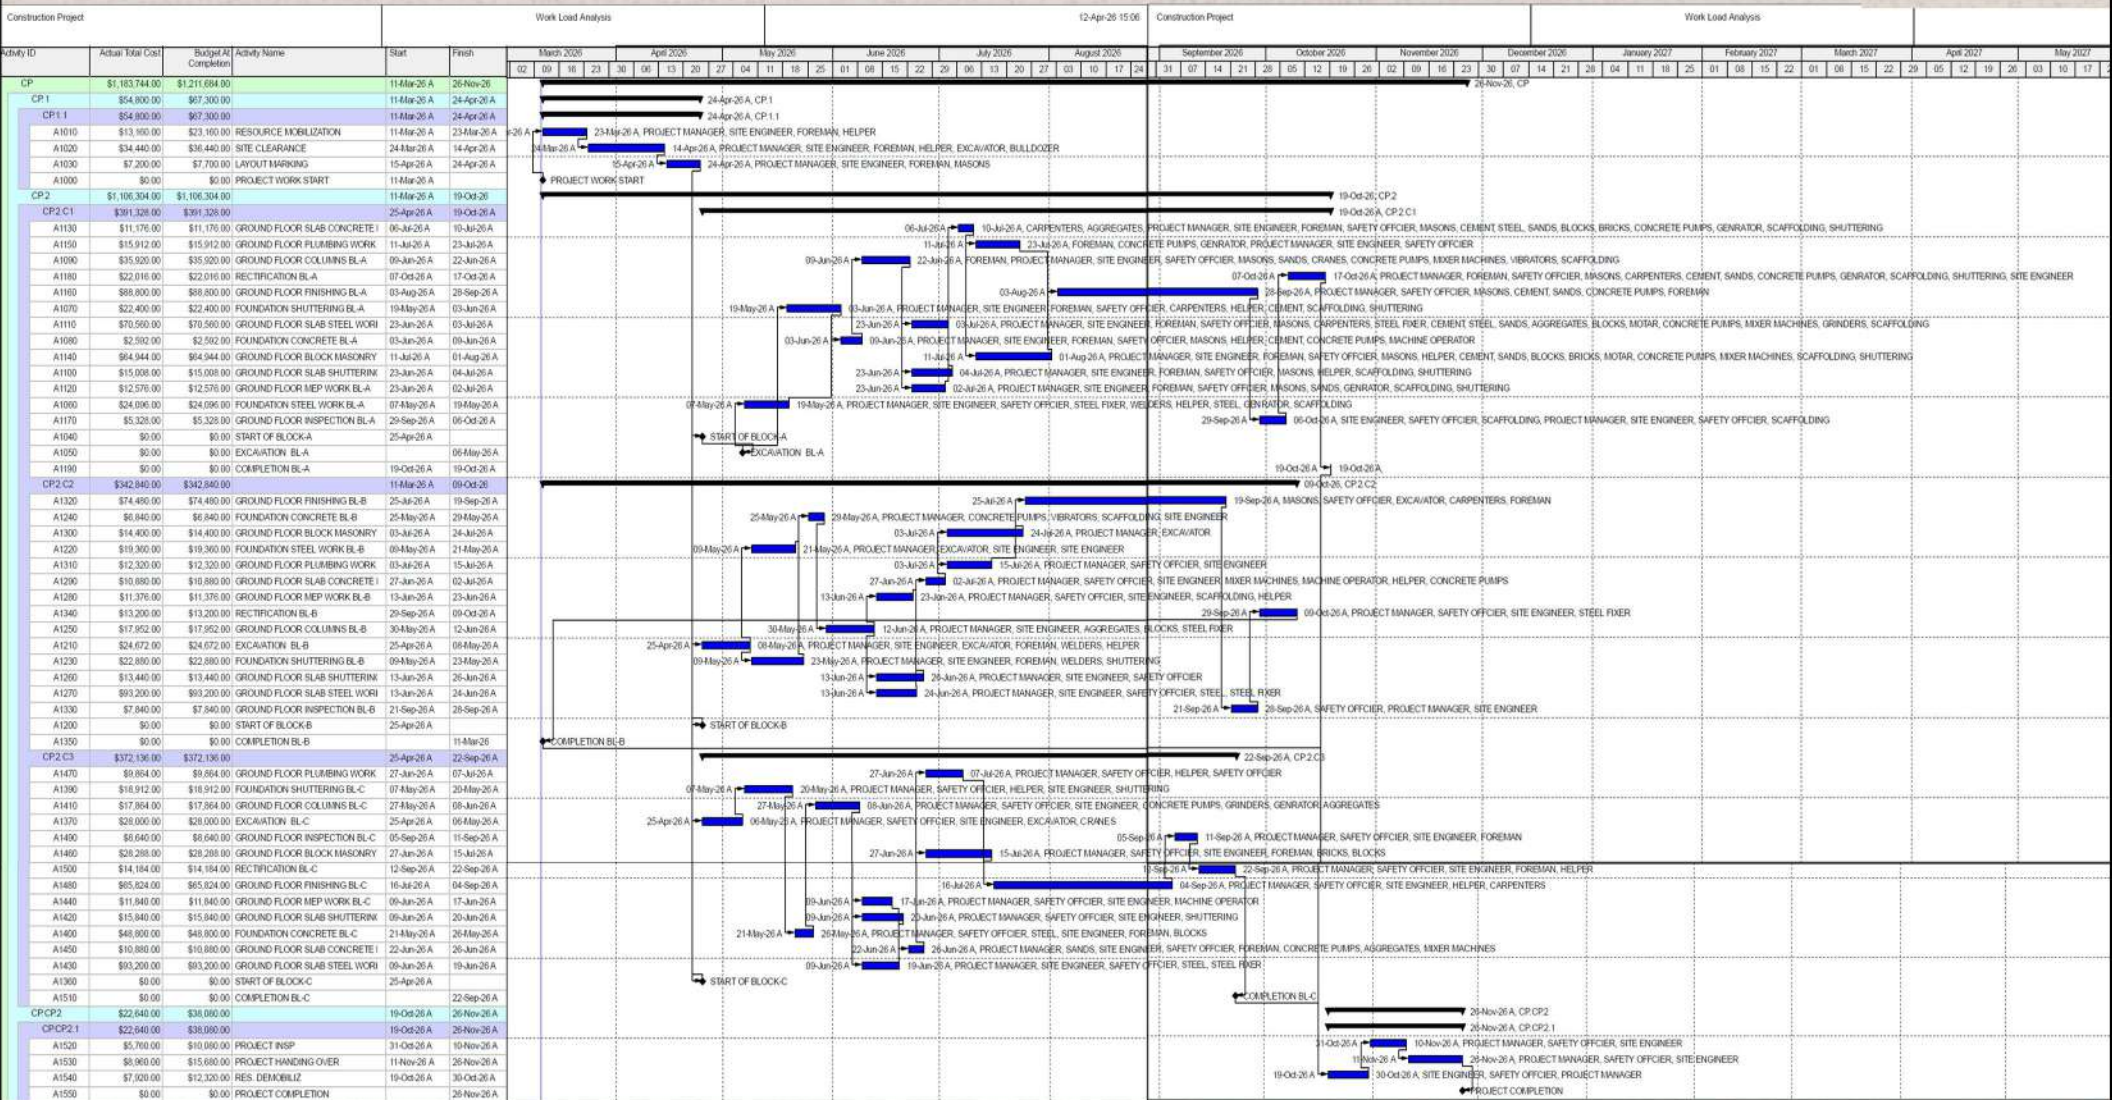

RESOURCE AND COST LOADING

This is a resource-loaded Primavera P6 schedule showing activity sequencing with time-phased labor and cost distribution, enabling analysis of workforce demand, cost allocation, and execution planning.

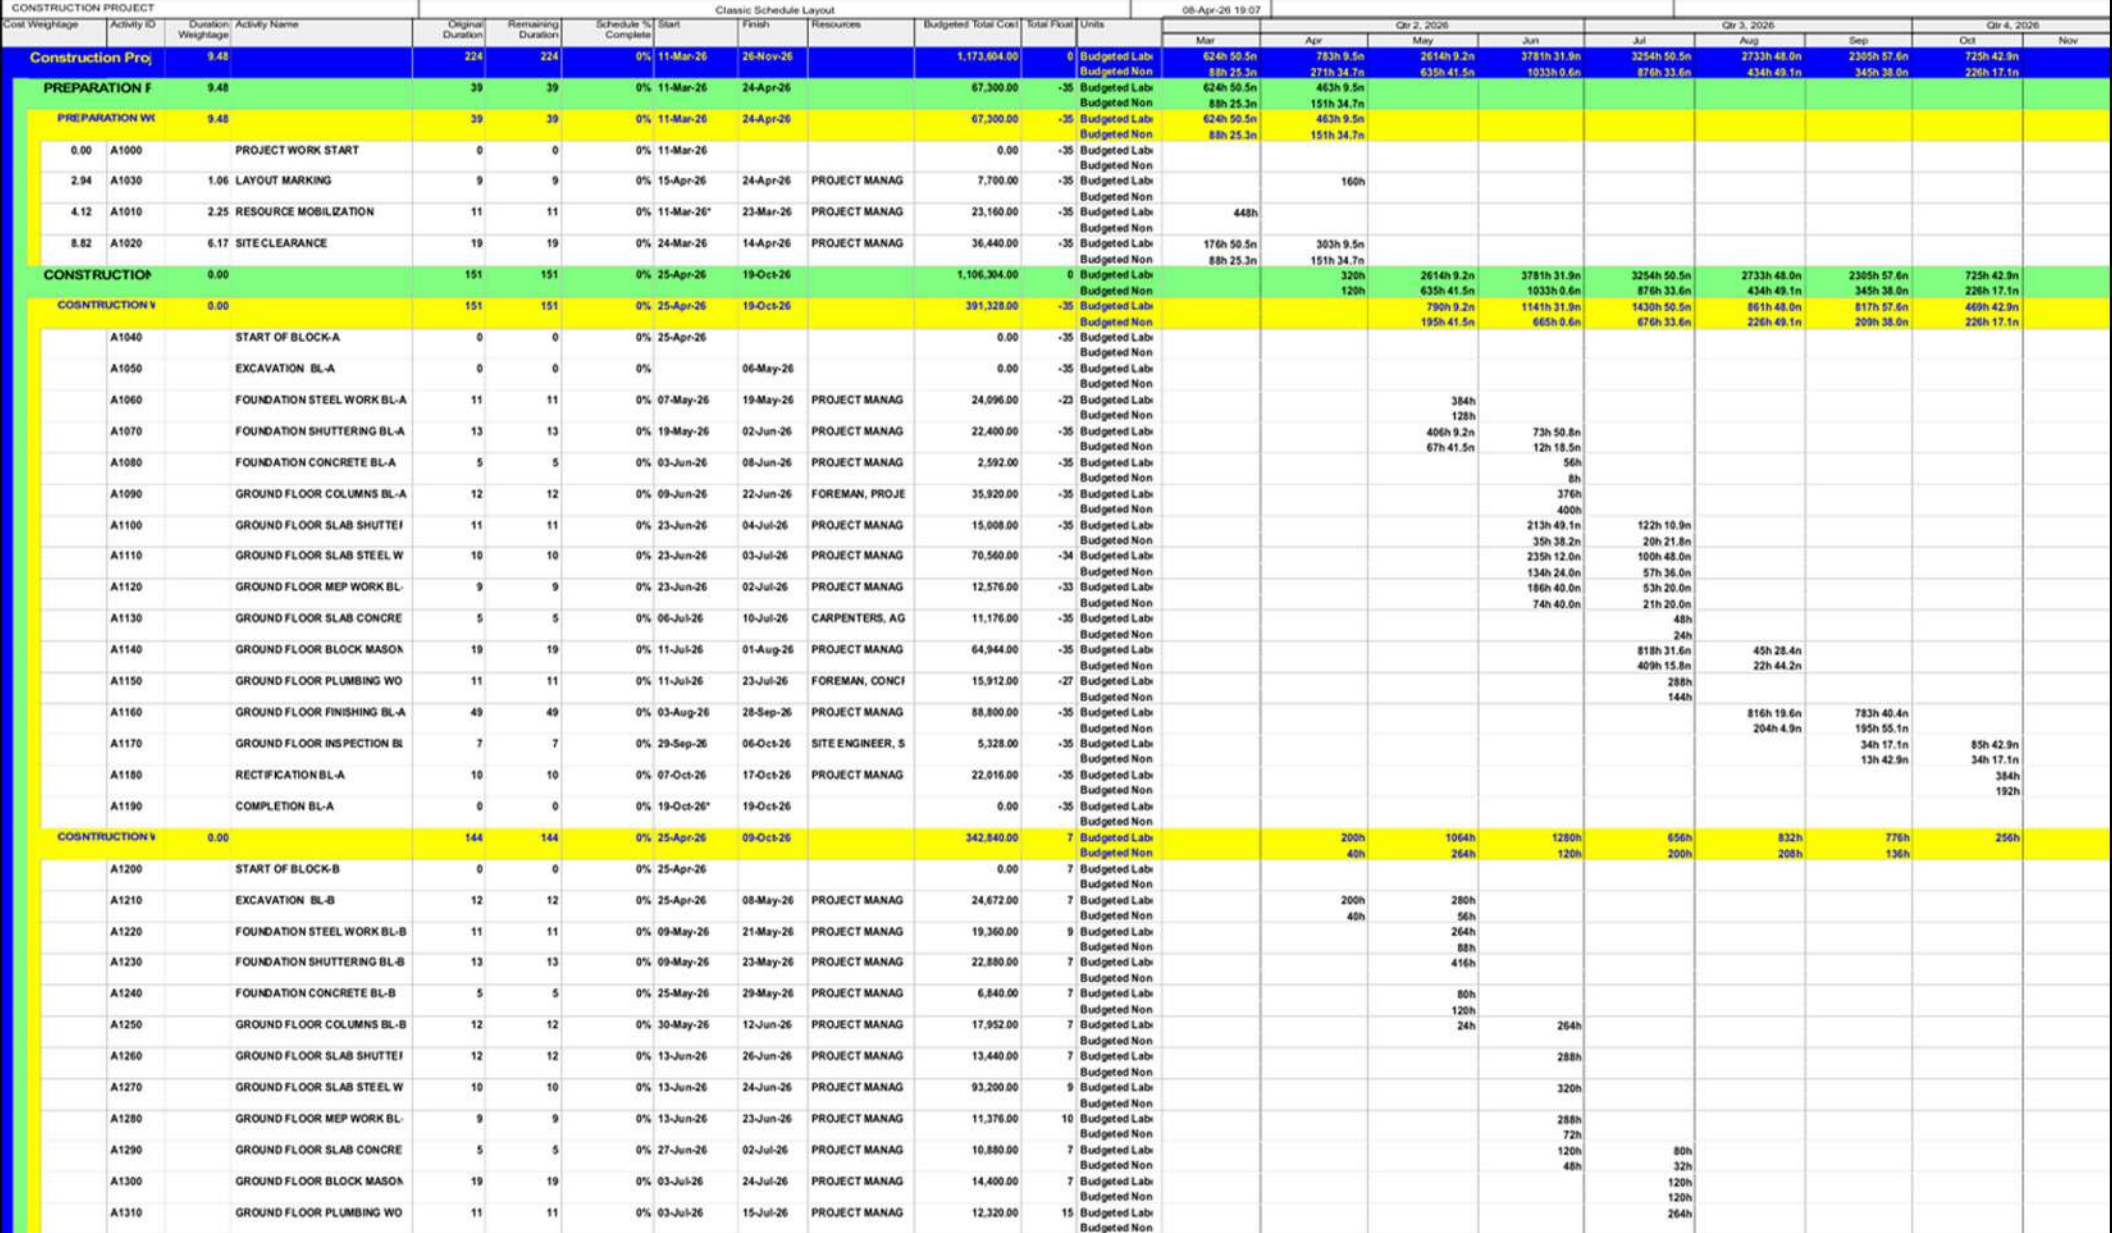

REPORTING AND CONTROLS

Labour-Based Resource & Cost Distribution

This report shows short-term resource assignments for upcoming activities, enabling effective workforce planning and execution readiness at the weekly level.

Construction Project
Report Date 11-Apr-26 00:04

Project Start 11-Mar-26
Project Finish 02-Oct-26

RA-02 Resource Assignments, Start This Week

User's Notes:

Resource Code	Resource Name	Project Code	WBS Code	Activity Code	Activity	Planned Units	Planned Duration	Planned Start	Planned Finish
PM PROJECT MANAGER									
Baseline	Baseline.1.1	A1030		LAYOUT MARKING		40.0	5	06-Apr-26	10-Apr-26
					Total	40.0			
SE SITE ENGINEER									
Baseline	Baseline.1.1	A1030		LAYOUT MARKING		40.0	5	06-Apr-26	10-Apr-26
					Total	40.0			
FM FOREMAN									
Baseline	Baseline.1.1	A1030		LAYOUT MARKING		40.0	5	06-Apr-26	10-Apr-26
					Total	40.0			
MSN MASONS									
Baseline	Baseline.1.1	A1030		LAYOUT MARKING		40.0	5	06-Apr-26	10-Apr-26
					Total	40.0			

Monthly Cost Report (Actual vs Budget Tracking)

This monthly cost report tracks actual vs budgeted cost over time, enabling analysis of cost distribution, peak spending periods, and overall budget performance.


Construction Project

Monthly Report

Activity ID	Activity Status	Cost 01-Mar-26 - 31-Oct-26	Mar 2026	Apr 2026	May 2026	Jun 2026	Jul 2026	Aug 2026	Sep 2026	Oct 2026	Period Total
A1420	Completed	Actual Total	15,840.00								15,840.00
		Budgeted Total				15,840.00					15,840.00
A1430	Completed	Actual Total	93,200.00								93,200.00
		Budgeted Total				93,200.00					93,200.00
A1440	Completed	Actual Total	11,840.00								11,840.00
		Budgeted Total				11,840.00					11,840.00
A1450	Completed	Actual Total	10,880.00								10,880.00
		Budgeted Total				10,880.00					10,880.00
A1460	Completed	Actual Total	28,288.00								28,288.00
		Budgeted Total				5,304.00	22,984.00				28,288.00
A1470	Completed	Actual Total	9,864.00								9,864.00
		Budgeted Total				3,288.00	6,576.00				9,864.00
A1480	Completed	Actual Total	65,824.00								65,824.00
		Budgeted Total					20,944.00	38,896.00	5,984.00		65,824.00
A1490	Completed	Actual Total	8,640.00								8,640.00
		Budgeted Total							8,640.00		8,640.00
A1500	Completed	Actual Total	14,184.00								14,184.00
		Budgeted Total							14,184.00		14,184.00
A1510	Completed	Actual Total									0.00
		Budgeted Total									0.00
A1520	Completed	Actual Total	5,760.00								5,760.00
		Budgeted Total								1,120.00	1,120.00
A1530	Completed	Actual Total	8,960.00								8,960.00
		Budgeted Total									0.00
A1540	Completed	Actual Total	7,920.00								7,920.00
		Budgeted Total								12,320.00	12,320.00
A1550	Completed	Actual Total									0.00
		Budgeted Total									0.00
Total		Actual Total	1,183,744.00								1,183,744.00
		Budgeted Total	36,585.26	54,894.74	196,225.95	403,402.83	206,736.02	127,140.23	110,144.16	49,821.71	1,187,044.00

RESOURCE USAGE & LABOR CURVES

Time-phased resource usage and cumulative labor curves were used to analyze workforce demand, identify peak resource periods, and optimize manpower planning.

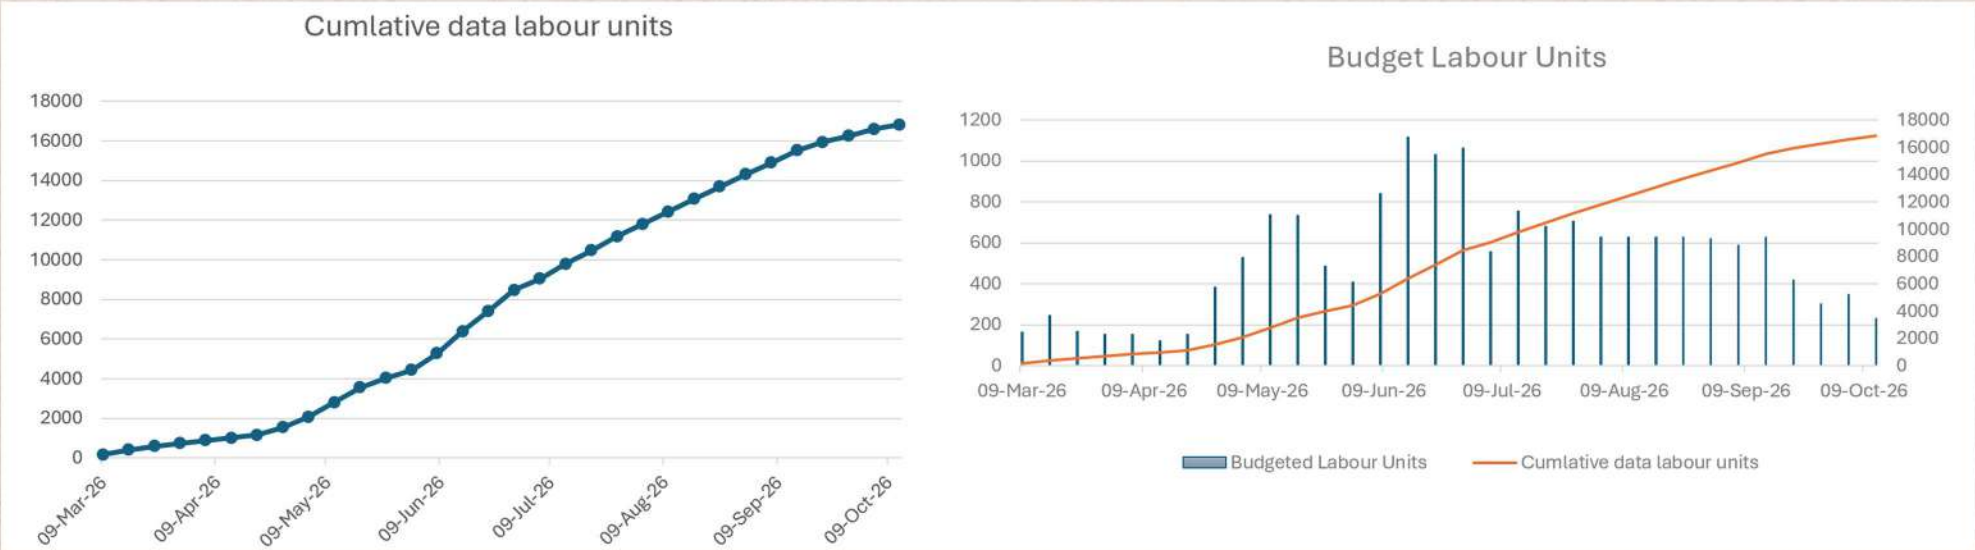

PERFORMANCE / RESOURCE CONTROL

This chart compares planned versus actual labor utilization, highlighting significant over-allocation and indicating inefficiencies in resource management during peak construction phases.



Labor Performance Analysis


RISK REPORT

This report identifies and tracks project risks, including their impact, causes, timelines, and responsible owners to support proactive risk management.

Risks											
Risk ID	Risk Name	Risk Category	Risk Type	Risk Status	Risk Owner	Identified By	Identified On	Exposure Start	Exposure Finish	Project	Cause
R001	Design and Approval delays	Schedule	Threat	Open	PM/PROJECT MANAGER	PM/PROJECT MANAGER	01-Jan-26	24-Mar-26	14-Apr-26	CP	Delays in design approvals or changes in the project scope can disrupt critical path activities, leading to missed deadlines and project delays. Such delays typically arise from the complexity of design requirements, prolonged regulatory approval processes, or last-minute changes in project scope.
	Activity: SITE CLEARANCE	Risk: Design and Approval delays	Project: CP								
R002	Materials Shortages or Price Fluctuations	Supplier	Threat	Open	PM/PROJECT MANAGER	PM/PROJECT MANAGER	25-Jan-26	07-May-26	09-Jun-26	CP	Material shortages or unexpected price fluctuations can disrupt construction schedules and significantly increase project costs. These risks typically arise from supply chain issues, unexpected market conditions, or unforeseen demand spikes for critical materials.
	Activity: FOUNDATION STEEL WORK B/LA	Risk: Materials Shortages or Price Fluctuations	Project: CP								
	Activity: FOUNDATION CONCRETE B/LA	Risk: Materials Shortages or Price Fluctuations	Project: CP								
R003	Unexpected Site Conditions	Weather/Environment Hazards	Threat	Proposed	PM/PROJECT MANAGER	PM/PROJECT MANAGER	01-Jan-26	25-Apr-26	08-May-26	CP	Unforeseen conditions, such as poor soil quality, underground utilities, or contamination, may require additional work or redesign. This can delay construction, lead to budget increases, and disrupt the project's timeline.
	Activity: EXCAVATION B/LA	Risk: Unexpected Site Conditions	Project: CP								
	Activity: EXCAVATION B/LB	Risk: Unexpected Site Conditions	Project: CP								
	Activity: EXCAVATION B/LC	Risk: Unexpected Site Conditions	Project: CP								


Earned Value / Cost Control

This S-curve compares baseline and actual cost distribution, showing peak expenditure during core construction and demonstrating effective cost control with close alignment between planned and actual values

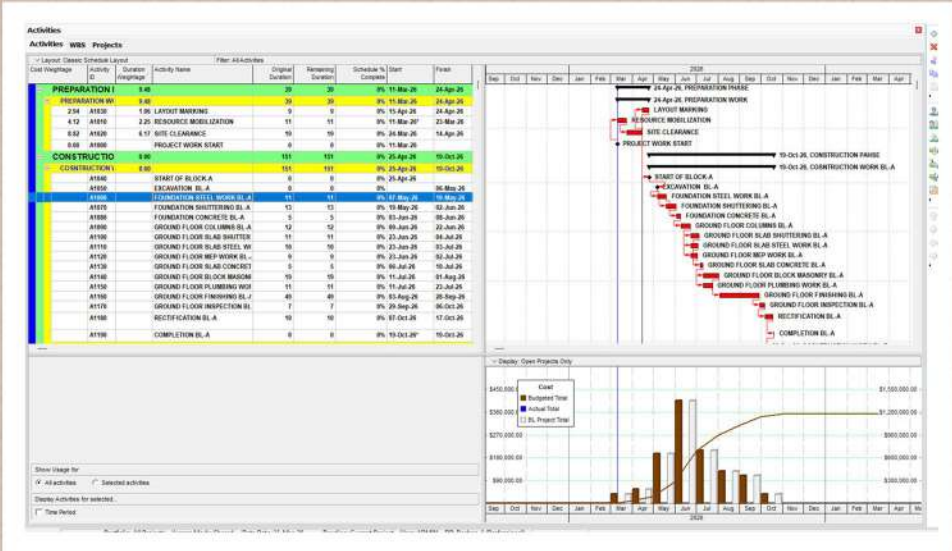

Cost S-Curve

The project shows early cost overrun and inefficient spending, with actual costs exceeding planned values, indicating a need for tighter cost control and resource optimization.

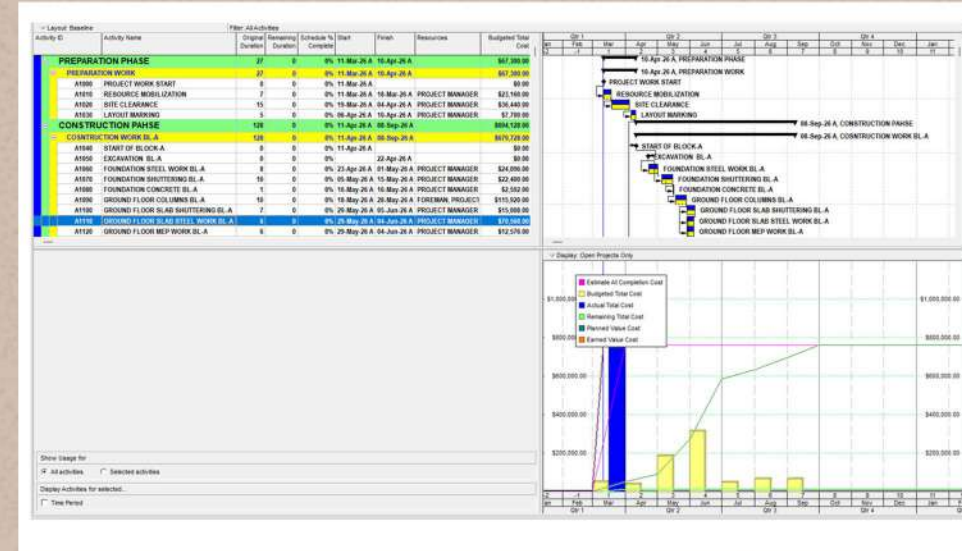

Resource & Cost Loading (Primary), Earned Value / Cost

This earned value dashboard in Primavera P6 presents key performance metrics, including CPI (~0.93-1.00) and SPI (~0.59-1.00), along with cost & schedule variances at the WBS level, enabling evaluation of project performance where values below 1 indicate cost overruns and schedule delays, helping identify deviations from the baseline and support timely corrective actions.

EVM Dashboard (WBS-Level Performance Analysis)											
Layout Name	Earned Value										
Planned Value	Budget At Completion	Estimate To Complete	Estimate At Completion	Variance At Completion	Cost Variance	Schedule Variance	Cost Performance Index	Schedule Performance Index	Cost Variance	Schedule Variance	Index
\$602,940.00	\$1,005,580.00	\$491,640.00	\$1,019,340.00	(\$13,760.00)	(\$13,760.00)	(\$85,000.00)	0.97	0.85	-0.03	-0.15	
\$95,300.00	\$95,300.00	\$0.00	\$102,720.00	(\$7,420.00)	(\$7,420.00)	\$0.00	0.93	1.00	-0.08	0.00	
\$95,300.00	\$95,300.00	\$0.00	\$102,720.00	(\$7,420.00)	(\$7,420.00)	\$0.00	0.93	1.00	-0.08	0.00	
\$507,640.00	\$881,240.00	\$462,600.00	\$887,580.00	(\$6,340.00)	(\$6,340.00)	(\$89,000.00)	0.99	0.82	-0.02	-0.18	
\$420,880.00	\$572,720.00	\$213,120.00	\$575,380.00	(\$2,660.00)	(\$2,660.00)	(\$61,280.00)	0.99	0.85	-0.01	-0.15	
\$41,880.00	\$153,320.00	\$130,680.00	\$167,000.00	(\$3,680.00)	(\$3,680.00)	(\$9,240.00)	0.90	0.78	-0.11	-0.22	
\$44,880.00	\$145,200.00	\$110,300.00	\$145,200.00	\$0.00	\$0.00	(\$18,480.00)	1.00	0.59	0.00	-0.41	
\$0.00	\$29,040.00	\$29,040.00	\$29,040.00	\$0.00	\$0.00	\$0.00	0.00	0.00	0.00	0.00	
\$0.00	\$29,040.00	\$29,040.00	\$29,040.00	\$0.00	\$0.00	\$0.00	0.00	0.00	0.00	0.00	

EVM Dashboard (WBS-Level Performance Analysis)

The EVM analysis shows that Actual Cost exceeds Earned Value and Earned Value is lower than Planned Value, indicating the project is over budget and behind schedule. The Cost Performance Index (CPI ≈ 0.79) confirms cost inefficiency, while the Schedule Performance Index (SPI ≈ 0.70) indicates delayed progress. Additionally, both Cost Variance (CV) and Schedule Variance (SV) are negative, highlighting performance issues and the need for corrective actions



Resource & Cost Loading (Primary), Earned Value / Cost

PRIMAVERA P6 SCHEDULE CHECK REPORT

The schedule health check report demonstrates a well-structured and logically connected schedule, with no missing predecessor/successor relationships, indicating strong network integrity. The Baseline Execution Index (BEI = 1.00) confirms that activities are progressing in alignment with the baseline plan, reflecting effective schedule tracking and control. The absence of negative lags, hard constraints, and excessive float further highlights good scheduling practices and compliance with industry standards. Overall, the schedule shows high reliability, strong baseline adherence, and a solid foundation for performance monitoring and decision-making, with minor areas identified for refinement in progress data management.

4/12/26, 11:03 PM

Check Schedule Report

Check Schedule Report

12-Apr-26

PM.EXE

▼ Projects Checked

Project ID	Project Name	Data Date	Total Activities	Complete Activities	Internal Relationships	External Relationships
CP-2	Construction Project	11-Mar-26	55	54	67	0

▼ Project checked to have links to the following closed projects

Closed Project ID	Closed Project Name	Data Date	Links to/from the closed project
-------------------	---------------------	-----------	----------------------------------

▼ Check Summary

Check	Description	Target	Percent	Found	Total
Logic	Activities missing predecessors or successors	< 5.00 %	0.00 %	0	1
Negative Lags	Relationships with a lag duration of less than 0	< 1.00 %	0.00 %	0	2
Positive Lags	Relationships with a positive lag duration	< 5.00 %	0.00 %	0	2
Long Lags	Relationships with a lag duration greater than 352 hours	< 5.00 %	0.00 %	0	2
Relationship Type	The majority of relationships should be Finish to Start	> 90.00 %	50.00 %	1	2
Hard Constraints	Constraints that prevent activities being moved	< 1.00 %	0.00 %	0	1
Soft Constraints	Constraints that do not prevent activities being moved	< 5.00 %	0.00 %	0	1
Large Float	Activities with total float greater than 352 hours	< 1.00 %	0.00 %	0	1
Negative Float	Activities with a total float less than 0	< 1.00 %	0.00 %	0	1
Large Durations	Activities that have a remaining duration greater than 352 hours	< 5.00 %	N/A	0	0
Invalid Progress Before Data Date	Incomplete activities before the data date	< 1.00 %	0.00 %	0	55
Invalid Progress After Data Date	Activities with actual dates after the data date	< 1.00 %	98.18 %	54	55
Resources/Cost	Activities that do not have an expense or a resource assigned	< 1.00 %	2.13 %	1	47
Late Activities	Activities scheduled to finish later than the project baseline	< 5.00 %	N/A	0	0
Out of Sequence	Activities which are completed or in-progress before their predecessors.	< 2.00 %	1.82 %	1	55

Check	Description	Target	BEI Ratio	Project Activities	Baseline Activities
BEI	Baseline Execution Index	> 0.95	1.00	47	47

▼ Logic

Activities missing predecessors or successors

Project ID	Activity ID	Activity Name	Predecessor	Successor
------------	-------------	---------------	-------------	-----------

▼ Negative Lags

Relationships with a lag duration of less than 0

Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type	Lag Duration (hours)	Successor Project ID	Successor Activity ID	Successor Activity Name
------------------------	-------------------------	---------------------------	-------------------	----------------------	----------------------	-----------------------	-------------------------

▼ Positive Lags

Relationships with a positive lag duration

Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type	Lag Duration (hours)	Successor Project ID	Successor Activity ID	Successor Activity Name
------------------------	-------------------------	---------------------------	-------------------	----------------------	----------------------	-----------------------	-------------------------

▼ Long Lags

Relationships with a lag duration greater than 352 hours

Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type	Lag Duration (hours)	Successor Project ID	Successor Activity ID	Successor Activity Name
------------------------	-------------------------	---------------------------	-------------------	----------------------	----------------------	-----------------------	-------------------------

▼ Relationship Type

The majority of relationships should be Finish to Start

Relationship Type	Count	Percent
FS	1	50.00 %
FF	1	50.00 %
SS	0	0.00 %
SF	0	0.00 %

Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type	Lag Duration (hours)	Successor Project ID	Successor Activity ID	Successor Activity Name
CP-2	A1340	RECTIFICATION BL-B	FF	0.00	CP-2	A1350	COMPLETION BL-B

▼ Hard Constraints

Constraints that prevent activities being moved

Project ID	Activity ID	Activity Name	Primary Constraint	Primary Constraint Date	Secondary Constraint	Secondary Constraint Date
------------	-------------	---------------	--------------------	-------------------------	----------------------	---------------------------

▼ Soft Constraints

Constraints that do not prevent activities being moved

Project ID	Activity ID	Activity Name	Primary Constraint	Primary Constraint Date	Secondary Constraint	Secondary Constraint Date
------------	-------------	---------------	--------------------	-------------------------	----------------------	---------------------------

▼ Large Float

Activities with total float greater than 352 hours

Project ID	Activity ID	Activity Name	Total Float (hour)
------------	-------------	---------------	--------------------

▼ Negative Float

Activities with a total float less than 0

Project ID	Activity ID	Activity Name	Total Float (hour)
------------	-------------	---------------	--------------------

▼ Large Durations

Activities that have a remaining duration greater than 352 hours

Project ID	Activity ID	Activity Name	Remaining Duration (hour)
------------	-------------	---------------	---------------------------

▼ Invalid Progress Before Data Date

Incomplete activities before the data date

Project ID	Activity ID	Activity Name	Data Date	Start	Finish	Remaining Early Start	Remaining Early Finish
------------	-------------	---------------	-----------	-------	--------	-----------------------	------------------------

▼ Invalid Progress After Data Date

Activities with actual dates after the data date

Project ID	Activity ID	Activity Name	Data Date	Actual Start	Actual Finish
CP-2	A1000	PROJECT WORK START	11-Mar-26	11-Mar-26	11-Mar-26
CP-2	A1010	RESOURCE MOBILIZATION	11-Mar-26	11-Mar-26	23-Mar-26
CP-2	A1020	SITE CLEARANCE	11-Mar-26	24-Mar-26	14-Apr-26
CP-2	A1030	LAYOUT MARKING	11-Mar-26	15-Apr-26	24-Apr-26
CP-2	A1040	START OF BLOCK-A	11-Mar-26	25-Apr-26	25-Apr-26
CP-2	A1050	EXCAVATION BL-A	11-Mar-26	06-May-26	06-May-26
CP-2	A1060	FOUNDATION STEEL WORK BL-A	11-Mar-26	07-May-26	19-May-26
CP-2	A1070	FOUNDATION SHUTTERING BL-A	11-Mar-26	19-May-26	02-Jun-26
CP-2	A1080	FOUNDATION CONCRETE BL-A	11-Mar-26	03-Jun-26	08-Jun-26
CP-2	A1090	GROUND FLOOR COLUMNS BL-A	11-Mar-26	09-Jun-26	22-Jun-26
CP-2	A1100	GROUND FLOOR SLAB SHUTTERING BL-A	11-Mar-26	23-Jun-26	04-Jul-26
CP-2	A1110	GROUND FLOOR SLAB STEEL WORK BL-A	11-Mar-26	23-Jun-26	03-Jul-26
CP-2	A1120	GROUND FLOOR MEP WORK BL-A	11-Mar-26	23-Jun-26	02-Jul-26
CP-2	A1130	GROUND FLOOR SLAB CONCRETE BL-A	11-Mar-26	06-Jul-26	10-Jul-26
CP-2	A1140	GROUND FLOOR BLOCK MASONRY BL-A	11-Mar-26	11-Jul-26	01-Aug-26
CP-2	A1150	GROUND FLOOR PLUMBING WORK BL-A	11-Mar-26	11-Jul-26	23-Jul-26
CP-2	A1160	GROUND FLOOR FINISHING BL-A	11-Mar-26	03-Aug-26	28-Sep-26
CP-2	A1170	GROUND FLOOR INSPECTION BL-A	11-Mar-26	29-Sep-26	06-Oct-26
CP-2	A1180	RECTIFICATION BL-A	11-Mar-26	07-Oct-26	17-Oct-26
CP-2	A1190	COMPLETION BL-A	11-Mar-26	19-Oct-26	19-Oct-26
CP-2	A1200	START OF BLOCK-B	11-Mar-26	25-Apr-26	25-Apr-26
CP-2	A1210	EXCAVATION BL-B	11-Mar-26	25-Apr-26	08-May-26
CP-2	A1220	FOUNDATION STEEL WORK BL-B	11-Mar-26	09-May-26	21-May-26
CP-2	A1230	FOUNDATION SHUTTERING BL-B	11-Mar-26	09-May-26	23-May-26
CP-2	A1240	FOUNDATION CONCRETE BL-B	11-Mar-26	25-May-26	29-May-26
CP-2	A1250	GROUND FLOOR COLUMNS BL-B	11-Mar-26	30-May-26	12-Jun-26
CP-2	A1260	GROUND FLOOR SLAB SHUTTERING BL-B	11-Mar-26	13-Jun-26	26-Jun-26
CP-2	A1270	GROUND FLOOR SLAB STEEL WORK BL-B	11-Mar-26	13-Jun-26	24-Jun-26
CP-2	A1280	GROUND FLOOR MEP WORK BL-B	11-Mar-26	13-Jun-26	23-Jun-26
CP-2	A1290	GROUND FLOOR SLAB CONCRETE BL-B	11-Mar-26	27-Jun-26	02-Jul-26
CP-2	A1300	GROUND FLOOR BLOCK MASONRY BL-B	11-Mar-26	03-Jul-26	24-Jul-26
CP-2	A1310	GROUND FLOOR PLUMBING WORK BL-B	11-Mar-26	03-Jul-26	15-Jul-26
CP-2	A1320	GROUND FLOOR FINISHING BL-B	11-Mar-26	25-Jul-26	19-Sep-26
CP-2	A1330	GROUND FLOOR INSPECTION BL-B	11-Mar-26	21-Sep-26	28-Sep-26
CP-2	A1340	RECTIFICATION BL-B	11-Mar-26	29-Sep-26	09-Oct-26
CP-2	A1360	START OF BLOCK-C	11-Mar-26	25-Apr-26	25-Apr-26
CP-2	A1370	EXCAVATION BL-C	11-Mar-26	25-Apr-26	06-May-26
CP-2	A1390	FOUNDATION SHUTTERING BL-C	11-Mar-26	07-May-26	20-May-26
CP-2	A1400	FOUNDATION CONCRETE BL-C	11-Mar-26	21-May-26	26-May-26
CP-2	A1410	GROUND FLOOR COLUMNS BL-C	11-Mar-26	27-May-26	08-Jun-26
CP-2	A1420	GROUND FLOOR SLAB SHUTTERING BL-C	11-Mar-26	09-Jun-26	20-Jun-26
CP-2	A1430	GROUND FLOOR SLAB STEEL WORK BL-C	11-Mar-26	09-Jun-26	19-Jun-26
CP-2	A1440	GROUND FLOOR MEP WORK BL-C	11-Mar-26	09-Jun-26	17-Jun-26
CP-2	A1450	GROUND FLOOR SLAB CONCRETE BL-C	11-Mar-26	22-Jun-26	26-Jun-26
CP-2	A1460	GROUND FLOOR BLOCK MASONRY BL-C	11-Mar-26	27-Jun-26	15-Jul-26
CP-2	A1470	GROUND FLOOR PLUMBING WORK BL-C	11-Mar-26	27-Jun-26	07-Jul-26
CP-2	A1480	GROUND FLOOR FINISHING BL-C	11-Mar-26	16-Jul-26	04-Sep-26
CP-2	A1490	GROUND FLOOR INSPECTION BL-C	11-Mar-26	05-Sep-26	11-Sep-26
CP-2	A1500	RECTIFICATION BL-C	11-Mar-26	12-Sep-26	22-Sep-26
CP-2	A1510	COMPLETION BL-C	11-Mar-26	22-Sep-26	22-Sep-26
CP-2	A1520	PROJECT INSP	11-Mar-26	31-Oct-26	10-Nov-26
CP-2	A1530	PROJECT HANDING OVER	11-Mar-26	11-Nov-26	26-Nov-26
CP-2	A1540	RES. DEMOBILIZ	11-Mar-26	19-Oct-26	30-Oct-26
CP-2	A1550	PROJECT COMPLETION	11-Mar-26	26-Nov-26	26-Nov-26

▼ Resources/Cost

Activities that do not have an expense or a resource assigned

Project ID	Activity ID	Activity Name
CP-2	A1190	COMPLETION BL-A

▼ Late Activities

Activities scheduled to finish later than the project baseline

Project ID	Activity ID	Activity Name	Finish Variance (hour)
------------	-------------	---------------	------------------------

▼ Baseline

Activities missing in assigned baseline

Project ID	Activity ID	Activity Name
------------	-------------	---------------

▼ Links to Closed Projects

Activities with links to closed projects. *= Closed Project

Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type	Lag Duration (hours)	Successor Project ID	Successor Activity ID	Successor Activity Name
------------------------	-------------------------	---------------------------	-------------------	----------------------	----------------------	-----------------------	-------------------------


▼ Out of Sequence

Activities which are completed or in-progress before their predecessors.

Project ID	Activity ID	Activity Name	Predecessor Project ID	Predecessor Activity ID	Predecessor Activity Name	Relationship Type
CP-2	A1540	RES. DEMOBILIZ	CP-2	A1350	COMPLETION BL-B	FS



-THESIS-

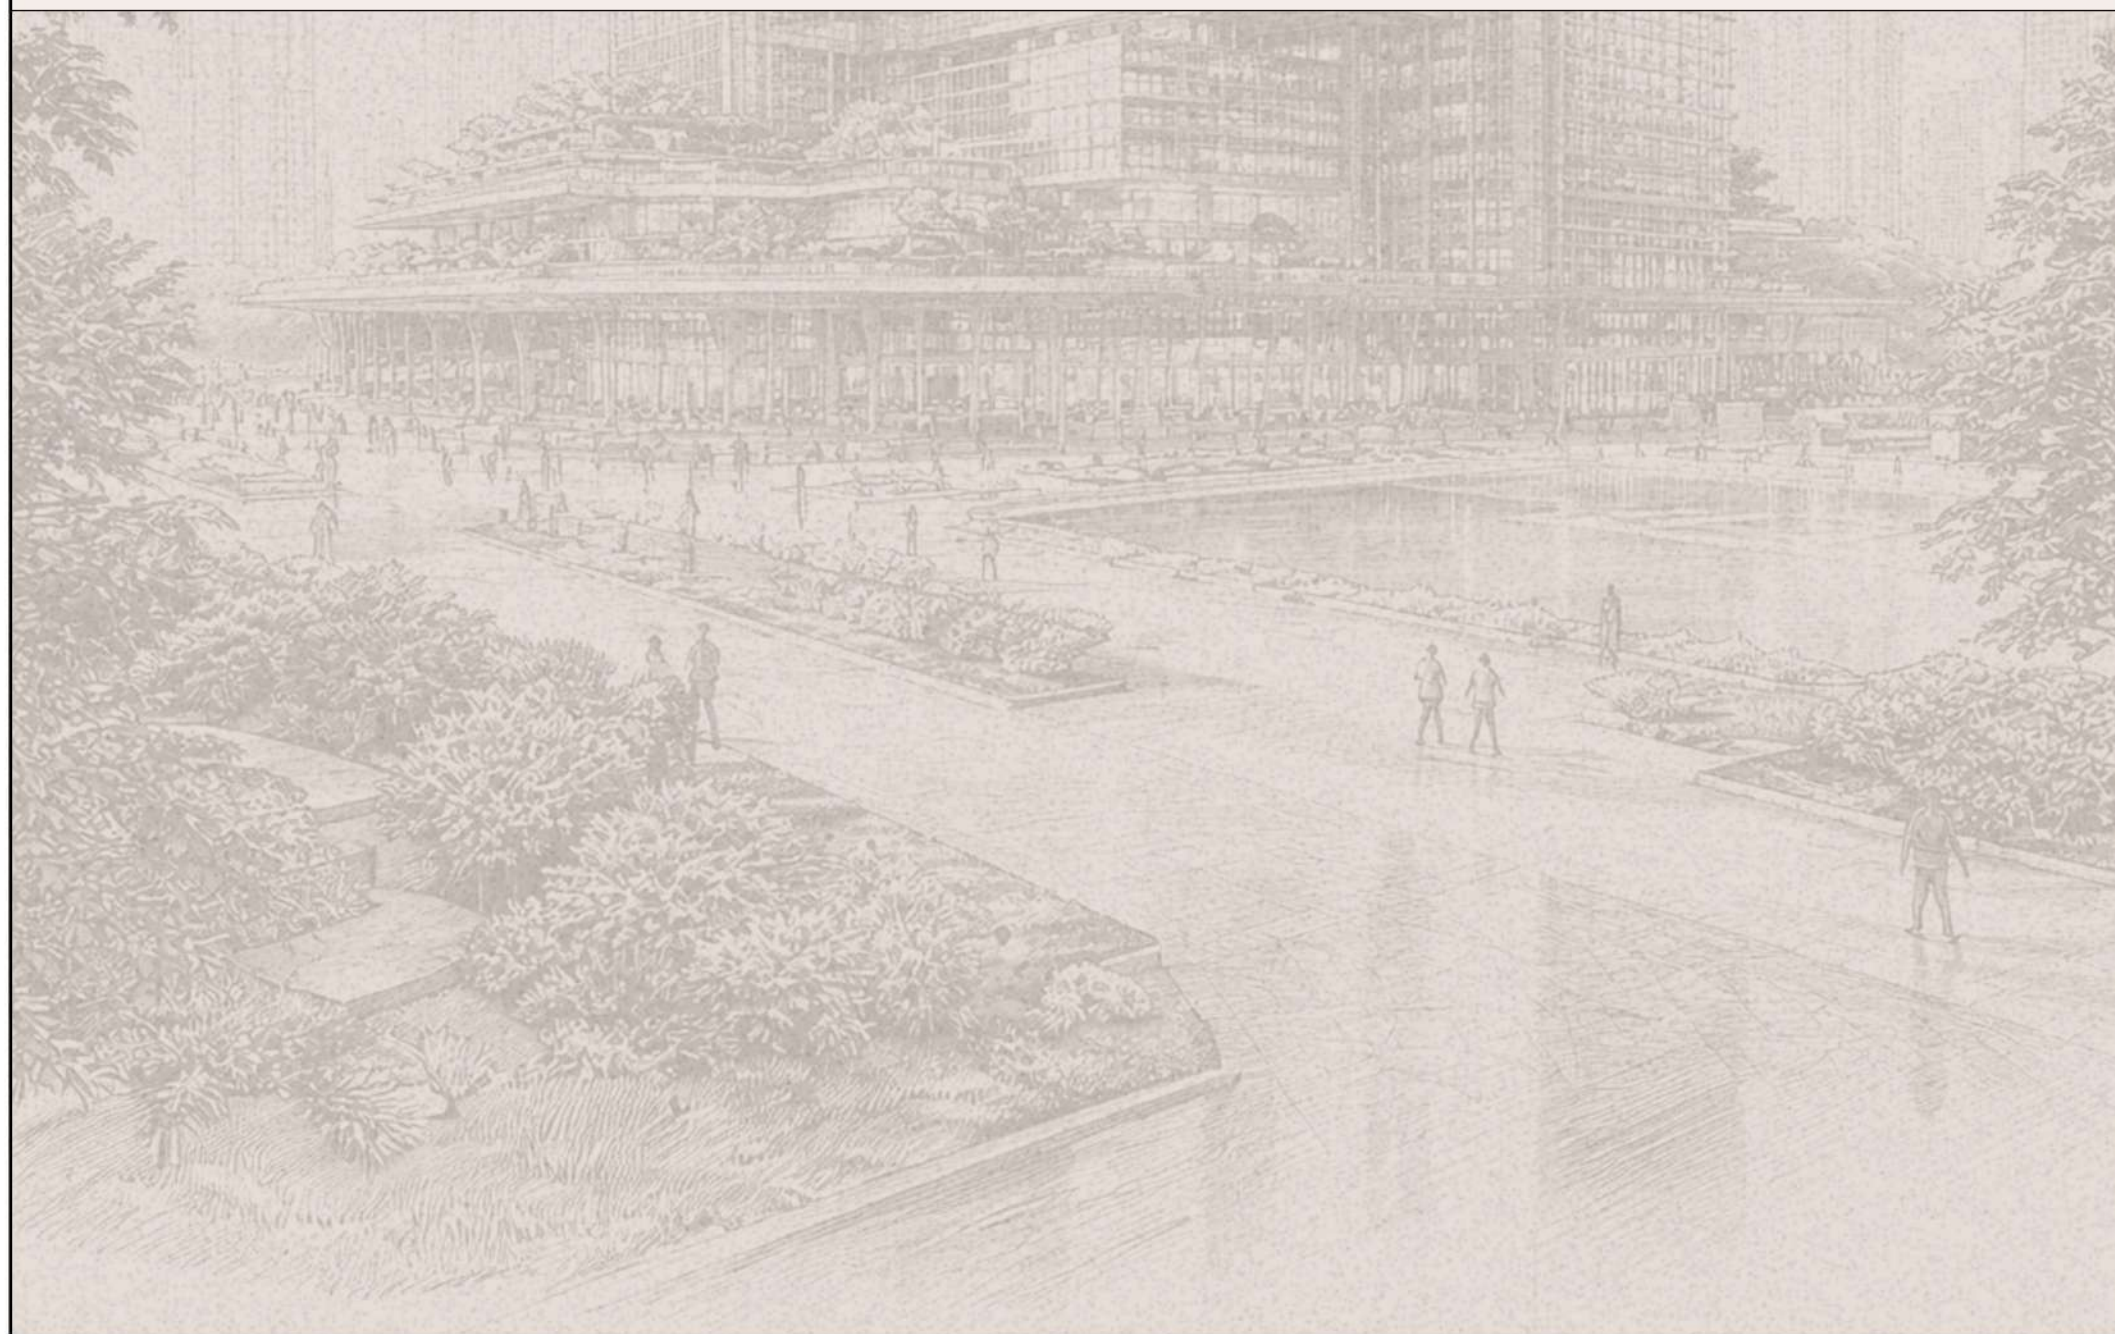

MULTIPURPOSE SPORTS COMPLEX



AIM

To design a Multipurpose sports and recreation facility supporting international facilities and Olympic standards serving as space for sports person and public to develop their talent and pursue their dream in Bangalore.

SCOPE

- Popularizing sports amongst the youth as way of life.
- Matters relating to participation and performance of sports persons and teams in international sporting events.
- Early identification of sports talent and nurturing of the identified talent.
- Welfare measures for sports persons
- Integration of sports in educational curriculum in schools, colleges and universities.
- Increasing outreach of sports to all areas

OBJECTIVES

- To establish a world class sports complex in Bangalore.
- Provide modern sporting facilities and technologies for sports persons.
- To understand the specific technical requirements of the relevant national and international sport organizations for the sports to be accommodated.
- To design an indoor sports stadium and aquatic complex with international standards.
- To give them a public space to train & to achieve goals.
- To give them a platform to gain confidence and overcome their physical limitations.
- Need to give them sports medical Centre which caters to 24x7 open treatment area, physician exam rooms, and pharmacy and also keep a periodic track of their fitness.

NEWS


Only 5.56% of Indian population is sports literate

Research suggests that only 57 lakh people are associated with sports out of 125 crore people of India.

BBC report says under 30% of women in India engage in sports

NEED

- Karnataka have played a significant role in the sports scenario of the country. There is a lack of basic sports infra structure facilities for the sports persons, the sports organizations, youngsters of Bangalore. The scope of the work includes. the design of an indoor stadium and aquatic complex.
- The detailed design of sports complex and supporting facilities such as administrative. accommodation, parking, gymnasium, health club and cafeteria.
- A sports complex may include a wide variety of indoor and outdoor sports facilities such as football and cricket stadiums, swimming, basketball, table tennis etc. Considering the available site area and requirements, only indoor facilities like basketball volley ball, tennis etc. are included.
- Recreation facilities such as player's facilities and club house and spa are also the other requirement.

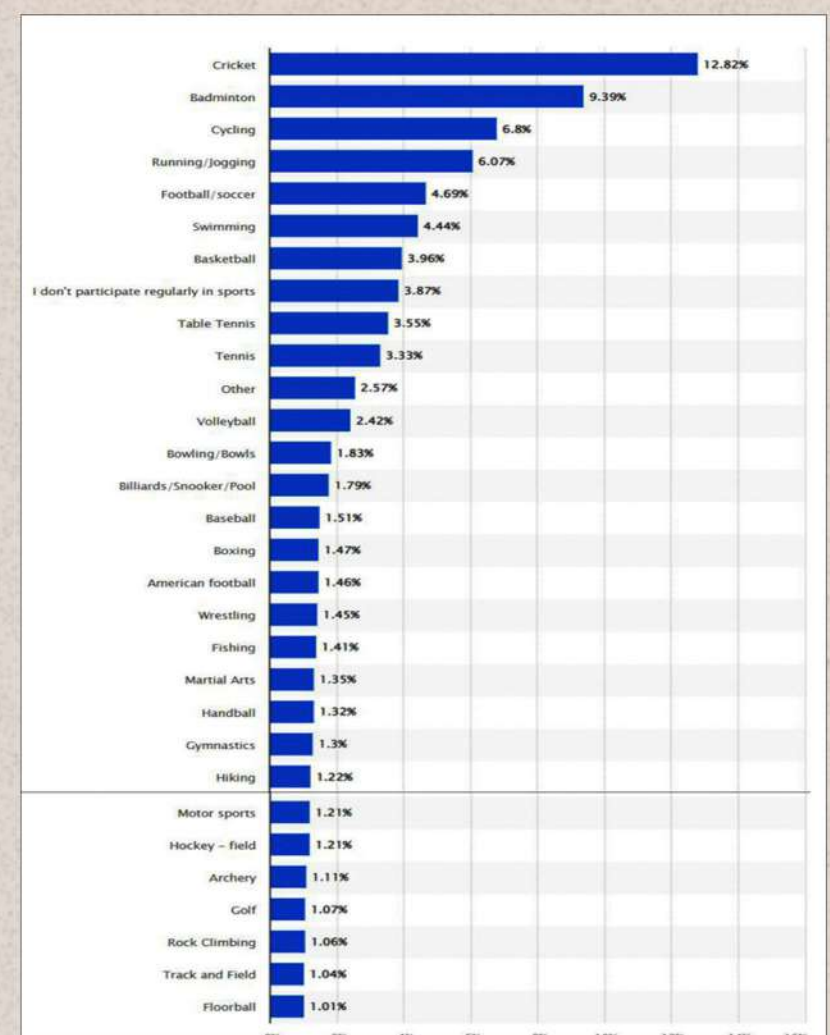

Graph of the no. of people getting into sports in 2020 according to the survey CHAPTER 2

SITE STUDY AND ANALYSIS

LOCATION

Bengaluru is the Capital of the Indian State of Karnataka. It has a population of over ten million, making it a megacity and the Third populous City and 5th most populous urban agglomeration in India. It is in Southern India on the Deccan Plate.




SITE IDENTIFICATION



The site is located within a dense urban fabric characterized by a mix of residential, institutional, and commercial developments.

The plot is irregular and currently appears underutilized, presenting strong for redevelopment. Surrounding land uses include built-up structures with varying heights, open pockets, and water bodies, which contribute to both opportunities and constraints in design.

PROXIMITY

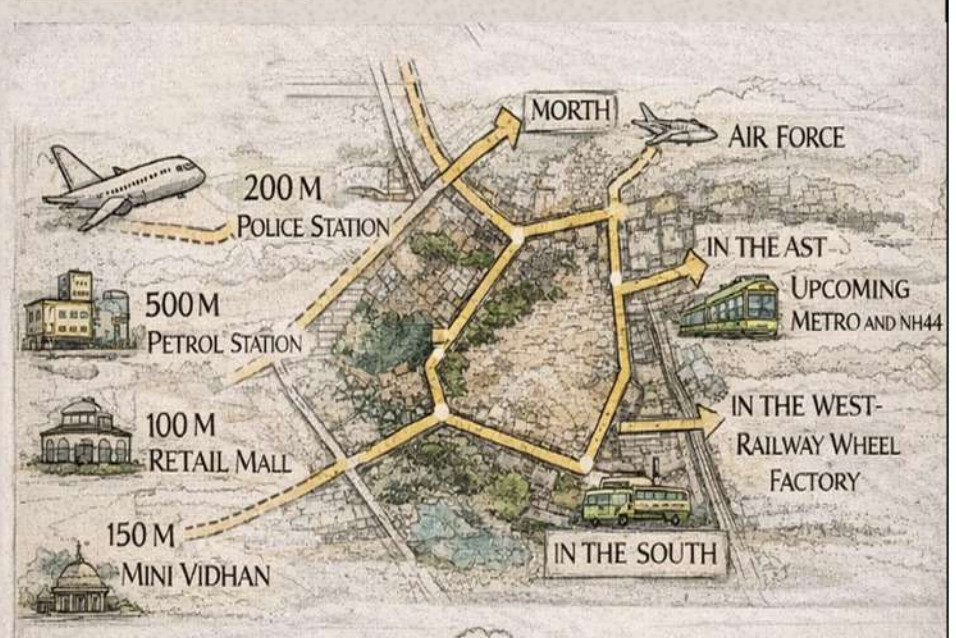

SITE JUSTIFICATION


- Yelahanka is slowly progressed and developed in every single.
- Easy accessibility for the public.
- Existing space that are dedicated for the recreation and sports facilities.
- Large space available in prime area
- Lots green space available.
- Proximity to airport 15 km away from Kempe Gowda airport. Takes 20 mins by car.
- Proximity to high voltage transmission lines
- There were no high voltage transmission lines running throughout the site.
- Avoiding the presence of toxic and hazardous substances
- There were no chemical producing factories around the site .
- Area with less traffic
- The site had less intensity of vehicles moving around the site.
- Proximity to major highway
- Connects to the Airport -doddballapur and chickbalapur link high way in 600m
- Less noise caused in the surrounding
- Very minimal sound was created by the vehicles which pass by every 10 -15 mins.

STRENGTH

- Water bodies inside site
- Easy accessibility
- Prime location
- Existing land use for sports ground

WEAKNESS

- Prime location
- Barren land
- Flood prone areas in southern side of site

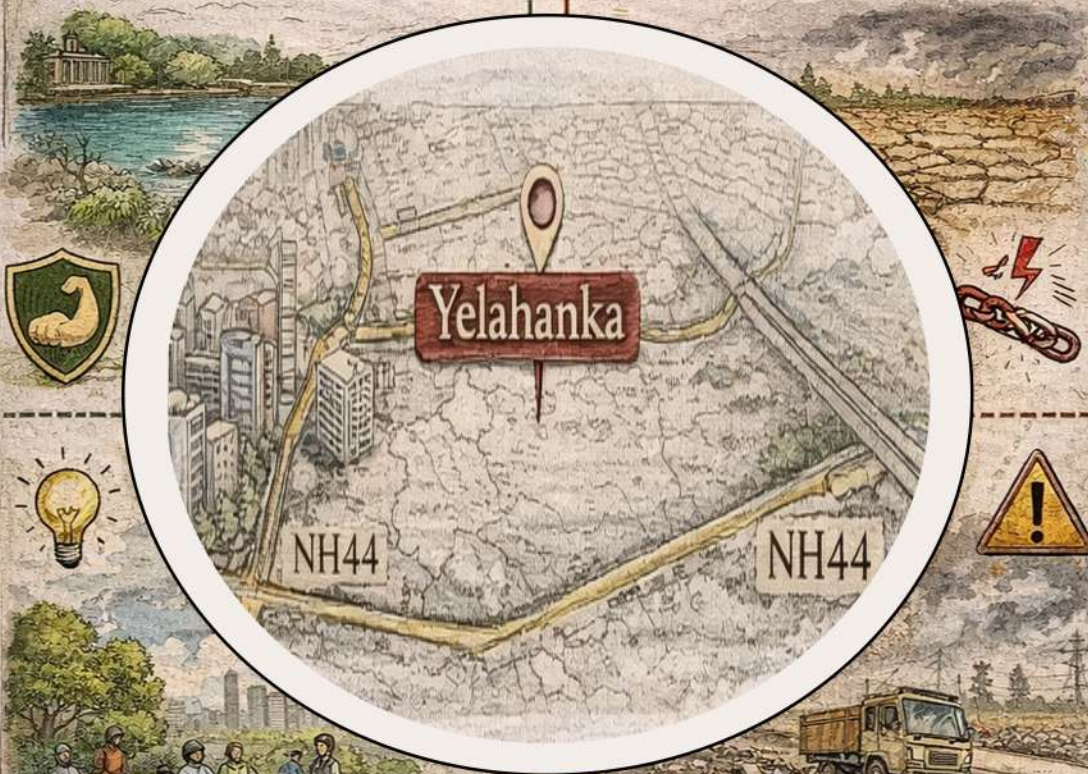

OPPORTUNITY

- Has the opportunity to become a gathering hub for persons with disabilities across nation and world
- Can enhance the growth of the area

THREAT


- Large site in prime area
- Barren lands could be used as dump yards
- Existing roads adds on to the noise

CONCEPT DEVELOPMENT

Spine plays very important role in a human being, spine can be effective in any normal or specially abled people, so considering this factor taking spine as my concept in my planning.

Taking inspiration from spine to connect all the sporting facilities. The spine gives the posture to the body and defines the structure of the body and it connects all the vertebrates and makes it one single structure showing everything together makes one single unit.

Spine helps in connecting all the parts of the sports complex showing the critical path that has to be taken during the journey inside the sports complex.





Different entry points to maximize the view towards the site and use the site surroundings to the advantage.

Closer to the road are the most public and service areas so the circulation is minimum.

Separating building blocks with open space road around the major zone which is the stadium. The curve pathways and the building should complement each other and maintaining the focus to the building. The building orientation and design should be merged with site and the layout.


The green patches are designed with organic patterns which are put together around building to make a random.

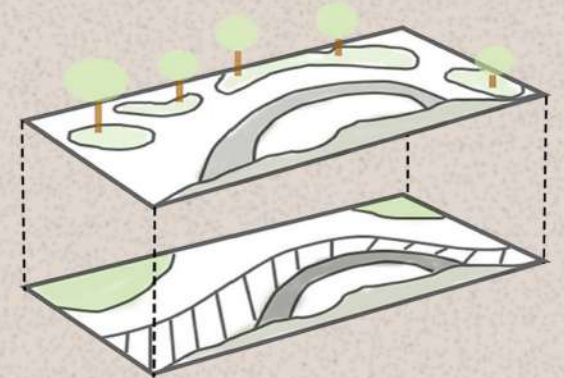


Proximity between Training Centre and Indoor stadium There are two parts in the Main building, Indoor stadium and the Training center which has separate entrances and are to be provided in close proximity because of the combined services and other facilities they share.




Combining the two function into a single block and creating a lobby space in between them. The access road should be around the building accommodating the large crowd exiting from the stadium. The major services can be placed in the training portion to make a variable massing.



A variable massing is used to differentiate the two sides of the building although formed they are formed into one block. Carving out the surfaces to make it organic and merge with surrounding rather than projecting a whole-together different profile.




Creating a combination of different spaces into a whole structure which merges into the landscape and at the same time stand out.

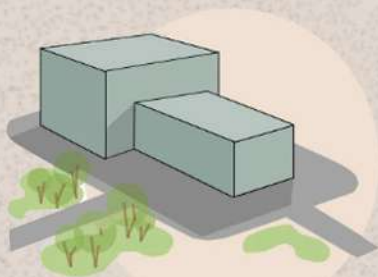


Hierarchy

The Two structures are combined but with different scales so as to differentiate the uses as well as to built up the view from the entry point and the footprint.

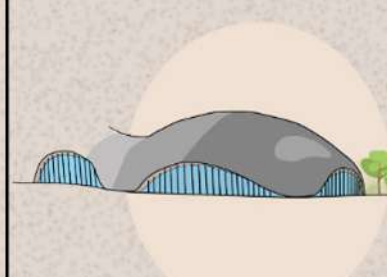


Organic Structure

The outer shell of the overall structure should complement the planar form. The basic idea is an organic form which flows through the space.

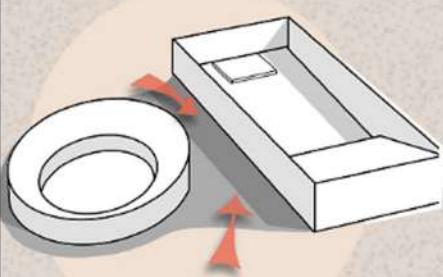

Common Lobby space

The entry point is to be placed between the stadium and the auditorium so the common space can be used as lobby space. The large crowd can eased through the use of this space and the corridor also should be provided around the stadium.

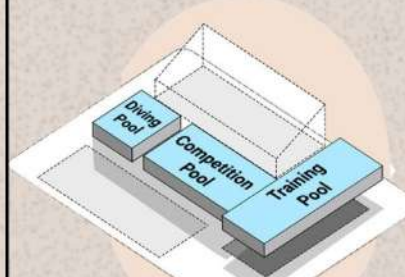

Swimming Complex

The complex has three different pools out of which, training pool is stacked above on top and the ground is used as the entrance lobby and such. The spectators seating areas are placed on both sides of the competition pools.

TECHINICAL DRAWINGS




PROJECT SUMMARY


- Indoor Stadium and Training center - 24478 sqm
- Swimming Complex - 10883 sqm
- Administration Block - 1600sqm
- Site Area- 28 acres

INDOOR STADIUM


Ground Floor Plan

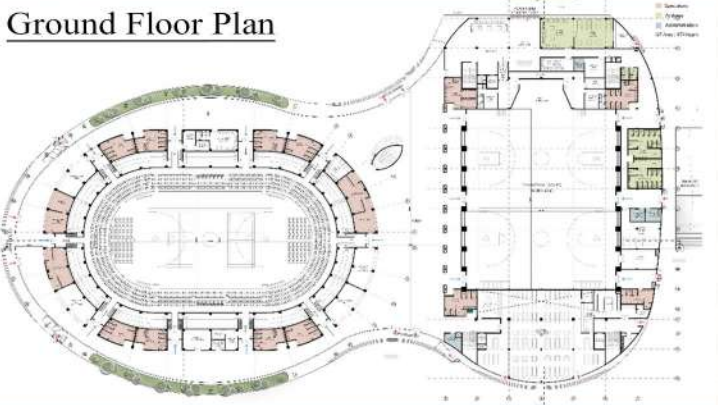


Column Layout

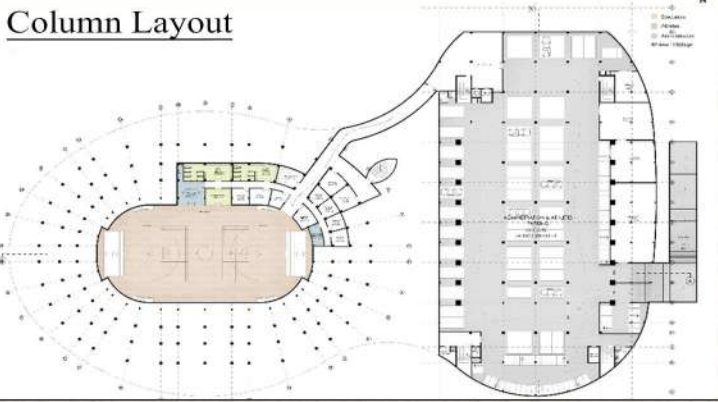



First Floor Plan

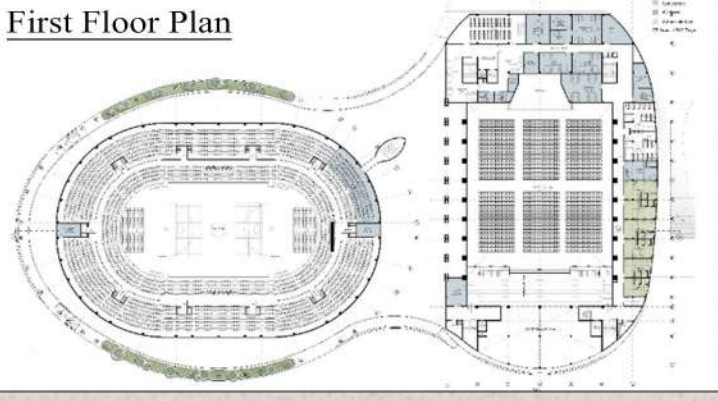

Second Floor Plan

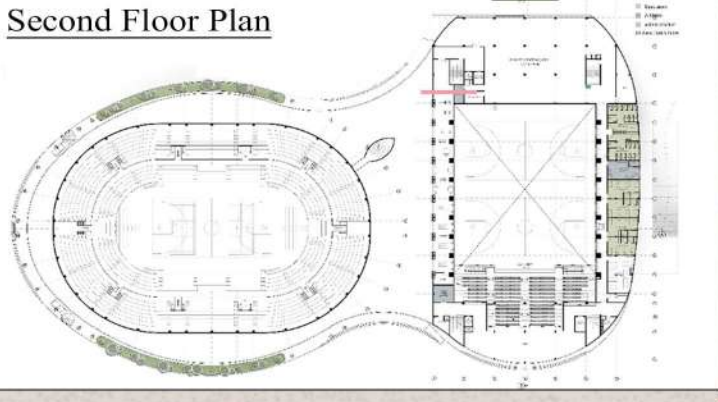

Third and Fourth Floor Plan

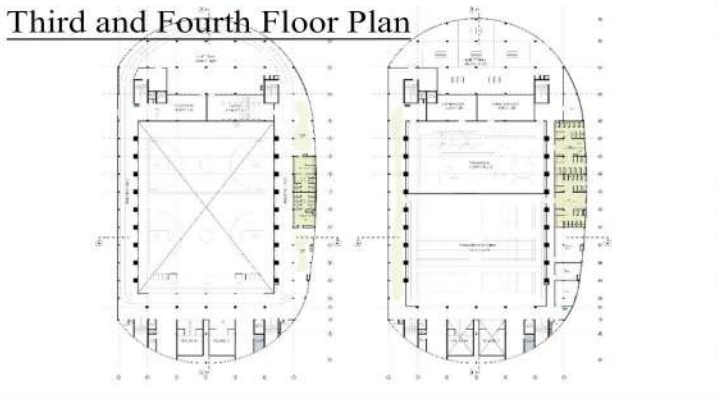


SITE PLAN




SWIMMING COMPLEX


Ground Floor Plan

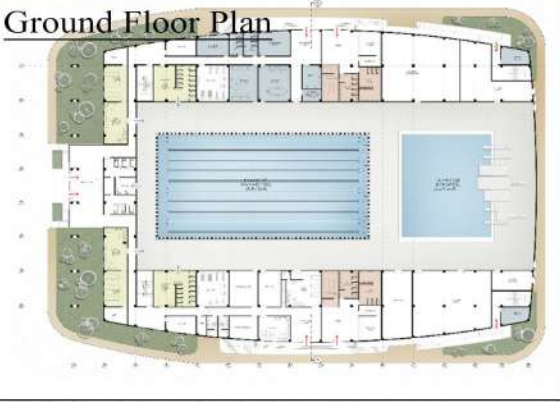



First Floor Plan

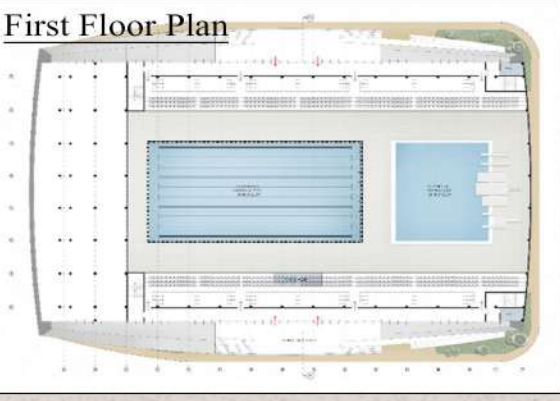

Second Floor Plan

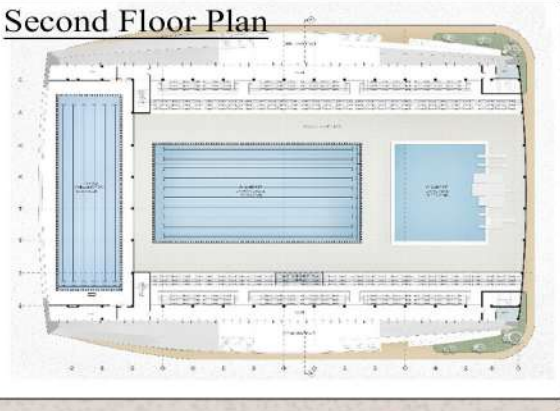


ADMINISTRATION AND CLUB HOUSE

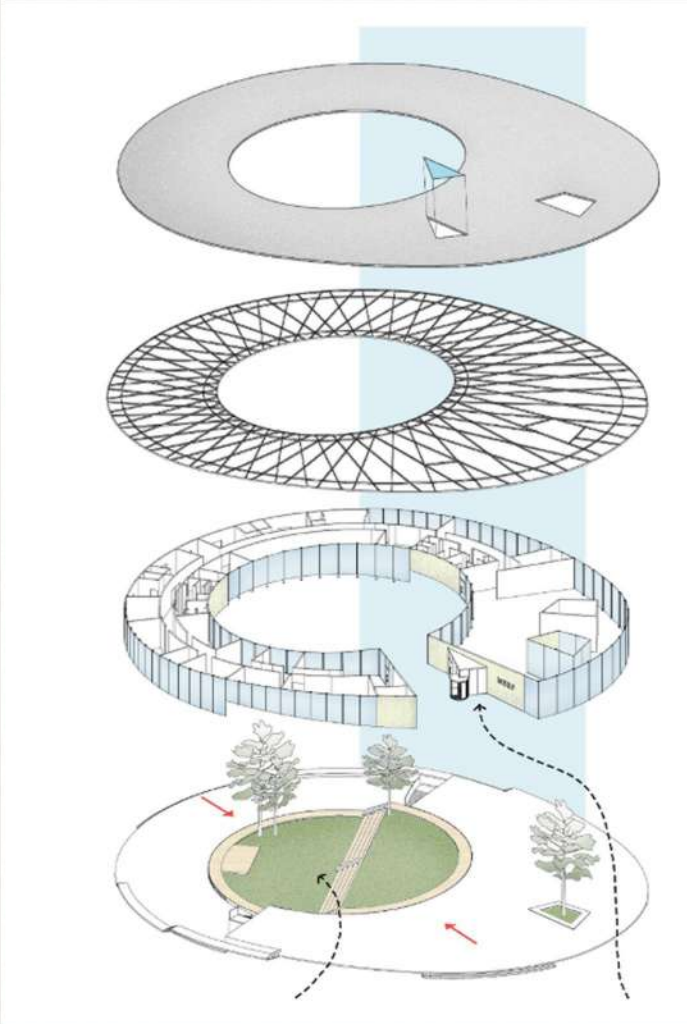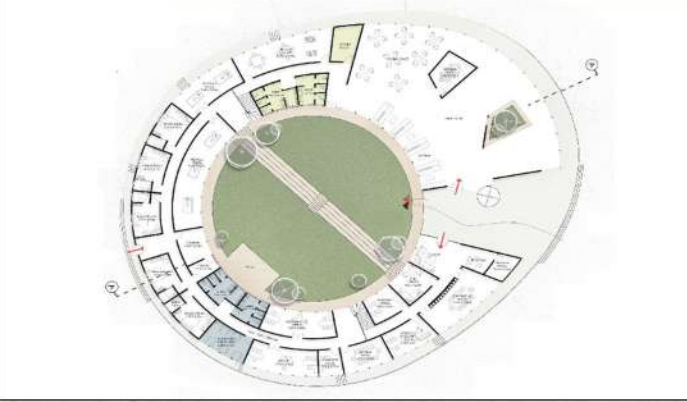



ARCHITECTURAL DESIGN



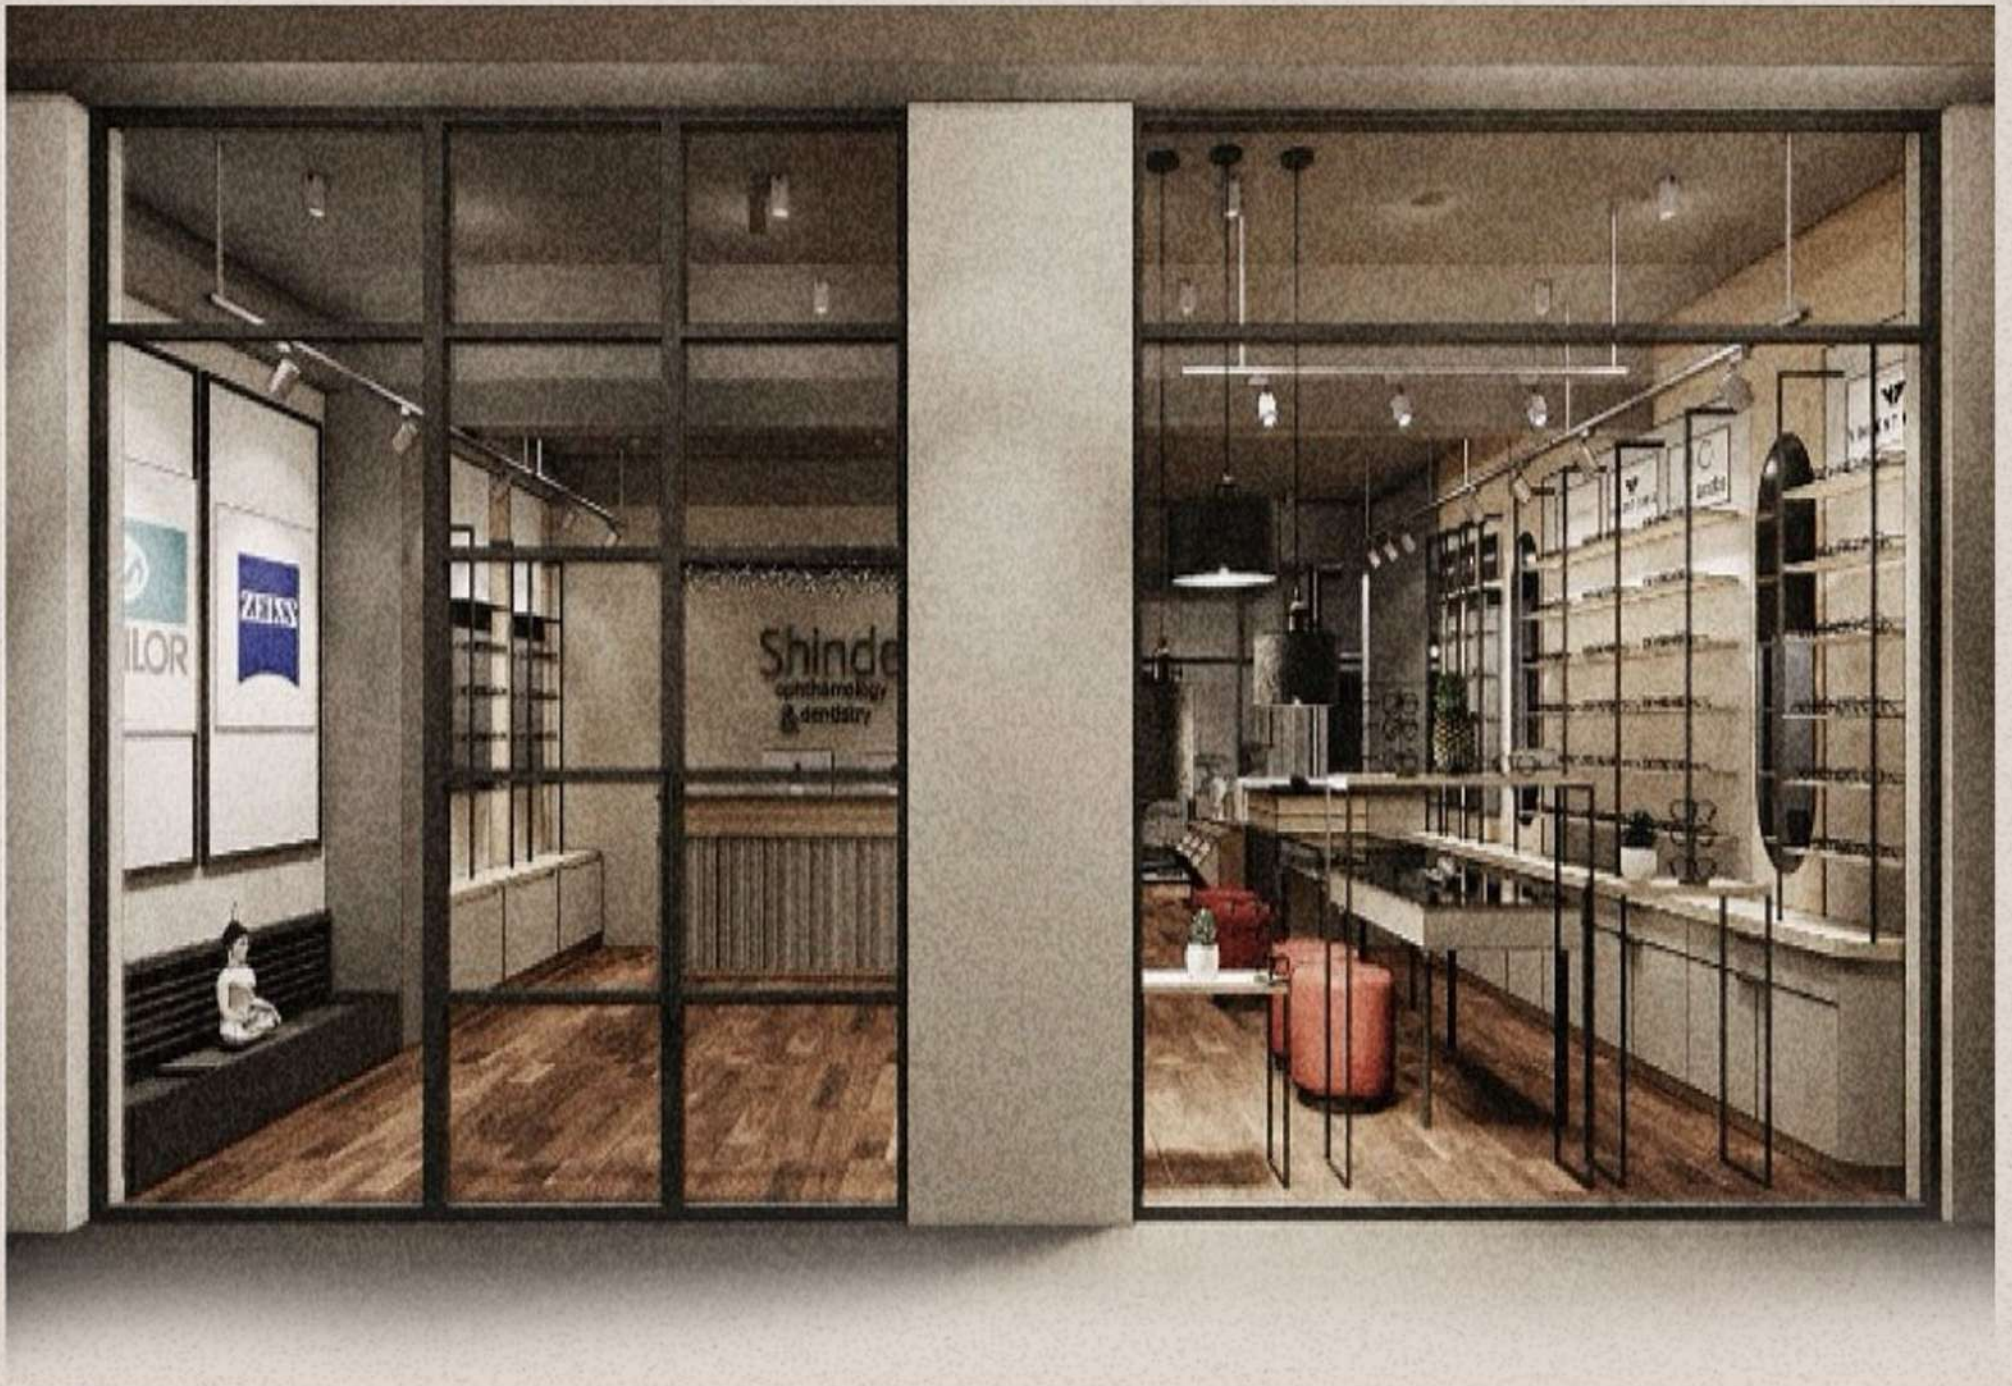


SHINDE DENTAL & EYE CARE

LOCATION: YELEHANKA- 560064
COMMERCIAL INTERIORS

A 4,000 sq.ft. eye and dental healthcare center executed under a design-bid-build delivery method, designed to balance clinical functionality with a refined, patient-centric experience. The layout integrates a retail eyewear zone to enhance accessibility and engagement, while maintaining the cleanliness and clarity essential to a healthcare environment. A dedicated children's play area was incorporated to improve patient comfort and overall experience..

CONCEPT & PLANNING

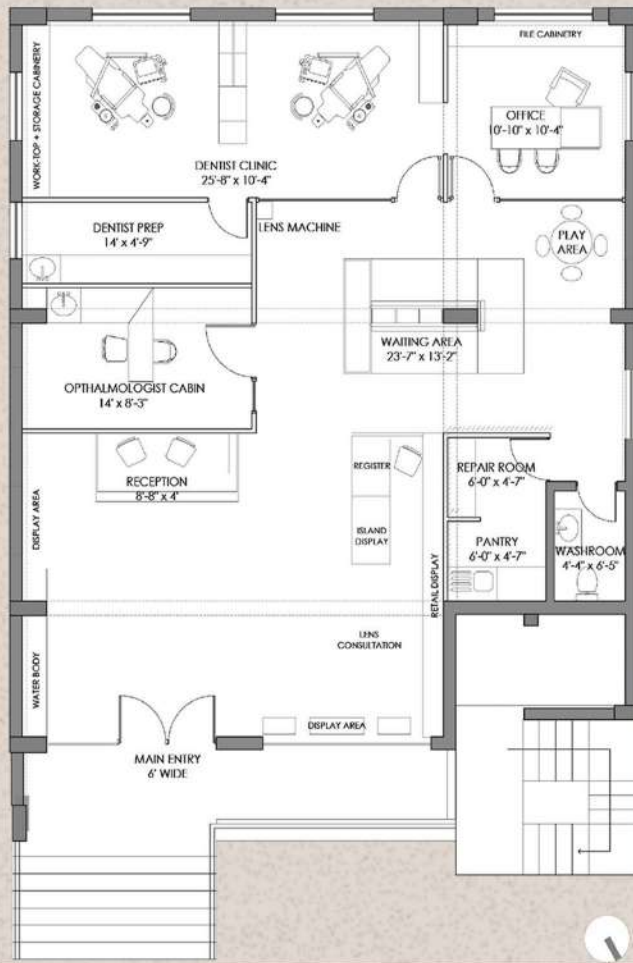

MY ROLE

- Led the end-to-end design development from concept through preconstruction
- coordination, working closely with the principal architect, clients, and consultants.
- Developed design concepts and presentation sets
- Coordinated multiple design iterations with stakeholders
- Supported permit approvals and ensured ISO healthcare compliance
- Acted as a bridge between design intent and technical execution

DESIGN STRATEGY

Function + Experience

- Clean, organized layouts to reinforce a clinical environment
- Subtle material palette to introduce warmth without compromising sterility

Integrated Retail

- Eyewear display positioned to attract patients
- Seamless transition between clinic and retail zone

Patient-Centric Planning

- Separate children's play area
- Clear circulation to minimize congestion and improve flow

Technical Coordination

- Developed zoning layouts for medical equipment

- Coordinated architectural, MEP, and HVAC systems within tight constraints
- Ensured compliance with healthcare design standards

Preconstruction & Project Controls

- Prepared BOQs, bid packages, and cost analyses
- Managed 15+ vendors and suppliers
- Tracked RFIs and submittals, improving coordination and reducing design conflicts
- Maintained QA/QC standards through documentation and review

Impact

- Delivered a functional, compliant, and patient-focused healthcare environment
- Improved coordination efficiency across disciplines
- Balanced design quality with cost and constructability







WINDMERE VALLEY RESORT

LOCATION: YERCUD, TAMIL NADU

PROJECT TYPE: BOUTIQUE HOSPITALITY RESORT

DELIVERY METHOD: DESIGN-BID-BUILD

SITE AREA: ~2 ACRES

The project is a 2-acre boutique resort located in the scenic hill station of Yercaud in the Salem district, positioned along the edge of a cliff at a higher elevation. The site offers uninterrupted panoramic views of the valley, with a strong visual connection to the surrounding landscape and a distinct advantage of sunset-facing orientations.

ARCHITECTURAL PLAN








TYPE- A



TYPE- B




TYPE- C

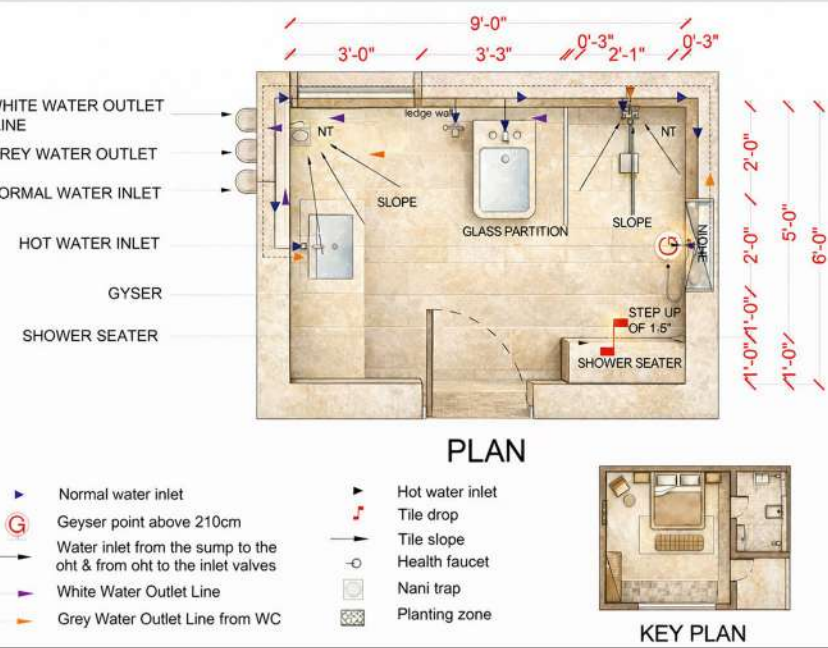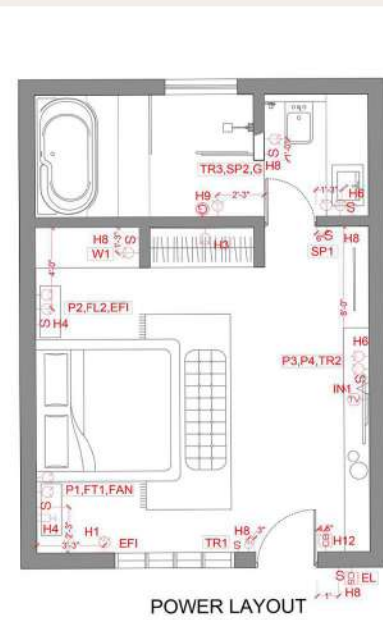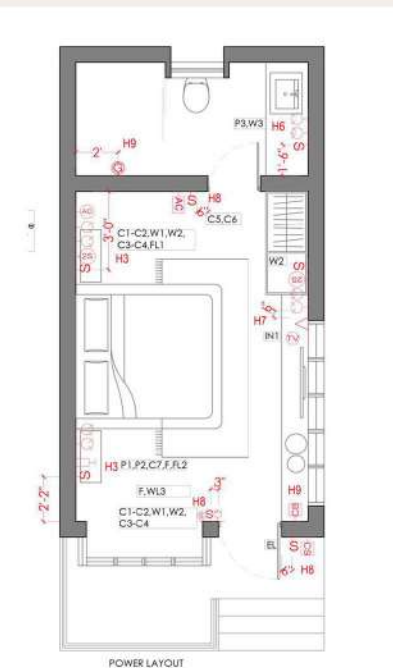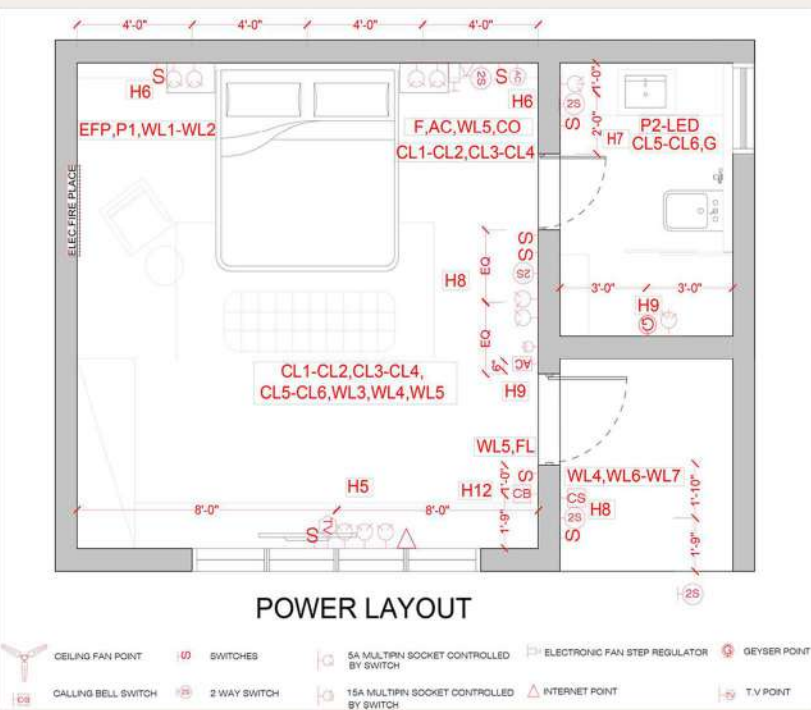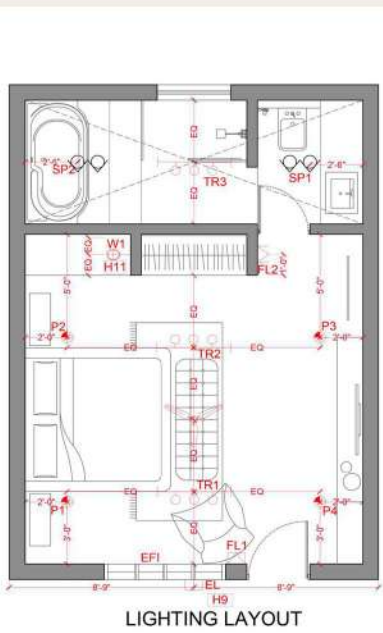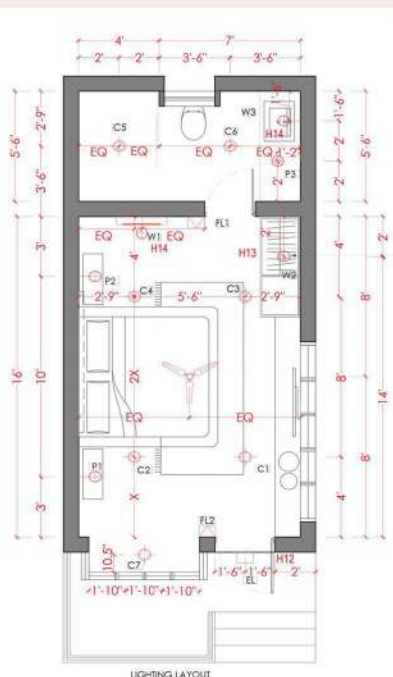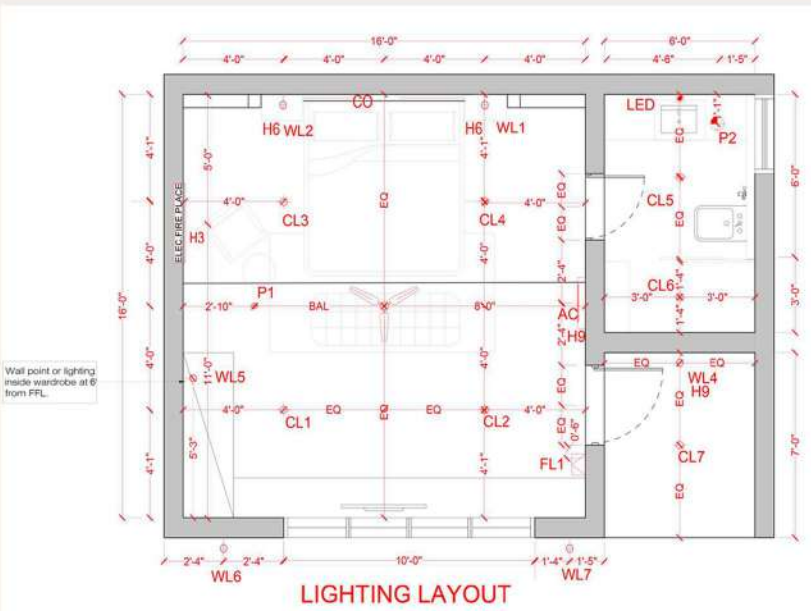

VIEWS



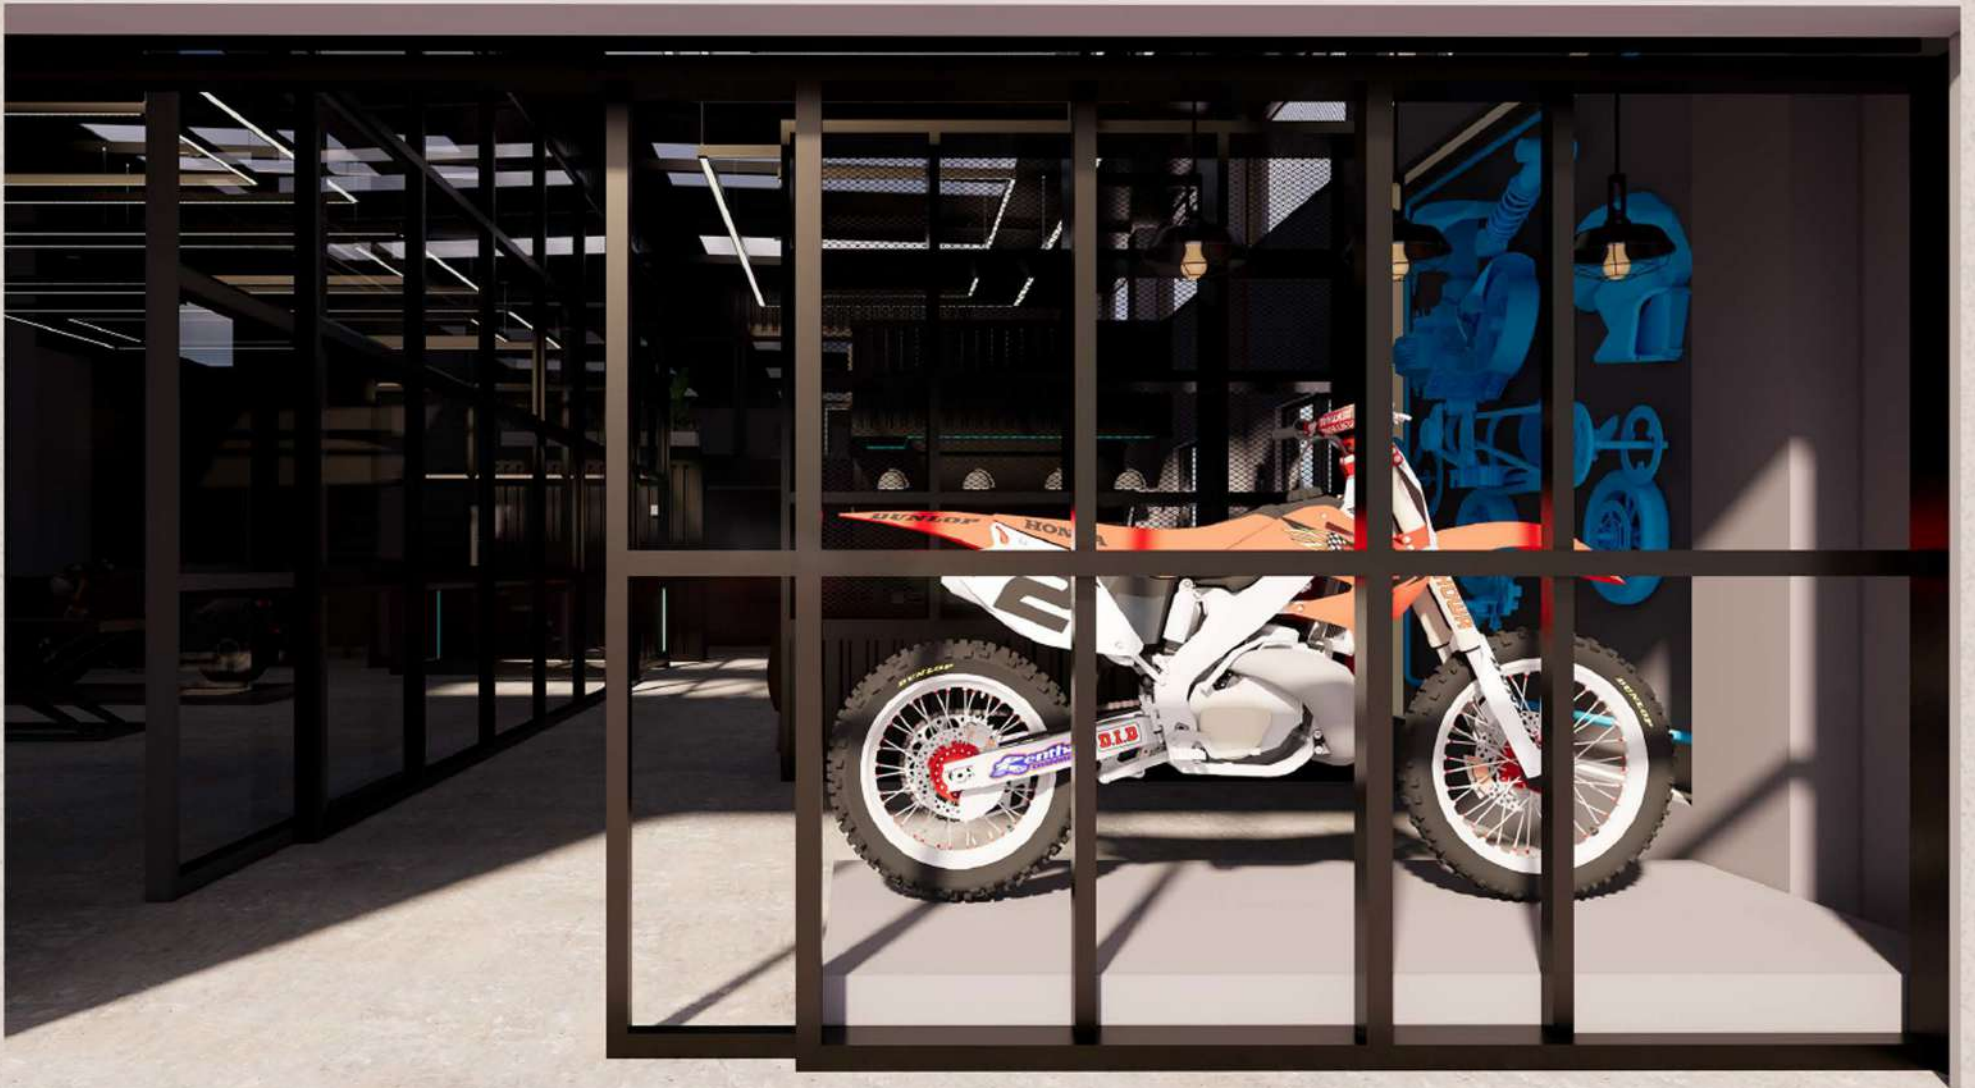

Motorcycle Service Facility

Commercial + Service + Retail Integration | AARDE Construction & Design

AREA- 24,300 SQ.FT.

BUDGET- \$2.6M

A large-scale 24,300 sq.ft. motorcycle service facility delivered through a design-build approach, transforming a bare shell into a fully integrated space combining workshop operations, retail/café experience, and office functions. The project focused on optimizing spatial planning, system integration, and operational efficiency within a commercial service environment.

MOTORCYCLE SERVICE FACILITY

ROLES & RESPONSIBILITY

Led preconstruction, coordination, and execution across design-build delivery:

- Collaborated with architectural, structural, and MEP teams to transform a shell structure into a fully functional facility
- Directed procurement and construction execution, ensuring alignment between design intent, equipment requirements, and site conditions
- Managed contractors, vendors, and suppliers throughout execution

Technical Scope

- Coordinated OEM equipment integration within building systems (MEP + layout constraints)
- Optimized space planning for workshop efficiency, customer flow, and operational functionality
- Produced shop drawings and technical layouts to guide execution
- Resolved on-site coordination issues through real-time adjustments and stakeholder alignment

Preconstruction & Strategy

- Led business development and client acquisition efforts
- Prepared RFPs, budgeting, and feasibility analysis to align scope, cost, and timeline
- Established procurement strategy for equipment and materials

Execution & Delivery

- Directed construction sequencing and vendor coordination
- Ensured smooth integration of workshop, café, and office zones
- Delivered project within budget and 10 days ahead of schedule

Impact

- Successfully transformed a bare shell into a high-performance service facility
- Improved coordination across disciplines and stakeholders
- Demonstrated strong control over cost, schedule, and execution

